

# WILLIAMSON COUNTY, TEXAS

CHANGE ORDER NUMBER: 5

1. CONTRACTOR: DeNucci Constructors
2. Change Order Work Limits: Sta. Varies to Sta. Varies
3. Type of Change(on federal-aid non-exempt projects): Minor (Major/Minor)
4. Reasons: 2E (3 Max. - In order of importance - Primary first)


Project:	<u>Great Oaks Dr. Improvements</u>
Roadway:	<u>Great Oaks Dr. @ Brushy Creek</u>
CSJ Number:	<u>T4327</u>

5. Describe the work being revised:

**2. Differing Site Conditions. 2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9).** This Change Order adds an item to pay for additional signs needed at the Oak Ridge Drive and Great Oaks Drive intersection during Phase 3 construction. This Change Order also adds an item to pay for water valves to be adjusted on the southwest corner of the existing Great Oaks Drive and Brushy Creek Road intersection.

6. Work to be performed in accordance with Items: See Attached
7. New or revised plan sheet(s) are attached and numbered: N/A
8. New Special Provisions/Specifications to the contract are attached: ☐ Yes ☒ No
9. New Special Provisions to Item N/A No. N/A, Special Specification Item N/A are attached.

Each signatory hereby warrants that each has the authority to execute this Change Order (CO).

<p><i>The contractor must sign the Change Order and, by doing so, agrees to waive any and all claims for additional compensation due to any and all other expenses; additional changes for time, overhead and profit; or loss of compensation as a result of this change.</i></p> <p>THE CONTRACTOR Date <u>3/7/23</u></p> <p>By <u></u></p> <p>Typed/Printed Name <u>Aaron DeNucci</u></p> <p>Typed/Printed Title <u>PM</u></p>	<p><b>The following information must be provided</b></p> <p>Time Ext. #: <u>N/A</u> Days added on this CO: <u>0</u></p> <p>Amount added by this change order: <u>\$2,831.80</u></p>
--	---

## RECOMMENDED FOR EXECUTION:

 3/8/2023  
Project Manager Date

N/A  
Design Engineer Date

 3/8/2023  
Program Manager Date


Design Engineer's Seal:

County Commissioner Precinct 1 Date  
☐ APPROVED ☐ REQUEST APPROVAL

County Commissioner Precinct 2 Date  
☐ APPROVED ☐ REQUEST APPROVAL

County Commissioner Precinct 3 Date  
☐ APPROVED ☐ REQUEST APPROVAL

County Commissioner Precinct 4 Date  
☐ APPROVED ☐ REQUEST APPROVAL

 Mar 22, 2023  
County Judge Date  
☐ APPROVED

# WILLIAMSON COUNTY, TEXAS

**CHANGE ORDER NUMBER:** 5

**Project #** *Great Oaks Dr. Improvements*

**TABLE A: Force Account Work and Materials Placed into Stock**[illegible]**TABLE B: Contract Items:**

				ORIGINAL + PREVIOUSLY REVISED		ADD or (DEDUCT)	NEW		
ITEM	DESCRIPTION	UNIT	UNIT PRICE	QUANTITY	ITEM COST	QUANTITY	QUANTITY	ITEM COST	OVERRUN/ UNDERRUN
502-WC01	TEMP TRAFFIC CONTROL SIGNS	EA	\$404.00	0.00	\$0.00	3.00	3.00	\$1,212.00	\$1,212.00
504S-3W	ADJUSTING WATER VALVE BOXES TO GRADE	EA	\$809.90	0.00	\$0.00	2.00	2.00	\$1,619.80	\$1,619.80
<b>TOTALS</b>					<b>\$0.00</b>			<b>\$2,831.80</b>	<b>\$2,831.80</b>

## CHANGE ORDER REASON(S) CODE CHART

1. Design Error or Omission	1A. Incorrect PS&E 1B. Other
2. Differing Site Conditions (unforeseeable)	2A. Dispute resolution (expense caused by conditions and/or resulting delay) 2B. Unavailable material 2C. New development (conditions changing after PS&E completed) 2D. Environmental remediation 2E. Miscellaneous difference in site conditions (unforeseeable)(Item 9) 2F. Site conditions altered by an act of nature 2G. Unadjusted utility (unforeseeable) 2H. Unacquired Right-of-Way (unforeseeable) 2I. Additional safety needs (unforeseeable) 2J. Other
3. County Convenience	3A. Dispute resolution (not resulting from error in plans or differing site conditions) 3B. Public relations improvement 3C. Implementation of a Value Engineering finding 3D. Achievement of an early project completion 3E. Reduction of future maintenance 3F. Additional work desired by the County 3G. Compliance requirements of new laws and/or policies 3H. Cost savings opportunity discovered during construction 3I. Implementation of improved technology or better process 3J. Price adjustment on finished work (price reduced in exchange for acceptance) 3K. Addition of stock account or material supplied by state provision 3L. Revising safety work/measures desired by the County 3M. Other
4. Third Party Accommodation	4A. Failure of a third party to meet commitment 4B. Third party requested work 4C. Compliance requirements of new laws and/or policies (impacting third party) 4D. Other
5. Contractor Convenience	5A. Contractor exercises option to change the traffic control plan 5B. Contractor requested change in the sequence and/or method of work 5C. Payment for Partnering workshop 5D. Additional safety work/measures desired by the contractor 5E. Other
6. Untimely ROW/Utilities	6A. Right-of-Way not clear (third party responsibility for ROW) 6B. Right-of-Way not clear (County responsibility for ROW) 6C. Utilities not clear 6D. Other

## **Williamson County Road Bond Program**

### **Great Oaks Drive Improvements Williamson County Project No. T4327**

#### **Change Order No. 5**

#### **Reason for Change**

This Change Order adds a new pay item for additional signs needed at the Oak Ridge Drive and Great Oaks intersection during Phase 3 construction. This Change Order also adds a new pay item to adjust existing water valves at the southwest corner of Great Oaks Drive and Brushy Creek Road that were not included in the plans.

The following new items will be added by this Change Order.

ITEM	DESCRIPTION	QUANTITY	UNIT
502-WC01	TEMP TRAFFIC CONTROL SIGNS	3	EA
504S-3W	ADJUSTING WATER VALVE BOXES TO GRADE	2	EA

This Change Order results in a net increase of \$2,831.80 to the Contract amount, for an adjusted Contract total of \$10,752,935.41. The original Contract amount was \$10,580,634.11. As a result of this and all Change Orders to-date, \$172,301.30 has been added to the Contract, resulting in a 1.63% net increase in the overall Contract cost. No time will be added to the Contract for this Change Order.

#### **HNTB Corporation**

Oscar Salazar-Bueno, P.E.

# CHANGE ORDER PROPOSAL

Contractor: DeNucci Constructors, LLC.

Project Name: T4327 Great Oaks Dr Improvements at Brushy Creek

Change Order Proposal Number: 10.1 Date: 1/10/2023

Description:	<p><b>1.</b> HNTB instructed DeNucci to install (3) additional temporary traffic control signs at the Great Oaks x Oak Ridge intersection for P3 TCP. <b>2.</b> At the SW corner of the work area, DeNucci was instructed to raise two valve cans for the existing BCMUD WL to finished grade (approx. 3' ea.). Unit pricing provided for both items.</p>
--------------	---

[illegible][illegible]

Subcontractors/Vendors:	Description						Total
Subtotal							\$0.00



[illegible]

<b>Equipment:</b>	Description	Quantity	Unit	Operating Cost/Day	FHWA	Total
						\$0.00
						\$0.00
						\$0.00
						\$0.00
						\$0.00
	Subtotal					\$0.00

Labor		\$0.00
Labor Burden	55%	\$0.00
Labor P & O	15%	\$0.00
Material		\$0.00
Material P & O	15%	\$0.00
Subcontractor		\$0.00
Subcontractor P & O	15%	\$0.00
Bid Item		\$2,803.78
Equipment	15%	\$0.00
Bond	1%	\$28.04
<b>TOTAL</b>		<b>\$2,831.82</b>

**Additional days requested:** 1

REPLACE WITH  
STOP SIGN REMOVED &  
NB GREAT OAKS & BRUSHY CREEK

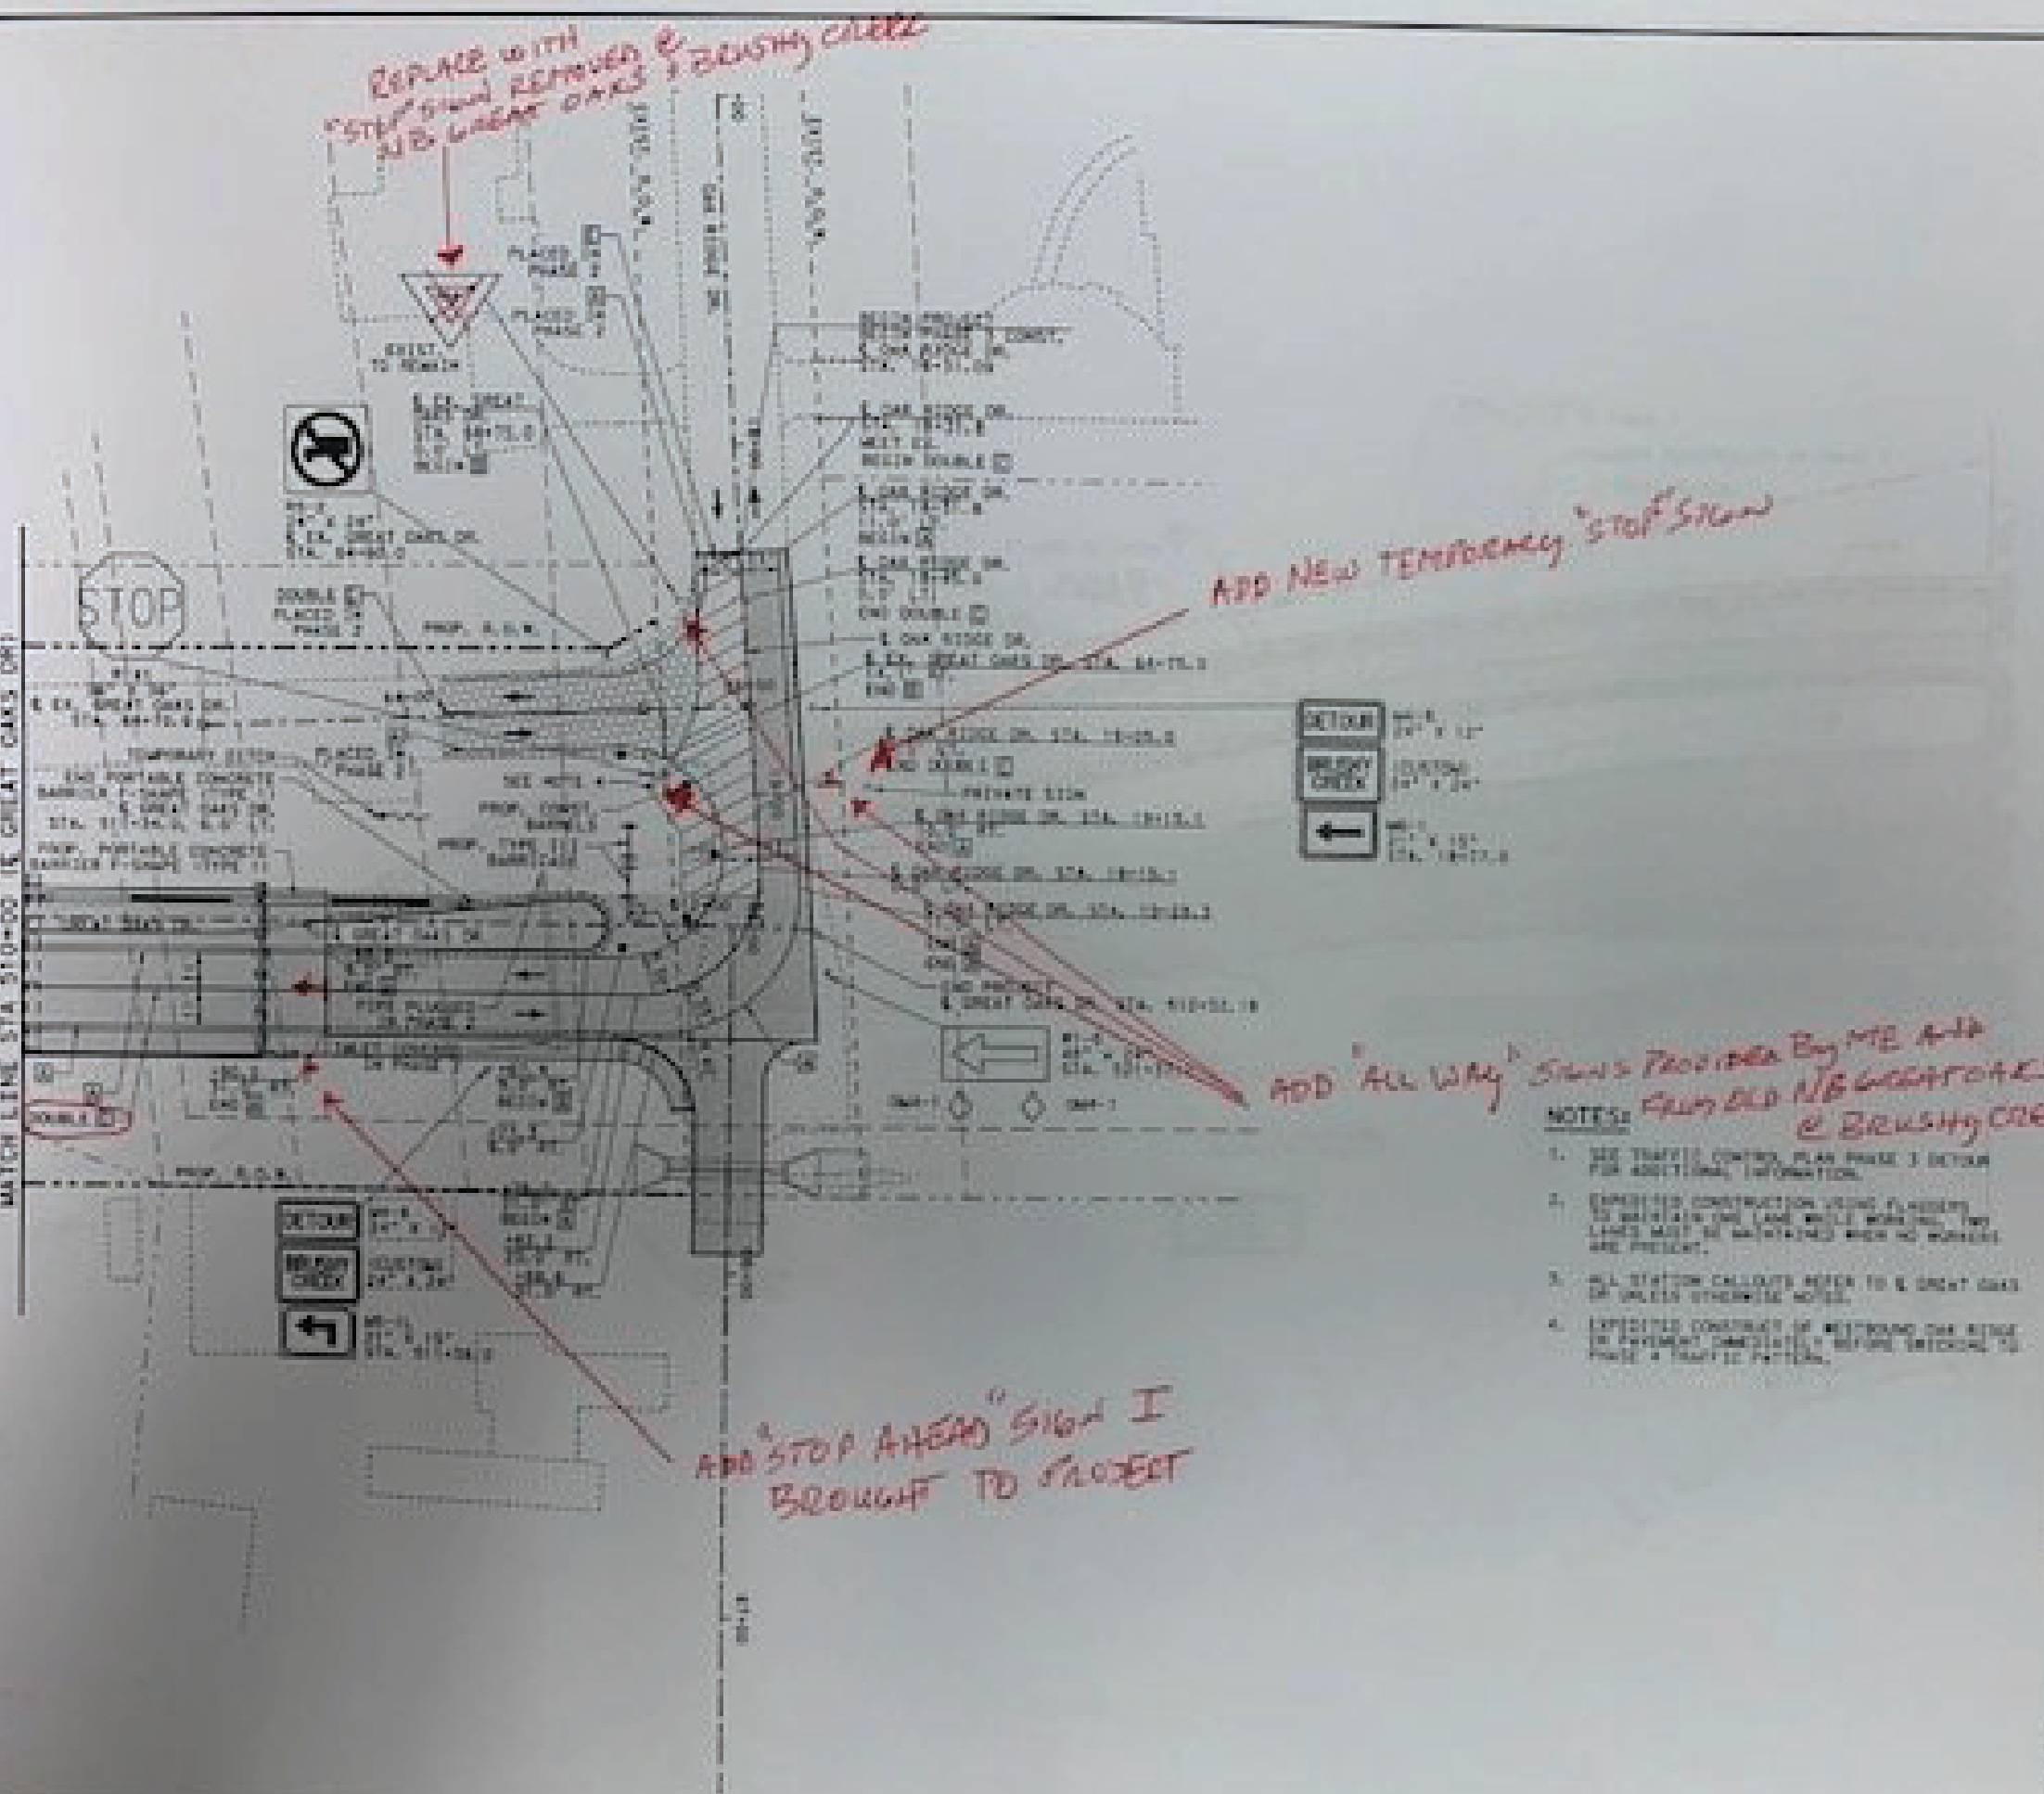


**LEGEND**

EXISTING ROW	---
PROPOSED ROW	---
PROPERTY LINE	---
TEMP SPECIAL SHOWING	---
PORTABLE CONCRETE	---
TRAFFIC BARRIER	---
CONCRETE BARRIERS	---
CONCRETE BARRIERS	---
WORK ZONE	---
EXPEDITED CONEST	---
PERMANENT REMOVAL	---
COMPLETED PAVEMENT	---
DETOUR PAVEMENT	---

1	45	24	PAV	WKS	NON-ROAD	181	4"	15L21
2	45	24	PAV	WKS	NON-ROAD	181	24"	15L21
3	45	24	PAV	WKS	NON-ROAD	171	4"	15L21
4	45	24	PAV	WKS	NON-ROAD	171	4"	15L21
5	45	24	PAV	WKS	NON-ROAD	180	36"	15L21, 15L22




**NOTES**

1. SEE TRAFFIC CONTROL PLAN PHASE 3 DETOUR FOR ADDITIONAL INFORMATION.
2. EXPEDITED CONSTRUCTION USING PAVING TO MAINTAIN ONE LANE WHILE WORKING. TWO LANE MUST BE MAINTAINED WHEN NO WORKERS ARE PRESENT.
3. ALL STATION CALLOUTS REFER TO E GREAT OAKS DR UNLESS OTHERWISE NOTED.
4. EXPEDITED CONSTRUCTION OF RESTORING ONE SIDE OF PAVEMENT COMPLETED BEFORE RETURNING TO PHASE 4 TRAFFIC PATTERN.



12/11/2018



**WILLIAMSON COUNTY**  
TEXAS



**PESC** P.E. Structural Consultants, Inc.  
www.PESCinc.com  
1875 Fm. Hw. P. 1071

GREAT OAKS DR AT BRUSHY CREEK RD

**TRAFFIC CONTROL  
PHASE 3 LAYOUT**

REVISIONS		SHEET 3 OF 3	
NO.	DATE	DESCRIPTION	BY
1	12/11/2018	ISSUED FOR PERMIT	WJW
2	12/11/2018	REVISED	WJW
3	12/11/2018	REVISED	WJW
4	12/11/2018	REVISED	WJW
5	12/11/2018	REVISED	WJW

CONSTRUCTION PROJECT - AVERAGE LOW BID

District: ALL

UPDATED :: 08/10/2022

STATEWIDE						DISTRICT NAME:		
						DISTRICT NUMBER:		
3 Month						12 Month		
ITEM CODE	ITEM DESCRIPTION	ITEM UNIT	STATEWIDE 3M COUNT	STATEWIDE 3M QUANTITY	STATEWIDE 3M AVG	STATEWIDE 12M COUNT	STATEWIDE 12M QUANTITY	STATEWIDE 12M AVG
70496064	ADJUST WATER VALVE BOX	EA				2	2.00	\$801.89
