

SUPPLEMENTAL WORK AUTHORIZATION NO. 7
TO
WORK AUTHORIZATION NO. 1

WILLIAMSON COUNTY ROAD BOND PROJECT:
CR 110 North

This Supplemental Work Authorization No. 7 to Work Authorization No. 1 is made pursuant to the terms and conditions of the Williamson County Contract for Engineering Services, being dated March 19, 2024 (“Contract”) and entered into by and between Williamson County, Texas, a political subdivision of the State of Texas, (the "County") and RPS Infrastructure, Inc. (the "Engineer").

WHEREAS, the County and the Engineer executed Work Authorization No. 1 dated effective March 22, 2024 (the “Work Authorization”);

WHEREAS, pursuant to Article 14 of the Contract, amendments, changes and modifications to a fully executed Work Authorization shall be made in the form of a Supplemental Work Authorization; and

WHEREAS, it has become necessary to amend, change and modify the Work Authorization.

AGREEMENT

NOW, THEREFORE, premises considered, the County and the Engineer agree that the Work Authorization shall be amended, changed and modified as follows:

- I. The Work Authorization shall terminate on February 28, 2026. The Services to be Provided by the Firm shall be fully completed on or before said date unless extended by additional Supplemental Work Authorization. The revised Work Schedule is attached hereto as Attachment “C-7” (must be attached).


Except as otherwise amended by prior or future Supplemental Work Authorizations, all other terms of the Work Authorization are unchanged and will remain in full force and effect.

This Supplemental Work Authorization does not waive the parties’ responsibilities and obligations provided under the Contract.

IN WITNESS WHEREOF, the County and the Engineer have executed this Supplemental Work Authorization, in duplicate, to be effective as of the date of the last party's execution below.

ENGINEER:

RPS Infrastructure, Inc.

By: 
Signature


Kevin Hoffman
Printed Name

Regional Director of Transportation
Title

12/8/2025
Date

COUNTY:

Williamson County, Texas

By: 
Steve Snell (Dec 17, 2025 10:49:45 CST)
Signature

Steve Snell
Printed Name

Wilco Judge
Title

12/17/2025
Date


LIST OF ATTACHMENTS

Attachment C-7 – Work Schedule

APPROVED
By Christen Eschberger at 3:14 pm, Dec 08, 2025

**ATTACHMENT C-7
WORK SCHEDULE
CR 110 NORTH-PS&E**

ID	Task Name	Duration	Est Start	Est Finish
1	CR 110 North PS&E	709 days	Fri 3/22/24	Sat 2/28/26
2	Notice to Proceed	0 days	Fri 3/22/24	Fri 3/22/24
3	Project Management	709 days	Fri 3/22/24	Sat 2/28/26
4	Communication	709 days	Fri 3/22/24	Sat 2/28/26
5	Monthly Progress Report, invoices	709 days	Fri 3/22/24	Sat 2/28/26
6	QA/QC	709 days	Fri 3/22/24	Sat 2/28/26
7	Project Coordination & Admin	709 days	Fri 3/22/24	Sat 2/28/26
8	Progress/Coordination Meetings	709 days	Fri 3/22/24	Sat 2/28/26
9	Project Schedule	709 days	Fri 3/22/24	Sat 2/28/26
10	Public Involvement	207 days	Tue 4/16/24	Fri 11/8/24
14	Utility Coordination	512 days	Sun 4/7/24	Sun 8/31/25
17	Condemnation Support	227 days	Mon 9/16/24	Wed 4/30/25
20	Survey	88 days	Mon 7/1/24	Thu 9/26/24
23	Hydrology and Hydraulics	92 days	Mon 5/27/24	Mon 8/26/24
28	Environmental	69 days	Wed 8/21/24	Mon 10/28/24
38	Geotechnical & Pavement Design Reports	86 days	Wed 8/21/24	Thu 11/14/24
47	PS&E Production	693 days	Sun 4/7/24	Sat 2/28/26
48	Roadway Modeling	40 days	Sun 4/7/24	Thu 5/16/24
53	60% Deliverables	65 days	Thu 6/6/24	Fri 8/9/24
60	90% Deliverables	66 days	Sat 8/10/24	Mon 10/14/24
67	100% Deliverables	63 days	Tue 10/15/24	Mon 12/16/24
74	Final Sealed Deliverables	251 days	Mon 6/23/25	Sat 2/28/26
75	Plans	61 days	Mon 6/23/25	Fri 8/22/25
76	Specifications	5 days	Sat 8/23/25	Wed 8/27/25
77	Estimate	5 days	Sat 8/23/25	Wed 8/27/25
78	Quality Control	9 days	Thu 8/28/25	Fri 9/5/25
79	Final Sealed Submittal	0 days	Fri 9/5/25	Fri 9/5/25
80	Client Review	14 days	Sat 9/6/25	Fri 9/19/25
81	Addressing Comments	14 days	Sat 9/20/25	Fri 10/3/25
82	THC Field Research, Reporting & Approval	148 days	Sat 10/4/25	Sat 2/28/26
83	Bid Advertisement Assistance	89 days	Sat 10/4/25	Wed 12/31/25

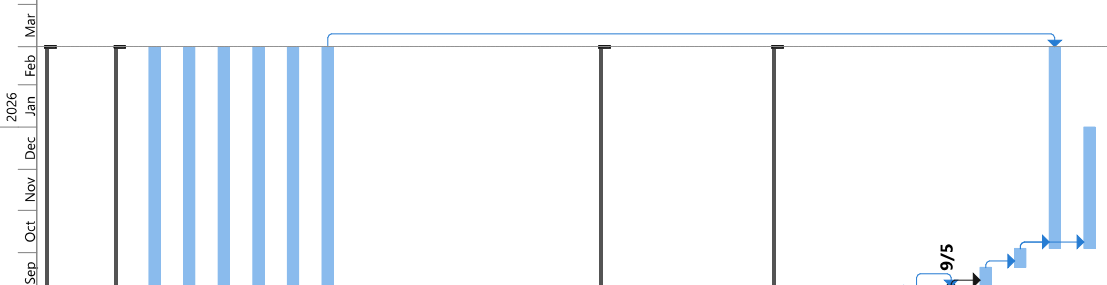









12/16/2025 Agenda Item #44 (CR110North) RPS SWA#07WA#01

Final Audit Report

2025-12-17

Created:	2025-12-12
By:	Crystal Hansen (chansen@hntb.com)
Status:	Signed
Transaction ID:	CBJCHBCAABAAI4otmaBRDJ_ACdD_B4c8symIRYCQsqV4

"12/16/2025 Agenda Item #44 (CR110North) RPS SWA#07WA#01" History

-  Document created by Crystal Hansen (chansen@hntb.com)
2025-12-12 - 4:38:58 PM GMT- IP address: 23.121.243.60
-  Document emailed to Delia Colon (delia.colon@wilcotx.gov) for signature
2025-12-17 - 3:30:24 PM GMT
-  Email viewed by Delia Colon (delia.colon@wilcotx.gov)
2025-12-17 - 3:32:10 PM GMT- IP address: 66.76.4.65
-  Document signing delegated to Steve Snell (steve.snell@wilcotx.gov) by Delia Colon (delia.colon@wilcotx.gov)
2025-12-17 - 3:36:44 PM GMT- IP address: 66.76.4.65
-  Document emailed to Steve Snell (steve.snell@wilcotx.gov) for signature
2025-12-17 - 3:36:44 PM GMT
-  Email viewed by Steve Snell (steve.snell@wilcotx.gov)
2025-12-17 - 4:49:18 PM GMT- IP address: 66.76.4.65
-  Document e-signed by Steve Snell (steve.snell@wilcotx.gov)
Signature Date: 2025-12-17 - 4:49:46 PM GMT - Time Source: server- IP address: 66.76.4.65
-  Agreement completed.
2025-12-17 - 4:49:46 PM GMT
