

**COUNTY OF YOLO**  
**DIVISION OF INTEGRATED WASTE MANAGEMENT**  
**CALIFORNIA UNIFORM PUBLIC CONSTRUCTION COST ACCOUNTING ACT**  
**CONTRACT CHANGE ORDER NO. #1**

**Federal Project No.**       N/A      

**W.O. No.**   9194  

**Project:** Waste Management Unit 2 Drainage System Modifications

**Vendor No.**  13668 

**Location:** Yolo County Central Landfill

**Date:** 9/26/25

---

To: , You are hereby directed to make the herein described changes from the PLANS and SPECIFICATIONS or do the following described WORK not included in the PLANS and SPECIFICATIONS on this CONTRACT.

Change requested by: COUNTY

---

Initial Contract Amt: \$132,000 CCO's to date: \$0.00 This CCO: \$18,000 New Encumbered Amount: \$ 150,000

---

**DESCRIPTION OF WORK**

In accordance with Section 8 of the Standard Terms & Conditions (Exhibit B) perform the following changes to the WORK.

This Contract Change Order will be on a Lump Sum Price basis for a total cost of \$18,000. Contractor shall furnish and install the following additional items:

1. 26 linear feet of 48-inch diameter storm drain.
2. 60 square feet of asphalt concrete paving, thickness to match existing
3. Install CLSM backfill within road section
4. Install aggregate base backfill in road section
5. Utilize shoring and traffic control as necessary
6. Install rock slope protection including geotextile
7. Modify grades as necessary to accommodate new features
8. Omit relocation of one condensate sump

See attached Request for Change Order #1 submitted by CONTRACTOR and attached drawing of drainage modification.

**Contractor:**

CONTRACTOR accepts the terms and conditions stated above as full and final settlement of any and all claims arising out of or related to the subject of this CONTRACT CHANGE ORDER and acknowledges that the compensation (time and cost) set forth herein comprises the total compensation due for the work or change defined in the CONTRACT CHANGE ORDER, including all impact on any unchanged work. By signing this CONTRACT CHANGE ORDER, the CONTRACTOR acknowledges and agrees that the stipulated compensation includes payment for all work contained in the CONTRACT CHANGE ORDER, plus all payment for any acceleration or interruption of schedules, extended overhead costs, delay, and all impact or cumulative impact on all WORK under this CONTRACT. The signing of this CONTRACT CHANGE ORDER acknowledges full mutual accord and satisfaction for the change and that the stated time and/or cost constitute the total equitable adjustment owed the CONTRACTOR as a result of the change. The CONTRACTOR hereby releases and agrees to waive all rights, without exception or reservation of any kind whatsoever, to file any further claim or request for equitable adjustment of any type, for any reasonably foreseeable cause that shall arise out of, or as a result of, this CONTRACT CHANGE ORDER and/or its impact on the remainder of the WORK under the CONTRACT.



YOLO COUNTY CENTRAL LANDFILL  
44090 COUNTY ROAD 28H  
WOODLAND, CA 95776

Date of Request: 9/24/2025

<b>Job Name:</b>	<b>Spec.</b>	<b>Contract #</b>	<b>Purchase Order No</b>	<b>RJG Job Number:</b>
IFB-WMU 2 DRAINAGE SYSTEM MODIFICATIONS		9194		25-0902
<b>Job Location:</b>	<b>Station #</b>	<b>Station #</b>	<b>Station #</b>	

DESCRIPTION	QTY	UNIT PRICE	AMOUNT
48 Inch Storm-Drain pipe alignment modification and inlet protection	1.00	20,100.00	20,100.00
<b>Change alignment of 48" SD road crossing:</b>			
Includes F&I additional approx. 26LF of 48" Storm drain pipe			
Additional approximately 60SF of AC paving			
CLSM backfill within road section			
AB backfill as required			
Shoring as necessary			
Traffic control as necessary			
Fit/Modify inlet to grades			
<b>SD Inlet Protection:</b>			
Confirm grades to new inlet alignment			
Excavate subgrade for RSP			
Excavate and backfill geotextile anchor trench			
F&I Geotextile			
F&I RSP			
Traffic control as necessary			
<b>Credit</b>			
Relocation of one leachate sump	-1.00	(2,100.00)	(2,100.00)

The original (Contract Sum)(Guaranteed Max Cost) was.....	132,000.00
Net Change by previously authorized Change Orders.....	-
The (Contract Sum)(Guaranteed Max Cost) prior to this Change Order was.....	132,000.00
The (Contract Sum)(Guaranteed Max Cost) will be (increased)(decreased)(unchanged) by this Change Order .....	18,000.00
The new (Contract Sum)(Guaranteed Maximum Cost) including this Change Oirder will be: .....	150,000.00
The Contract Time will be (increased)(decreased)(unchanged) by .....	[ ]Days
The Date of Substantial Completion as of the date of this Change Order therefore is.....	/ /

Agreed to:

R J Gordon Construction, Inc.

Owner \_\_\_\_\_

Contractor \_\_\_\_\_



Printed Name [Project Manager] \_\_\_\_\_



Nic Algra

Printed Name [Project Manager] \_\_\_\_\_

Signature [Project Manager] \_\_\_\_\_

*Nic Algra*  
Signature [Project Manager] \_\_\_\_\_

	<p>License # 616851 A PO Box 23204, Pleasant Hill, CA 94523 Phn: 925.680.8660 Fax: 925.680.8670 <a href="http://www.rjgordonconstruction.com">www.rjgordonconstruction.com</a></p>	
--	--	---

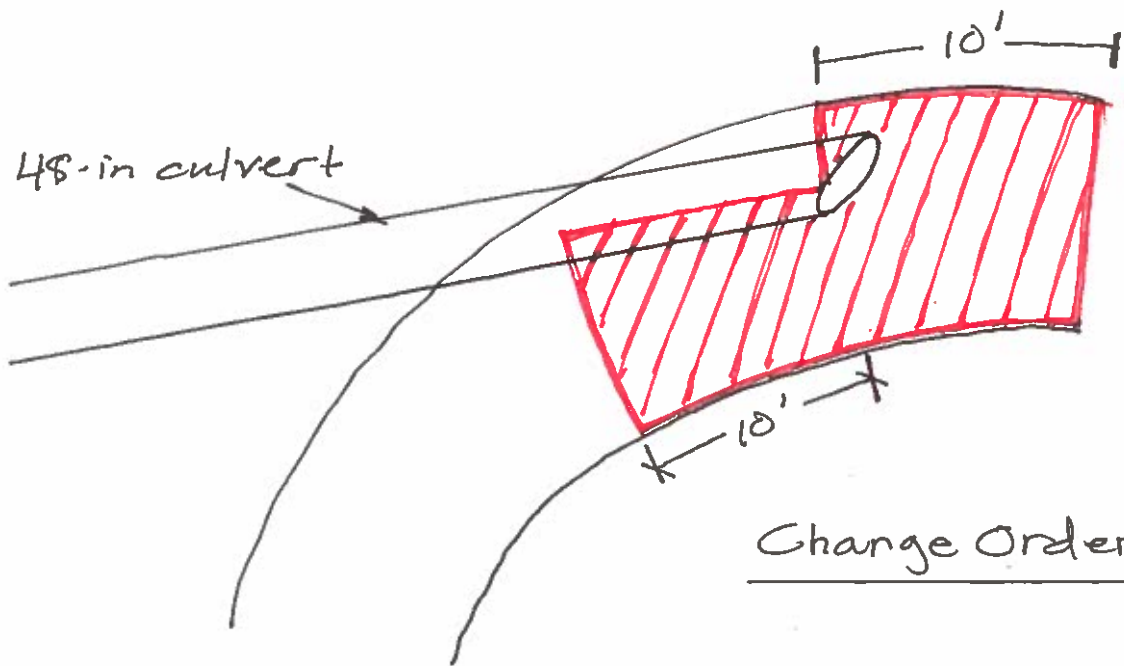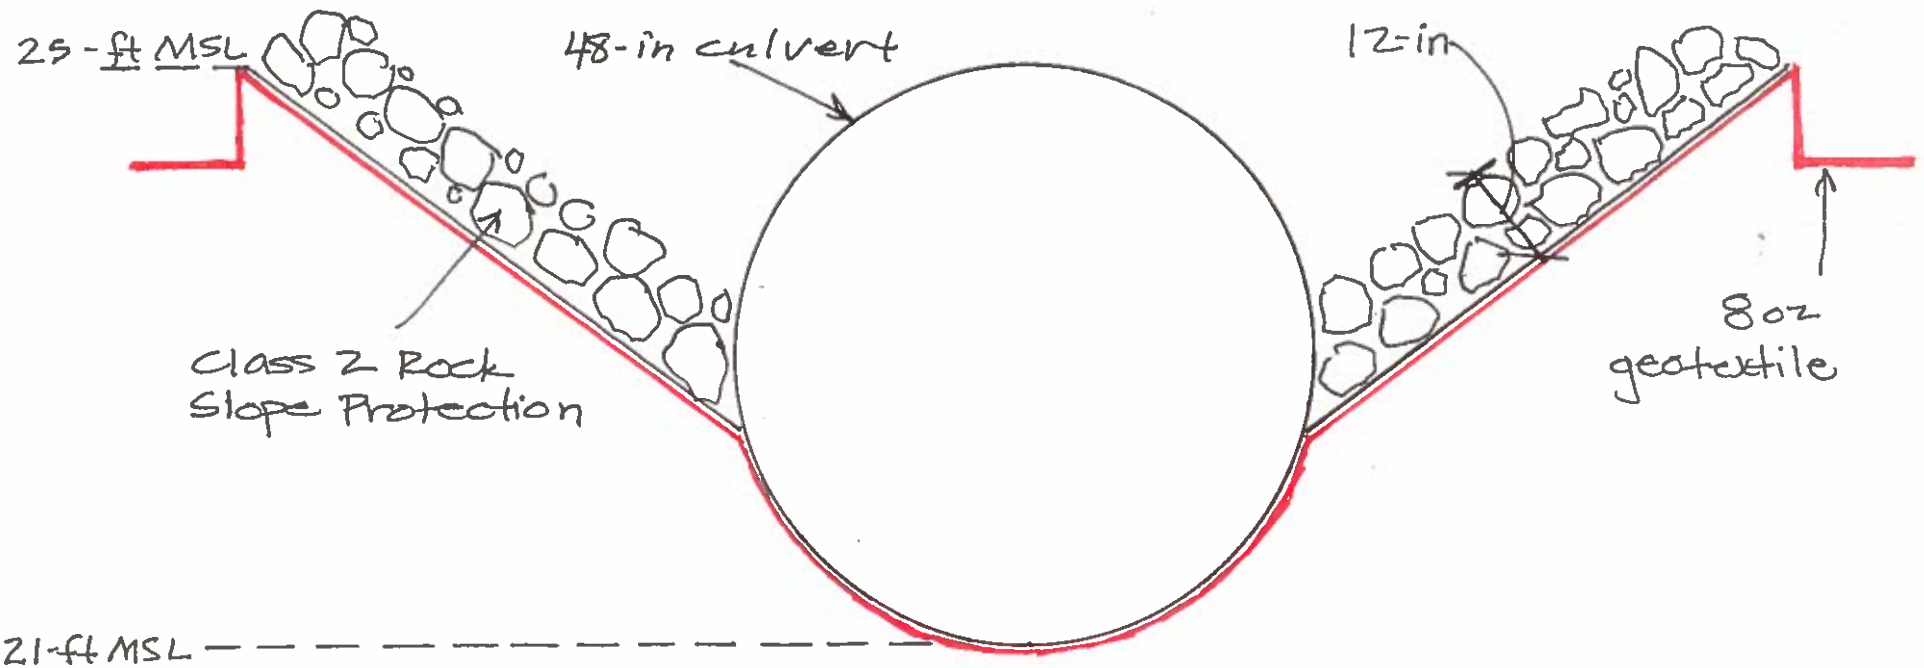

Change Order No 1. Detail
