



AIA[®] Document A133[™] – 2009 Exhibit A

Guaranteed Maximum Price Amendment

for the following PROJECT:

(Name and address or location)

New Hidalgo County Courthouse
100 N. Closner
Edinburg, TX 78539

THE OWNER:

(Name, legal status and address)

County of Hidalgo, Texas
100 East Cano, 2nd Fl
Edinburg, Texas 78539

THE CONSTRUCTION MANAGER:

(Name, legal status and address)

Morganti Texas, Inc.
10590 West Office Drive, Suite 150
Houston, TX 77459

ARTICLE A.1

§ A.1.1 Guaranteed Maximum Price

Pursuant to Section 2.2.6 of the Agreement, the Owner and Construction Manager hereby amend the Agreement to establish a Guaranteed Maximum Price. As agreed by the Owner and Construction Manager, the Guaranteed Maximum Price is an amount that the Contract Sum shall not exceed. The Contract Sum consists of the Construction Manager's Fee plus the Cost of the Work, as that term is defined in Article 6 of this Agreement.

§ A.1.1.1 The Contract Sum is guaranteed by the Construction Manager not to exceed One Hundred Twenty-Seven Million, Nine Hundred Two Thousand, Five Hundred Sixteen Dollars (\$ 127,902,516.00), subject to additions and deductions by Change Order as provided in the Contract Documents.

§ A.1.1.2 Itemized Statement of the Guaranteed Maximum Price. Provided below is an itemized statement of the Guaranteed Maximum Price organized by trade categories, allowances, contingencies, alternates, the Construction Manager's Fee, and other items that comprise the Guaranteed Maximum Price.
(Provide below or reference an attachment.)

See attached Exhibit A (GMP)

§ A.1.1.3 The Guaranteed Maximum Price is based on the following alternates, if any, which are described in the Contract Documents and are hereby accepted by the Owner:
(State the numbers or other identification of accepted alternates. If the Contract Documents permit the Owner to accept other alternates subsequent to the execution of this Amendment, attach a schedule of such other alternates showing the amount for each and the date when the amount expires.)

See Attached Exhibit A (Accepted Alternates and Approved Value Management Log)

ADDITIONS AND DELETIONS:

The author of this document has added information needed for its completion. The author may also have revised the text of the original AIA standard form. An *Additions and Deletions Report* that notes added information as well as revisions to the standard form text is available from the author and should be reviewed. A vertical line in the left margin of this document indicates where the author has added necessary information and where the author has added to or deleted from the original AIA text.

This document has important legal consequences. Consultation with an attorney is encouraged with respect to its completion or modification.

AIA Document A201[™]–2007, General Conditions of the Contract for Construction, is adopted in this document by reference. Do not use with other general conditions unless this document is modified.

Init.

§ A.1.1.4 Allowances included in the Guaranteed Maximum Price, if any:
(Identify allowance and state exclusions, if any, from the allowance price.)

Item	Price (\$0.00)
See Attached Exhibit B (Qualifications & Allowances)	

§ A.1.1.5 Assumptions, if any, on which the Guaranteed Maximum Price is based:

See Attached Exhibit B (Qualifications & Allowances)

§ A.1.1.6 The Guaranteed Maximum Price is based upon the following Supplementary and other Conditions of the Contract:

Document	Title	Date	Pages
NA			

§ A.1.1.7 The Guaranteed Maximum Price is based upon the following Specifications:
(Either list the Specifications here, or refer to an exhibit attached to this Agreement.)
See Attached Exhibit D (Drawing and Specification List)

Section	Title	Date	Pages
See Exhibit D			

§ A.1.1.8 The Guaranteed Maximum Price is based upon the following Drawings:
(Either list the Drawings here, or refer to an exhibit attached to this Agreement.)
See Attached Exhibit D (Drawing and Specification List)

Number	Title	Date
--------	-------	------

§ A.1.1.9 The Guaranteed Maximum Price is based upon the following other documents and information:
(List any other documents or information here, or refer to an exhibit attached to this Agreement.)

See Attached Exhibits C & E (Project Schedule & Look Ahead Schedule)

ARTICLE A.2

§ A.2.1 The anticipated date of Substantial Completion established by this Amendment:

7/13/2021 (Total Project Schedule of 34 Months or 1, 040 Calendar Days)

HIDALGO COUNTY

MORGANTI TEXAS, INC.

By:

OWNER (Signature)

By:

CONSTRUCTION MANAGER (Signature)

(Printed name and title)

(Printed name and title)

Hidalgo County Courthouse Exhibit A

- 50% GMP Guaranteed Maximum Price
- 50% GMP List of Accepted Alternates
- 50% GMP Accepted Value Management Log

BASE BID TABULATION																
PROJECT:		Hidalgo County Courthouse		Run: 11/1/2018		A SOLID FOUNDATION										
Exhibit A																
				</												

		TOTAL METALS								0	0	2,304,397	31,042	2,335,439	2,257,047	78,392
6	060000	WOOD, PLASTICS, AND COMPOSITES														
6	061053	ROUGH CARPENTRY	Hold	95,000	1	LS	-	-	-	-		95,000		95,000	418,920	(323,920)
6	061643	GYPSUM SHEATHING	w/ Drywall	0	1	LS	-	-	-	-		-		-		-
6	062000	FINISH CARPENTRY		6,099,973	1	LS	-	-	-	-		6,099,973		6,099,973	6,694,236	(594,263)
6	069999	Gallery Seating with Beaubois	w/062000		1	LS	-	-	-	-		-		-		-
6	069999			0	1	LS	-	-	-	-		-		-		-
6	069999			0	1	LS	-	-	-	-		-		-		-
		TOTAL CARPENTRY		6,194,973						0	0	6,194,973	-	6,194,973	7,113,156	(918,183)
7	070000	THERMAL AND MOISTURE PROTECTION														
7	071326	SELF-ADHERING SHEET MEMBRANCE WATERPROOFING (ESP)	ESP CO & WP w/ ESP (Elevator Pits, Chamberlin Has In Phase 1 Bid)	41,997	1	LS	-	-	-	-		41,997	121,140	163,137	3,315,159	(3,152,022)
7	071326	SELF-ADHERING SHEET MEMBRANCE WATERPROOFING			1	LS	-	-	-	-		-		-		-
7	071604	CONCRETE FLOOR MOISTURE TESTING	w/ Flooring (Daniel)	0	1	LS	-	-	-	-		-		-		-
7	071800	TRAFFIC COATINGS		121,720	1	LS	-	-	-	-		121,720		121,720		121,720
7	072100	Building Insulation Rigid at Stucco & Porcelain (Not Spandrel) w/ break girts		422,599	1	LS	-	-	-	-		422,599		422,599		422,599
7	072100	Batt Insulation Metal Stud framing as noted.	w/092200 EXCLUDE- None on Drawings		1	LS	-	-	-	-		-		-		-
7	072135	SPRAY APPLIED FIBER INSULATION (May be in Sally Port Roof)			1	LS	-	-	-	-		-		-		-
7	072729	FLUID APPLIED AIR BARRIER-VAPOR PERMEABLE		125,123	1	LS	-	-	-	-		125,123		125,123		125,123
7	074219	METAL PLATE RAINSCREEN WALL PANELS	EXCLUDE- None on Drawings	0	1	LS	-	-	-	-		-		-		-
7	074293	SOFFIT PANELS	w/095447	0	1	LS	-	-	-	-		-		-		-
7	074419	EXT. PORCELAIN WALL CLADDING	w/088123	0	1	LS	-	-	-	-		-		-		-
7	075421	ADHERED FLEECE BACK PVC ROOFING	w/076200		1	LS	-	-	-	-		-		-		-
7	076200	FLASHING AND SHEET METAL (Not Including Roof)		16,442	1	LS	-	-	-	-		16,442		16,442		16,442
7	076200	Roofing (Includes Wood Blocking Roof Only)		1,197,450	1	LS	-	-	-	-		1,197,450		1,197,450		1,197,450
7	077213	PREFABRICATED ROOF CURBING	W/ HVAC		1	LS	-	-	-	-		-		-		-
7	077233	ROOF HATCHES	w/076200		1	LS	-	-	-	-		-		-		-
7	078400	FIRESTOPPING (Head of CMU)		85,236	1	LS	-	-	-	-		85,236		85,236		85,236
7	078453	PERIMETER FIRE CONTAINMENT SYSTEMS	W/ glass	0	1	LS	-	-	-	-		-		-		-
7	079213	EXTERIOR JOINT SEALANTS		70,352	1	LS	-	-	-	-		70,352		70,352		70,352
7	079216	INTERIOR JOINT SEALANTS		47,991	1	LS	-	-	-	-		47,991		47,991		47,991
7	079999	Perimeter firestopping at Curtainwall?	w/ glass	0	1	LS	-	-	-	-		-		-		-
7	079999	Head of wall firestopping (drywall & CMU?)	w/078400		1	LS	-	-	-	-		-		-		-
7	079999	Security Sealants	w/Detention		1	LS	-	-	-	-		-		-		-
7	079999			0	1	LS	-	-	-	-		-		-		-
7	079999			0	1	LS	-	-	-	-		-		-		-
		TOTAL THERMAL AND MOISTURE PROTECTION		2,128,910						0	0	2,128,910	121,140	2,250,050	3,315,159	(1,065,109)
8	080000	OPENINGS														
8	081113	HOLLOW METAL DOORS AND FRAMES		1,377,741	1	LS	-	-	-	-		1,377,741		1,377,741	12,313,581	(10,935,840)
8	081216	INTERIOR ALUMINUM DOOR AND WINDOW FRAMES	w/081113	0	1	LS	-	-	-	-		-		-		-
8	081416	FLUSH WOOD DOORS	w/081113	0	1	LS	-	-	-	-		-		-		-
8	081423	PLASTIC LAMINATE FACED DOORS	EXCLUDE	0	1	LS	-	-	-	-		-		-		-
8	081433	STILE AND RAIL WOOD DOORS	w/081113	0	1	LS	-	-	-	-		-		-		-
8	083116	ACCESS PANELS AND DOORS	Allowance w/ Security	0	1	LS	-	-	-	-		-		-		-
8	083300	SIDE COILING SECURITY GRILLES (CG)		171,195	1	LS	-	-	-	-		171,195		171,195		171,195
8	083323	OVERHEAD COILING DOORS (CD)		45,414	1	LS	-	-	-	-		45,414		45,414		45,414
8	083456	SECURITY GATES		163,104	1	LS	-	-	-	-		163,104		163,104		163,104
8	083483	ELEVATOR DOOR SMOKE CONTAINMENT SYSTEM		319,750	1	LS	-	-	-	-		319,750		319,750	-	319,750
8	084113	LOW-RISE ALUMINUM STOREFRONT	w/ Glass	0	1	LS	-	-	-	-		-		-		-
8	084115	ALUMINUM-FRAMED ENTRANCES	w/ Glass	0	1	LS	-	-	-	-		-		-		-
8	084118	INTERIOR ALUMINUM STOREFRONT	w/ Glass	0	1	LS	-	-	-	-		-		-		-
8	084414	UNITIZED CURTAIN WALL ASSEMBLY	w/ Glass	0	1	LS	-	-	-	-		-		-		-
8	087100	DOOR HARDWARE	w/081113	0	1	LS	-	-	-	-		-		-		-
8	087113	AUTOMATIC SWINGING DOOR OPERATORS	ALLOWANCE	30,000	1	LS	-	-	-	-		30,000		30,000		30,000
8	088123	EXTERIOR GLASS AND GLAZING		10,953,000	1	LS	-	-	-	-		10,953,000		10,953,000		10,953,000
8	088126	INTERIOR GLASS AND GLAZING		493,620	1	LS	-	-	-	-		493,620		493,620		493,620
8	088853	SECURITY GLAZING	w/111900	0	1	LS	-	-	-	-		-		-		-
8	089100	ARCHITECTURAL LOUVERS & Roof Mech Screen Wall		850,000	1	LS	-	-	-	-		850,000		850,000		850,000
8	089999	DF&H Install (Frames/Door Slabs & Access Panels) Not Hardware		190,501	1	LS	-	-	-	-		190,501		190,501		190,501
8	089999	Escalator Smoke containment- none shown	EXCLUDED	0	1	LS	-	-	-	-		-		-		-
8	089999			0	1	LS	-	-	-	-		-		-		-
		TOTAL OPENINGS		14,594,325						0	0	14,594,325	-	14,594,325	12,313,581	2,280,744

9	090000	FINISHES													
9	092216	NON-STRUCTURAL METAL FRAMING		w/ 092900		1	LS	-	-	-	-	-		-	-
9	092236	METAL LATH			286,320	1	LS	-	-	-	-	286,320		286,320	286,320
9	092300	GYPSUM PLASTER		w/Plaster/Stucco		1	LS	-	-	-	-	-		-	-
9	092355	IMPACT RESISTANT GYPSUM PLASTER		w/Plaster/Stucco		1	LS	-	-	-	-	-		-	-
9	092423	PORTLAND CEMENT PLASTER (PC)		w/Plaster/Stucco		1	LS	-	-	-	-	-		-	-
9	092424	PORTLAND CEMENT STUCCO		w/Plaster/Stucco		1	LS	-	-	-	-	-		-	-
9	092900	GYPSUM WALLBOARD			5,097,979	1	LS	-	-	-	-	5,097,979		5,097,979	13,993,491
9	093000	TILE			1,913,205	1	LS	-	-	-	-	1,913,205		1,913,205	1,913,205
9	095100	ACOUSTICAL CEILINGS (ACT)			1,941,902	1	LS	-	-	-	-	1,941,902		1,941,902	1,941,902
9	095447	EXTERIOR MODULAR METAL CEILING SYSTEMS		w/095100		1	LS	-	-	-	-	-		-	-
9	095753	METAL SECURITY CEILINGS		w/111900		1	LS	-	-	-	-	-		-	-
9	096513	RESILIENT BASE (RB)		w/ Flooring		1	LS	-	-	-	-	-		-	-
9	096517	TILE AT MAIN ID SIGN AG-403		ALLOWANCE	5,110	1	LS	-	-	-	-	5,110		5,110	5,110
9	096536	STATIC DISSIPATIVE RESILIENT TILE FLOORING (SDRT)		w/ Flooring		1	LS	-	-	-	-	-		-	-
9	096813	CARPET TILE (CPT)		w/ Flooring		1	LS	-	-	-	-	-		-	-
9	098400	ACOUSTICAL PANEL SYSTEM - CEMENTITIOUS WOOD FIBER		w/095100		1	LS	-	-	-	-	-		-	-
9	098447	MODULAR METAL WALL SYSTEM		w/ millwork		1	LS	-	-	-	-	-		-	-
9	099123	EXTERIOR PAINTING			1,995,000	1	LS	-	-	-	-	1,995,000		1,995,000	1,995,000
9	099123	INTERIOR PAINTING		w/ Paint		1	LS	-	-	-	-	-		-	-
9	099623	GRAFFITI - MOISTURE PROTECTION SURFACE SEALER		w/ paint- ALLOWANCE		1	LS	-	-	-	-	-		-	-
9	099999	Acoustical Panels in Courtrooms (Who has this?)			323,053	1	LS	-	-	-	-	323,053		323,053	323,053
9	099999	Tile for Mega Columns and Facia				1	LS	-	-	-	-	-		-	-
9	099999					1	LS	-	-	-	-	-		-	-
9	099999					1	LS	-	-	-	-	-		-	-
		TOTAL FINISHES			11,562,569					0	0	11,562,569	-	11,562,569	13,993,491
															(2,430,922)
10	100000	SPECIALTIES													
10	101100	MARKERBOARDS AND TACKBOARDS			31,390	1	LS	-	-	-	-	31,390		31,390	1,117,742
10	101300	DIRECTORIES AND BULLETIN BOARDS			3,806	1	LS	-	-	-	-	3,806		3,806	3,806
10	101403	IDENTIFICATION DEVICES - EXTERIOR			73,440	1	LS	-	-	-	-	73,440		73,440	73,440
10	101406	IDENTIFICATION DEVICES - INTERIOR		EXCLUDED- BY OWNER	0	1	LS	-	-	-	-	-		-	-
10	101416	PLAQUES		EXCLUDED- BY OWNER	0	1	LS	-	-	-	-	-		-	-
10	101443	PHOTOLUMINESCENT EGRESS MARKINGS			59,403	1	LS	-	-	-	-	59,403		59,403	59,403
10	101463	DIGITAL SIGNAGE SYSTEMS		EXCLUDED- BY OWNER		1	LS	-	-	-	-	-		-	-
10	102114	SOLID POLYMER HDPE TOILET PARTITIONS	VE		138,402	1	LS	-	-	-	-	138,402		138,402	138,402
10	102600	WALL PROTECTION SPECIALTIES			9,076	1	LS	-	-	-	-	9,076		9,076	9,076
10	102813	TOILET AND BATH ACCESSORIES			145,937	1	LS	-	-	-	-	145,937		145,937	145,937
10	104400	FIRE PROTECTION SPECIALTIES			42,030	1	LS	-	-	-	-	42,030		42,030	42,030
10	105113	METAL LOCKERS			99,390	1	LS	-	-	-	-	99,390		99,390	99,390
10	105523	MAIL BOXES		ALLOWANCE	13,883	1	LS	-	-	-	-	13,883		13,883	13,883
10	105536	DROP BOX		ALLOWANCE	6,900	1	LS	-	-	-	-	6,900		6,900	6,900
10	105626	MOTORIZED MOBILE STORAGE SHELVING		EXCLUDED- BY OWNER	0	1	LS	-	-	-	-	-		-	-
10	107500	FLAGPOLES		PLUG	37,654	1	LS	-	-	-	-	37,654		37,654	37,654
10	108113	BIRD CONTROL DEVICE		EXCLUDED- NONE SHOWN	0	1	LS	-	-	-	-	-		-	-
10	109999	Recessed Entrance Mat- No Spec		ALLOWANCE	6,598	1	LS	-	-	-	-	6,598		6,598	6,598
10	109999				0	1	LS	-	-	-	-	-		-	-
		TOTAL SPECIALTIES			667,909					0	0	667,909	-	667,909	1,117,742
															(449,833)
11	DIV 11	EQUIPMENT													
11	111200	PARKING EQUIPMENT		ALLOWANCE	100,000	1	LS	-	-	-	-	100,000		100,000	3,500,000
11	111319	DOCK LEVELERS AND EQUIPMENT			13,690	1	LS	-	-	-	-	13,690		13,690	-
11	111900	DETENTION EQUIPMENT			3,213,400	2	LS	-	-	-	-	3,213,400		3,213,400	1
11	111919	TAMPER RESISTANT FASTENERS		w/111900	0	1	LS	-	-	-	-	-		-	-
11	112423	WINDOW WASHING SYSTEM		EXCLUDED	0	1	LS	-	-	-	-	-		-	-
11	112426	SAFETY TIE-BACKS		EXCLUDED	0	1	LS	-	-	-	-	-		-	-
11	115213	PROJECTION SCREENS		None/Excluded	0	1	LS	-	-	-	-	-		-	-
11	119999	Access Panels of any kind/ other Misc. security devices		ALLOWANCE	88,100	1	LS	-	-	-	-	88,100		88,100	-
11	119999				0	1	LS	-	-	-	-	-		-	-
		TOTAL EQUIPMENT			3,415,190					0	0	3,415,190	-	3,415,190	3,500,001
															(84,811)
12	120000	FURNISHINGS				1	LS	-	-	-	-				
12	120501	FURNITURE AND FURNISHINGS - GENERAL REQUIREMENTS		EXCLUDED	0	1	LS	-	-	-	-	-		-	-
12	122414	ROLLER SHADES		ALLOWANCE	100,000	1	LS	-	-	-	-	100,000		100,000	-
12	123200	ARCHITECTURAL CASEWORK		w/Millwork BeaBouis	0	1	LS	-	-	-	-	-		-	-
12	123663	SOLID SURFACE FABRICATIONS (SSF)		w/Millwork BeaBouis	0	1	LS	-	-	-	-	-		-	-
12	126700	BENCHES		w/Millwork BeaBouis	0	1	LS	-	-	-	-	-		-	-

12	129999				0	1	LS	-	-	-	-	-		-		-
		TOTAL FURNISHINGS			100,000					0	0	100,000	-	100,000	-	100,000
13	130000	SPECIAL CONSTRUCTION														
13	134263	STEEL DETENTION CELLS – PANELIZED CONSTRUCTION	w/111900		0	1	LS	-	-	-	-	-		-	-	-
13	139999				0	1	LS	-	-	-	-	-		-	-	-
		TOTAL SPECIAL CONSTRUCTION			0					0	0	-	-	-	-	-
14	140000	CONVEYING EQUIPMENT														
14	142100	ELECTRIC TRACTION ELEVATORS			3,865,658	1	LS	-	-	-	-	3,865,658		3,865,658	4,141,156	(275,498)
14	143100	ESCALATORS	w/142100			1	LS	-	-	-	-	-		-		-
14	144216	HYDRAULIC ELEVATOR	w/142100			1	LS	-	-	-	-	-		-		-
14	149999	Wheelchair Lifts			303,808	1	LS	-	-	-	-	303,808		303,808		303,808
		TOTAL CONVEYING EQUIPMENT			4,169,466					0	0	4,169,466	-	4,169,466	4,141,156	28,310
20	20000	MECHANICAL GENERAL REQUIREMENTS														
20	200500	SPECIAL MECHANICAL REQUIREMENTS (ESP)	w/ MEP			1	LS	-	-	-	-	-		-	-	-
20	200523	MANUAL VALVES (ESP)	w/ MEP			1	LS	-	-	-	-	-		-		-
20	200529	PENETRATIONS AND SUPPORTS (ESP)	w/ MEP			1	LS	-	-	-	-	-		-		-
20	200553	MECHANICAL IDENTIFICATIONS SYSTEMS (ESP)	w/ MEP			1	LS	-	-	-	-	-		-		-
20	201000	OUTSIDE UTILITIES - EARLY PACKAGE (ESP)	w/ MEP			1	LS	-	-	-	-	-		-		-
20	201100	PIPE AND FITTINGS (ESP)	w/ MEP			1	LS	-	-	-	-	-		-		-
20	209999	PLUMBING PIPING (ESP)	w/ MEP			1	LS	-	-	-	-	-		-		-
20	200510	ACCESS PANELS	w/ MEP			1	LS	-	-	-	-	-		-		-
20	200519	PIPING SPECIALITIES	w/ MEP			1	LS	-	-	-	-	-		-		-
20	200550	MECHANICAL SOUND AND VIBRATION CONTROL	w/ MEP			1	LS	-	-	-	-	-		-		-
20	200700	PIPE, DUCT AND EQUIPMENT INSULATION	w/ MEP			1	LS	-	-	-	-	-		-		-
20	200800	TESTING AND BALANCING (MTI NOT Commissioning)	w/HVAC		0	1	LS	-	-	-	-	-		-		-
20	209999					1	LS	-	-	-	-	-		-		-
		TOTAL MECHANICAL GENERAL REQUIREMENTS			0					0	0	-	-	-	-	-
21	210000	FIRE SUPPPRESSION														
21	211000	FIRE Suppression SYSTEMS			1,091,790	1	LS	-	-	-	-	1,091,790		1,091,790	1,392,000	(300,210)
21	212200	CLEAN AGENT FIRE PROTECTION SYSTEM	w/211000			1	LS	-	-	-	-	-		-		-
21	219999					1	LS	-	-	-	-	-		-		-
		TOTAL FIRE SUPPRESSION			1,091,790					0	0	1,091,790	-	1,091,790	1,392,000	(300,210)
22	220000	PLUMBING														
22	221016	PLUMBING PIPING (ESP)			0	1	LS	-	-	-	-	-	432,067	432,067		432,067
22	221100	WATER DISTRIBUTION SYSTEM (ESP)				1	LS	-	-	-	-	-		-		-
22	221300	SANITARY SEWERS (ESP)				1	LS	-	-	-	-	-		-		-
22	221400	STORM DRAINAGE SYSTEM (ESP)				1	LS	-	-	-	-	-		-		-
22	221016	PLUMBING PIPING			2,999,620	1	LS	-	-	-	-	2,999,620		2,999,620	4,513,740	(1,514,120)
22	221123	PLUMBING PUMPS			320,141	1	LS	-	-	-	-	320,141		320,141		320,141
22	221126	PACKAGED DOMESTIC WATER PRESSURE BOOSTER SYSTEM			39,041	1	LS	-	-	-	-	39,041		39,041		39,041
22	223116	WATER SOFTENER			28,990	1	LS	-	-	-	-	28,990		28,990		28,990
22	223300	DOMESTIC WATER HEATERS			130,838	1	LS	-	-	-	-	130,838		130,838		130,838
22	224200	PLUMBING FIXTURES			520,650	1	LS	-	-	-	-	520,650		520,650		520,650
22	229999	Plumbing Insulation			173,350	1	LS	-	-	-	-	173,350		173,350		173,350
22		Access Panels			0	1	LS	-	-	-	-	-		-		-
		TOTAL PLUMBING			4,212,630					0	0	4,212,630	432,067	4,644,697	4,513,740	130,957
23	230000	HVAC														
23	232113	HYDRONIC PIPING SYSTEM (ESP)	w/ ESP			1	LS	-	-	-	-	-		-		-
23	230000	HVAC PACKAGE 2	Include Security Barrier/Grating Grills. Nu		10,533,045	1	LS	-	-	-	-	10,533,045		10,533,045	12,833,999	(2,300,954)
		TOTAL HVAC			10,533,045					0	0	10,533,045	-	10,533,045	12,833,999	(2,300,954)
26	250000	INTEGRATED AUTOMATION														
26	255000	BUILDING MANAGEMENT AND CONTROL SYSTEM	w/230000		0	1	LS	-	-	-	-	-		-	-	-
26	259999					1	LS	-	-	-	-	-		-		-
		INTEGRATED AUTOMATION			0					0	0	-	-	-	-	-
26	260000	ELECTRICAL														
26	260010	ELECTRICAL GENERAL REQUIREMENTS			10,277,040	1	LS	-	-	-	-	10,277,040	429,913	10,706,953	10,565,996	140,957

26	260533	CONDUITS		w/ 260010		1	LS	-	-	-	-	-	-	-	-	-	-
26	260534	BOXES		w/ 260010		1	LS	-	-	-	-	-	-	-	-	-	-
26	260534	SYSTEMS		w/ 260010		1	LS	-	-	-	-	-	-	-	-	-	-
26	260000	ELECTRICAL PACKAGE 2		w/ 260010		1	LS	-	-	-	-	-	-	-	-	-	-
26	269999					1	LS	-	-	-	-	-	-	-	-	-	-
		TOTAL ELECTRICAL				10,277,040				0	0	10,277,040	429,913	10,706,953	10,565,996	140,957	
27	270000	COMMUNICATIONS															
27	270528	PATHWAYS FOR COMMUNICATION SYSTEMS (Wiring & J-Hooks/Tele/Data/Cable Tray Buildout)				1,125,385	1	LS	-	-	-	-	1,125,385		1,125,385	2,222,373	(1,096,988)
27	270000	COMMUNICATIONS FOR PACKAGE 2		w/270528			1	LS	-	-	-	-	-		-		-
27	271523	Intercommunication Systems (Master Intercom incl. handsets/cabling/cabling systems/loud speaker)				575,000	2	LS	-	-	-	-	575,000		575,000		575,000
27	274116	Integrated A/V & Equipment (Projection Screens/Microphones/Digital Signal/Amps/HDMI/Teleconference/Video Displays)				4,385,000	3	LS	-	-	-	-	4,385,000		4,385,000		4,385,000
27	274126	Television System (Ant/Signal Amps/Coax/)				320,000	4	LS	-	-	-	-	320,000		320,000		320,000
27	279999	146 Displays not on A/V drawings		Excluded			5	LS	-	-	-	-	-		-		-
27	279999	SMART ROW CONTAINMENT CENTER FOR MDF		ALLOWANCE		256,000	6	LS	-	-	-	-	256,000		256,000		256,000
27	279999						7	LS	-	-	-	-	-		-		-
27	279999	TELECOM		w/270528			1	LS	-	-	-	-	-		-		-
		TOTAL COMMUNICATIONS				6,661,385				0	0	6,661,385	-	6,661,385	2,222,373	4,439,012	
28	280000	SAFETY AND SECURITY															
28	280500	BASIC MATERIALS & METHODS FOR ELECTRONIC SYSTEMS				3,266,024	1	LS	-	-	-	-	3,266,024		3,266,024	4,311,430	(1,045,406)
28	280510	EQUIPMENT ENCLOSURES		w/280500		0	1	LS	-	-	-	-	-		-		-
28	280520	LOW VOLTAGE WIRE AND CABLE		w/280500		0	1	LS	-	-	-	-	-		-		-
28	281300	ACCESS CONTROL SYSTEM		w/280500		0	1	LS	-	-	-	-	-		-		-
28	282000	DETENTION COMMUNICATION SYSTEM		w/280500		0	1	LS	-	-	-	-	-		-		-
28	282300	VIDEO SURVEILLANCE SYSTEM		w/280500		0	1	LS	-	-	-	-	-		-		-
28	283100	FIRE ALARM SYSTEM				1,442,475	1	LS	-	-	-	-	1,442,475		1,442,475	1,160,638	281,837
28	283113	FIRE ALARM AND DETECTION SYSTEMS		w/283100		0	1	LS	-	-	-	-	-		-		-
28	283113E	FIRE ALARM AND DETECTION SYSTEMS		w/283100		0	1	LS	-	-	-	-	-		-		-
28	283130	AIR SAMPLING SMOKE DETECTION SYSTEM		w/283100		0	1	LS	-	-	-	-	-		-		-
28	283143	FIRE DEPARTMENT RADIO SYSTEM		w/280500		0	1	LS	-	-	-	-	-		-		-
28	284610	PROGRAMMABLE LOGIC CONTROLLER		w/280500		0	1	LS	-	-	-	-	-		-		-
28	284620	GRAPHICAL USER INTERFACE		w/280500		0	1	LS	-	-	-	-	-		-		-
28	284630	NETWORK EQUIPMENT		w/280500		0	1	LS	-	-	-	-	-		-		-
28	285000	UNINTERRUPTIBLE POWER SUPPLY		w/280500		0	1	LS	-	-	-	-	-		-		-
28	289999					0	1	LS	-	-	-	-	-		-		-
		TOTAL SAFETY AND SECURITY				4,708,499				0	0	4,708,499	-	4,708,499	5,472,068	(763,569)	
31	310000	SITE IMPROVEMENTS															
31	311000	SITE CLEARING (ESP)		EXCLUDE- ALL ESP		0	-	LS	-	-	-	-	-	998,600	998,600	1,307,100	(308,500)
31	312200	SITE EXCAVATION AND ROUGH GRADING (ESP)				0	1	LS	-	-	-	-	-		-		-
31	312213	ROUGH GRADING (ESP)				0	1	LS	-	-	-	-	-		-		-
31	312300	BUILDING EXCAVATION, FILLING, AND BACKFILLING (ESP)				0	1	LS	-	-	-	-	-		-		-
31	312319	DEWATERING (ESP)				0	1	LS	-	-	-	-	-		-		-
31	312323	TRENCH EXCAVATION AND BACKFILL (ESP)				0	1	LS	-	-	-	-	-		-		-
31	312333	TRENCHING, BACKFILLING AND COMPACTING FOR UTILITIES (ESP)				0	1	LS	-	-	-	-	-		-		-
31	312500	EROSION, SEDIMENT & DUST CONTROL (ESP)				0	1	LS	-	-	-	-	-	243,500	243,500		243,500
31	313116	TERMITE CONTROL (ESP)				0	1	LS	-	-	-	-	-	27,000	27,000		27,000
31	316329	DRILLED PIERS (ESP)				0	1	LS	-	-	-	-	-		-		-
31	319999	SLURRY EXISTING UTILITIES (ESP)				0	1	LS	-	-	-	-	-	65,000	65,000		65,000
31	319999	SURVEYING (ESP)				0	1	LS	-	-	-	-	-	22,430	22,430		22,430
31	312200	SITE EXCAVATION AND ROUGH GRADING				0	1	LS	-	-	-	-	-		-		-
31	312219	TOPSOILING AND FINISHED GRADING				0	1	LS	-	-	-	-	-		-		-
31	319999					0	1	LS	-	-	-	-	-		-		-
		TOTAL SITE IMPROVEMENTS				0				0	0	-	1,356,530	1,356,530	1,307,100	49,430	
32	320000	EXTERIOR IMPROVEMENTS															
31	321313	CONCRETE PAVING, CURBS and PIER Change				1,662,830	-	LS	-	-	-	-	1,662,830		1,662,830	2,345,204	(682,374)
32	321315	DECORATIVE CEMENT CONCRETE PAVEMENT		w/321313		0	1	LS	-	-	-	-	-		-		-
32	321713	PARKING BUMPERS				14,884	1	LS	-	-	-	-	14,884		14,884		14,884
32	321723	PAVING STRIPING AND MARKING				0	1	LS	-	-	-	-	-		-		-
32	323115	GATE OPERATOR - SLIDING				0	1	LS	-	-	-	-	-		-		-
32	323118	PRE-FABRICATED ORNAMENTAL ALUMINUM FENCE				99,923	1	LS	-	-	-	-	99,923		99,923		99,923
32	328423	IRRIGATION SYSTEM				355,074	1	LS	-	-	-	-	355,074		355,074		355,074
32	329219	SEEDING		w/328423		0	1	LS	-	-	-	-	-		-		-

[illegible]

Hidalgo County Courthouse
Accepted Alternates
[Exhibit A](#)

Alt 1	Build and Cold Shell 3rd Floor Area C (Bump Out)	\$611,355
Alt 6	Eliminate NE Green Space and Leave as Parking	-\$153,038
Alt 9	Change 2x6 Acoustical Ceiling Tiles to 2x2 Acoustical Ceiling Tiles	-\$47,561
Alt 14	Provide 2 Moveable Roof Davits	\$11,708

Total Value of Accepted Alternates

\$422,464

		Exhibit A																			
		Hidalgo County Court House																			
		Edinburg, TX 78539																			
		November 1, 2018																			
		Hidalgo County Courthouse 50% CDs																			
		▶ Value Management Summary																			
Approval Codes: A=Approved, Proceed; B=Rejected Final ; C=Hold, Pending Approval; D=Rejected-Owner to Acknowledge																					
Item No.	Item Description	Date Initiated	Total Cost	Owner Approval Code	Further Action By:	Required Complete Date	Amount Accepted (Code A & B)	Scope Change Rejected (Code D)	Pending Approval (Code C)	Comments	Corresponding / Conflicting VE Item										
	Civil & Landscaping																				
C1	Reduce Landscaping to CoE minimum	1-Nov-18	(\$70,000)	C					(\$70,000)												
C2	Save and utilize existing North End of Closner St for connection to new access drive.	1-Nov-18	(\$93,000)	C					(\$93,000)												
C3	Delete custom stamped/patterned walk concrete for standard concrete	1-Nov-18	(\$68,500)	C					(\$68,500)		A18										
C4	Delete patterned vehicular concrete paving for standard paving	1-Nov-18	W/ C3	C							A17										
	Structural																				
S1	Use fiber mesh in lieu of rebar at slab on grade	1-Nov-18	(\$55,000)	D				(\$55,000)													
S2	Use CMU in lieu of cast in place concrete at sheer walls at stairs	31-Oct-18	(\$250,000)	D				(\$250,000)													
S3																					
	Architectural																				
A1	Shell 2 Court Rooms and Back of House 10,849 SF at \$140/sf	1-Nov-18	(\$1,518,860)	D				(\$1,518,860)			Verify other shell options										
A2	Reduce SF back to program -45K SF	1-Nov-18	(\$15,040,000)	D				(\$15,040,000)													
A3	Delete Wheel Chair Lifts in favor of wood removable ramps or economical alternate (1 Per floor)	1-Nov-18	(\$213,808)	C					(\$213,808)												
A4	Delete Millwork Base and provide rubber base (ROPE Black/Brown 4"x1/8" Rubber Cove Molding 700 Series would cost USD\$5,021.00. We are still trying to get the cost of the wood base broken out.	1-Nov-18	(\$95,399)	C					(\$95,399)												
A5	Move exterior & interior identification devices to FFE	1-Nov-18	(\$73,000)	C					(\$73,000)												
A6	Slope roof 1/4" to reduce insulation	1-Nov-18	(\$300,000)	D				(\$300,000)													
A7	Delete all Stucco/Plaster at security wall, sally port and judges parking. Use colored CMU in lieu of standard CMU.	1-Nov-18	(\$205,000)	C					(\$205,000)												
A8	Delete all CMU at security wall and replace with 8' metal fence. Use colored CMU instead of stucco/plaster on judges parking and sally port. Change piers to footings	1-Nov-18	(\$225,000)	D				(\$225,000)													
A9	Move Courtroom Pews to FFE	1-Nov-18	(\$325,000)	D				(\$325,000)													
A10	Move Corridor Benches to FFE	1-Nov-18	(\$160,000)	D				(\$160,000)													
A11	Shell misc. square footage (Need areas where this might be possible) 10000 SF (target) \$90/ft	1-Nov-18	(\$900,000)	D				(\$900,000)													
A12	Delete roof penthouse for freight elevator	1-Nov-18	(\$25,000)	C					(\$25,000)												
A13	Delete freight elevator roof stop	1-Nov-18	(\$22,000)	C					(\$22,000)												
A14	Use TPO Roof in lieu of fleece back roof	1-Nov-18	(\$135,170)	C					(\$135,170)												
A15	Use Mod Bit in lieu of fleece back roof	1-Nov-18	(\$17,000)	D				(\$17,000)													
A16	Delete aluminum canopy at CUP	1-Nov-18	(\$38,135)	C					(\$38,135)												
A17	Delete site furnishings, decorative bollards, trash receptacles and benches.	1-Nov-18	(\$90,000)	C					(\$90,000)												
A18	Remove All Corridor Millwork	1-Nov-18	(\$186,000)	D				(\$186,000)													
A19	Shell one additional floor	1-Nov-18	(\$4,950,000)	D				(\$4,950,000)													
A20	Apply vinyl sign on curtainwall prior to setting in place	1-Nov-18	(\$22,000)	C					(\$22,000)												
A21	Use colored non-stc rated glass in lieu of porcelain panels	1-Nov-18	(\$310,000)	D				(\$310,000)													
A22	Alternate smoke doors. (Verified)	19-Oct-18	(\$20,000)	C					(\$20,000)												
A23	Delete anti graffiti surface	20-Oct-18	(\$150,000)	C					(\$150,000)												
A24	Delete roof mechanical screen wall	21-Oct-18	(\$347,316)	C					(\$347,316)												
A25	Delete main bldg. louvers	22-Oct-18	(\$60,000)	D				(\$60,000)													
A26	Delete CUP screen wall (replace with what?)	23-Oct-18	(\$97,000)	C					(\$97,000)												
A27	Delete sally port screen wall (replace with what?)	24-Oct-18	(\$175,500)	C					(\$175,500)												
A28	Brise Solei Steel frame in lieu of alum (Verified)	25-Oct-18	(\$37,250)	C					(\$37,250)												
A29	Delete Evidence storage partition walls at district clerk. Delete individual MEP utilities in favor of global utilities. (Verified)	27-Oct-18	(\$48,247)	C					(\$48,247)												
A30	Replace CMU walls north of holding in favor of standard metal framing and gyp board/paint. 12 locations throughout. (Not sure this can be done due to Security Issues) (Number is Verified)	27-Oct-18	(\$68,212)	C					(\$68,212)												
A31	ACM Panels in Lieu of Porcelain at Mega Columns	30-Oct-18	(\$123,250)	C					(\$123,250)												
A32	Delete Mega Column Decorative Panels	1-Nov-18	(\$350,000)	D				(\$350,000)													
A33	Change ACT-3 & ACT-4 from Tropic Models to Alaska Models	30-Oct-18	(\$142,979)	C					(\$142,979)												



Hidalgo County Court House
Edinburg, TX 78539
November 1, 2018
Hidalgo County Courthouse 50% CDs

HIDALGO COUNTY

JACOBS

HR

► Value Management Summary

Approval Codes: A=Approved, Proceed; B=Rejected Final ; C=Hold, Pending Approval; D=Rejected-Owner to Acknowledge

Item No.	Item Description	Date Initiated	Total Cost	Owner Approval Code	Further Action By:	Required Complete Date	Amount Accepted (Code A & B)	Scope Change Rejected (Code D)	Pending Approval (Code C)	Comments	Corresponding / Conflicting VE Item
A34	Change Exterior Soffit Panels from USG Ceilings Plus to American Decorative	30-Oct-18	(\$248,153)	C					(\$248,153)		
A35	Revise Interior Framing Loads for All Typical Walls & Restroom Walls to Industry Standard 5 PSF in lieu of what is specified in 09 22 16	30-Oct-18	(\$43,480)	D				(\$43,480)			
A36	Use Acoufelt Acoustical Wall Panels in Lieu of Specified Kirie	30-Oct-18	(\$98,549)	C					(\$98,549)		
A37	Alternate Flooring manufacturers (Use Interceramic for tile and Milliken for carpet). The SDRT and Linoleum will remain as scheduled.	1-Nov-18	(\$250,000)	D				(\$250,000)			
	Mechanical										
M1	Change one chiller/HVAC system to future (along with shelled space above). Is this a possibility?	1-Nov-18	(\$250,000)	D				(\$250,000)			Plug
M2	Change AHU coils from .025 to .020	1-Nov-18	(\$10,000)	D				(\$10,000)			
M3	Change AHU floor gauge to 1/8" thick and wall/roof to 18 ga	1-Nov-18	(\$8,000)	D				(\$8,000)			
M4	Change AHU wall/roof to galvanized	1-Nov-18	(\$28,000)	D				(\$28,000)			
M5	Insulate CHW lines with fiberglass	1-Nov-18	(\$51,000)	D				(\$51,000)			
M6	Delete Domestic CW piping insulation (except in areas subject to freezing)	1-Nov-18	(\$60,000)	C					(\$60,000)		
M7	Insulate roof drain piping insulation w/ flexible mineral fiber blanket in lieu of specified duct wrap (Verify not to be used in plenum spaces)	1-Nov-18	(\$18,370)	C					(\$18,370)		
M8	Alternate plumbing fixture package	1-Nov-18	(\$135,000)	D				(\$135,000)			
M9	WH's at gang RRS and Insta-Hots at judges chambers, servery and food prep.	1-Nov-18	(\$285,000)	C					(\$285,000)		
	Electrical/Low Voltage										
E1	More Economical Light Fixtures & Gear - Target	16-Jul-18	(\$165,000)	C					(\$165,000)		
E2	Move Complete Div. 271523, 274116 & 274126 to Courtroom Tech. Including digital display directories. MTI has conduit and back boxes	1-Nov-18	(\$5,400,000)	C					(\$5,400,000)		
E3	MC Cable in lieu of Conduit. Home runs in conduit	1-Nov-18	(\$340,000)	C					(\$340,000)		E8
E4	Reduce Active Server Rooms from 8 to 2.	1-Nov-18	(\$189,600)	D				(\$189,600)			
E5	Remove Networked Lighting Control System (substitution as recommended by South West Electric Specs)	1-Nov-18	(\$319,000)	D				(\$319,000)			
E6	Reduce LV drops from 4,600 to 3,000	1-Nov-18	(\$376,000)	C					(\$376,000)		
E7	Use refurbished generator	1-Nov-18	(\$90,000)	D							
E8	Generator & Emergency Power Reduction - Target	1-Nov-18	(\$120,000)	C					(\$120,000)		E3
	NOT ALL ESTIMATED TOTALS CAN BE USED TOGETHER. ONCE FULL ACCEPTED THE VALUES WILL BE UPDATED TO CORRECT TOTAL					Total Rejected		(\$25,930,940)			
						Total Pending			(\$9,471,838)		
						Accepted Total Project					
						Total if All Accepted	(\$9,471,838)				
						Current Budget	\$136,951,890				
						Approved Items Delta +/-	\$127,480,052				

Base Bid	136,951,890
Alts	422,464
VE	(9,471,838)
Total	127,902,516

Hidalgo County Courthouse Exhibit B

- 50% GMP Qualifications, Clarifications & Assumptions

Qualifications, Clarifications & Assumptions
Hidalgo County Courthouse
GMP at 50% CD's

Exhibit B
11/1/2018

Document Acknowledgement

- This Guaranteed Maximum Price ("GMP") is based upon the Hidalgo County, Texas New County Courthouse – Project No. 10085982 Courthouse Square Edinburg, Texas 78539 - 50% Construction Documents dated 09/04/2018 and through Addendum No. 3 to 50% Construction Documents and Specifications for New Hidalgo County Courthouse dated 10/4/2018 as reflected in Exhibit "D". MORGANTI TEXAS, INC. (MTI) has also included the Hidalgo County, Texas – New County Courthouse – Project No. 10085982 Courthouse Square Edinburg, Texas 78539 - 100% Construction Documents – Dated 09/04/2018 Structural Package and Addendum No. 1 To 100% Structural Construction Documents and Specifications for New Hidalgo County Courthouse dated 09/21/2018. Other Addendums and documents are excluded at this time and will be addressed following GMP.
- No work or changes in any addendum that affects the Early Site Package has been included in this GMP.
- The GMP includes a limited allowance of \$559,144 for any items requiring additional information, design or detailing. Further development of drawings are not included at this time beyond this allowance as our previous discussions indicated a limited GMP and further development of design must remain within the funds available.

Division 01: General Requirements

- The proposal is for the total project only, individual line item amounts are not guaranteed and may increase or decrease as the project progresses. (This is not a Line Item Estimate). This GMP will not change except through County-approved Change Orders based on changes in design.
- This GMP is based on an overall project schedule of (34 Months) 1040 calendar days from receipt of fully executed GMP2, notice to proceed and assumes approval of permitting for the remainder of the project in accordance with the construction schedule. An allowance for anticipated weather days been included within the 1,040 calendar days per 1.1.12 of the A201 General Conditions.
- We have found multiple items in the specifications that are not indicated on the drawings and are therefore impossible to quantify and price. We have identified some of these items below in more detail, specifications and drawings still need to be coordinated as the design progresses.
- This GMP does not include any City of Edinburg plan review comments which may increase or decrease the scope of the project.
- CCIP will be utilized for General Liability Insurance at lump sum amount of 1.30% of the total contract value. Coverage for the project and subcontractors will be in accordance with the CCIP policy for onsite work. Offsite coverage for insurance will be per the subcontractor's standard policy and will not include increased limits as these would be prohibitively expensive.
- Generally, a five day work week and normal working hours are included with the ability to work necessary hours or weekends from time to time. We are unaware of any Owner restrictions on work hours.

Construction Management | General Contracting | Design Build | Project Management

MORGANTI TEXAS, INC. ■ WWW.MORGANTI.COM

10590 Westoffice Drive, Suite 150 ■ Houston, Texas 77042 ■ Phone: (281) 448-1015 ■ Fax: (281) 448-8416

AFFIRMATIVE ACTION / EQUAL OPPORTUNITY EMPLOYER

- An allowance of \$115,000 for permitting costs and any other payments required by City of Edinburg is included.
 - MTI has excluded any utility usage or connection fees as these are covered by the Owner.
 - Coordination of the different design disciplines is not complete at the 50% Construction Document stage. Morganti reserves the right to adjust pricing accordingly once 95% Construction Documents are received if needed once this coordination is complete.
 - Our constructability comments have been issued separately.
 - Wage rates are based on South Texas College wage rates dated 4/26/16.
 - Any change orders associated with Package 1 are not included in this GMP.
 - Any Package 1 specifications are not included in this GMP.
 - All Package 1 RFI's have been excluded from this budget.
-
- This GMP assumes that any change orders required during the course of the project will be executed promptly and that the aggregate amount of any CCD's open where MTI is required to proceed will be limited to no more than \$200,000.
 - The GMP includes a contingency to be utilized by the Construction Manager as needed during the construction process. Issues for which this contingency may be used include, but are not limited to: expediting, temporary protection, overtime, shiftwork, scope gaps, subcontractor failures, low estimates, weather protection, escalation, deductibles, cost overruns and other circumstances that may arise or that may not be quantifiable prior to creation of the GMP. This contingency is not intended to be used for changes in the scope of the work or to cover errors or omissions in the construction documents. Any contingency remaining at the conclusion of the project will be treated as savings and returned to the Owner in accordance with the contract.

Division 02: Existing Conditions

- MTI's current plan is to have two tower cranes and one dual man and material hoist for the project for a duration of 14 months.

Division 03: Concrete

- MTI has excluded any precast concrete structures as none were found.
- Concrete pricing is based on bottom of slab to top of structure along with the CUP and Sallie Port.
- MTI has excluded any post tensioning as none was shown.
- GMP is contingent upon approval by all parties of the financials for Limon and Salazar as well as the JV agreement and proposed subcontract security provided by them in order to utilize their pricing.

Division 04: Masonry

- MTI has excluded integral waterproofing admixture. No locations for it could be found.
- MTI has excluded glass unit masonry units mentioned in specifications. None could be found.
- MTI has included an allowance of \$12,500 for Neoprene Pad at Top of CMU Detail A4/S-042E

Division 05: Metals

- MTI has excluded canopies at the CUP.

- MTI has included an allowance of \$560,000 for the Brise Soleil system and aluminum panel system including all framing, decorative metal aluminum panels and accessories.
- MTI has excluded restroom support frames as they were not shown in the contract documents.
- MTI has excluded Unistrut support metal as they do not show locations or quantities in the contract documents.
- MTI has excluded glass railings.
- MTI has included a steel ladder in lieu of aluminum ladders @ roof hatches.
- MTI has included a \$110,000 allowance for the MEP platform as shown on S1.08 / A and assumes this will be fully designed by the EOR. We have not included any design costs in this GMP for this work.

Division 06: Woods, Plastics, and Composites

- Jury Box seating has been excluded from this proposal as this is part of FF&E.
- Wood Base WB-1 will be custom made from Beaubois.
- The specified “Ceilings Plus” laminate is not compatible with the adhesives and equipment in use by the millwork fabricator. The fabricator will provide product data and samples of similar laminate for review and approval of the Architect.

Division 07: Thermal & Moisture Protection

- MTI has excluded the Vegetated Roof System; a standard roof will be provided.
- MTI has only included an expansion joint system between the sally port and the courthouse building.
- MTI has excluded Electric Field Vector Mapping (EFVM) testing at roof.
- MTI has excluded expansion joint covers as they do not appear on the contract documents.
- MTI has excluded Spray Applied Fire Proofing as it is not shown in the contract documents.
- MTI has excluded Spray Applied Fiber Insulation as they are no locations shown on the contract documents.
- MTI has excluded Metal Plate Rainscreen Wall Panels as they do not show location on drawings and this appears to be a specification that is not used.
- MTI has included the Fleece Back Roof shown on the contract documents but has excluded (075215) Modified Bitumen Roofing System due to incomplete spec section and drawings details.
- MTI has excluded downspouts and gutters as they do not show locations on drawings and therefore cannot be quantified.

Division 08: Openings

- MTI is excluding elevations 1, 2, 3, 5, & 7 on A-621 as they cannot be found on floor plans.
- MTI has included an allowance of \$30,000 for auto operators. Current documents do not show any locations.
- MTI has excluded plastic laminate doors per specification 08 14 23 as current door schedule does not indicate any.
- MTI has excluded key cabinets.
- MTI has excluded draft/fire curtains at escalators as they are called for in the specifications, but none are currently shown on the drawings.

Construction Management | General Contracting | Design Build | Project Management

- MTI has excluded curtain wall chamber testing. All testing to be done by an independent agent by Owner.

Division 09: Finishes

- MTI has excluded stucco and / or Plaster moldings as none are currently shown.
- MTI has excluded floor moisture treatment/remediation costs in the event concrete does not cure in time for floor installation.
- MTI has excluded any interior stucco and / or plaster as none is currently shown. Exterior stucco is included.
- MTI has excluded porcelain tile PT-5 as no locations could be found in current drawings.
- MTI has excluded all mineral wool insulation behind stucco and assumed rigid insulation.
- MTI has included an allowance of \$5,110 for the porcelain tile at the main ID sign shown on AG-403 as documents do not specify manufacturer or model of tile to use.

Division 10: Specialties

- MTI has excluded picture rails. These are part of FF&E package by owner.
- MTI has accounted for 5ft by 4ft glass enclosed bulletin boards. MTI is excluding illuminated directories and non-illuminated directories mentioned in specification 10 11 00.
- MTI has excluded general interior signage per specification 10 14 06. Interior signage is part of FF&E by owner (includes signage at clerk, county seals at courtrooms, and vinyl transfer graphic designs). MTI has included the monument sign, the vinyl sign on the window and code required signage only. All other signage is to be provided by owner as part of the FF&E.
- MTI has excluded Bird Control Devices per specification 10 81 13 as current documents do not show locations.
- MTI has excluded CG-2, SSCG-1, SSCG-2, PCG, WG, HR-1, and CR-1 mentioned in specification 10 26 00.
- MTI has accounted for fire extinguishers and cabinets per specification 10 44 00. MTI is excluding the oval fire extinguishers and carbon dioxide fire extinguishers mentioned in the drawing legends.
- MTI has excluded providing any hand dryers.
- MTI has excluded the digital signage system (by Owner).
- MTI has included an allowance of \$13,883 for mailboxes.
- MTI has included an allowance of \$6,900 for drop boxes.
- MTI has included an allowance of \$6,598 for Recessed entrance Mats.

Division 11: Equipment

- The GMP includes using Maxwell System in lieu of the Trust Build system specified for Detention Cells.
- MTI has included the window washing system davits as indicated in the accepted list of alternates.
- MTI has excluded any concrete bases for security pedestals – none were found.
- MTI has excluded any cell padding for detention cells.
- MTI has included an allowance of \$88,100 for access panels and any required hardware.
- MTI has excluded appliances. No appliance schedule has been provided to include in pricing.
- MTI has included an allowance of \$100,000 for Parking Equipment.

Division 12: Furnishings

Construction Management | General Contracting | Design Build | Project Management

- MTI is currently accounting for using Nevamar manufacturer's color Straightway Oak WO0040T for PL-1. The millwork subcontractor does not believe the ceilings plus material currently specified will work for the shown applications. The supplier cannot use the Ceilings Plus material at their plant due to the required glue creating contamination within the plant.
- MTI is including surface mounted post supports in lieu of what is shown on detail 10/A-571.
- MTI has excluded GSA and AWI labels as they are not required.
- MTI has excluded cipher locks, keyless security locks, and wireless cabinet locks mentioned in the specification 12 32 00 as none are shown in the current documents.
- MTI has excluded window sills mentioned in specification 12 32 00 as none are shown in current documents.
- MTI has excluded plexiglass and tack boards mentioned in specification 12 32 00 as none are shown in current documents.
- MTI has excluded jury seating and lecterns as they are part of the FF&E package by owner.
- MTI has excluded all wood panel wainscot similar to that shown on A-621 / 6.
- MTI has excluded solid surface integral sinks mentioned in specification 12 36 36 as they do not appear in the contract documents.
- MTI is currently accounting for SS-3/SS-4 cap on the waiting sides of transaction counter per I series drawings (I-101C for example).
- All low walls similar to sheet A-570 / 9 are included as wood structure and primed Non- fire rated MDF instead of metal stud and gyp board.
- MTI has included an allowance of \$100,000 for Window Coverings. Windows to receive coverings have not yet been indicated.

Division 13: Special Construction

- N/A

Division 14: Conveying Equipment

- MTI has used Schindler Elevators for this GMP.
- MTI is currently using the drawings for pricing as the specifications are currently in conflict.
- The main passenger elevator requires a room to house controls and cannot be more than 75ft from the overhead machine room. Current documents do not show this.
- MTI excludes knock out panels for Elevator door openings for Elevators P4 and P8 and drywall will be used to close the openings.
- In order to obtain elevators, prepayment must be made by the County to MTI and by MTI to the elevator vendor before the elevators can be placed into production.

Division 21: Fire Suppression

- MTI has excluded any painting of piping.

Division 22: Plumbing

- MTI has excluded any painting of plumbing system.
- MTI has excluded any systems for gases, devices or equipment.
- MTI has excluded all plumbing not shown on contract documents.

Construction Management | General Contracting | Design Build | Project Management

Division 23: HVAC

- MTI has excluded any painting of HVAC systems.
- MTI has excluded any commissioning by 3rd party; HVAC will assist 3rd party agent contracted directly by the Owner.
- MTI has excluded any kitchen/science/fume hoods.
- MTI has excluded Sound Analysis Testing.
- MTI has excluded dehumidifiers.
- MTI has excluded all HVAC not shown on contract documents.
- MTI has excluded ductwork cleaning.
- MTI has excluded the Louvered Penthouse mentioned in specification 23 37 23 as it does not appear in the contract documents.

Division 26: Electrical

- MTI has excluded the raceway, labor, and cost for primary electrical service entrance from electrical pole to primary load of Utility transformer as we understand this is to be provided by the utility provider.
- MTI has excluded any painting of electrical systems.
- MTI has excluded the cost of additional lighting modifications due to an incomplete emergency and egress lighting.
- MTI has excluded all electrical not shown on contract documents.
- MTI has included an alternative light fixture package in this GMP that will need to be reviewed by the architect. The specified light fixture package vendor did not provide pricing. Any adjustments requested will need to be maintained within the current pricing structure.

Division 27: Communications

- MTI has included an allowance of \$256,000 for Smart Row Containment Center (air coolant for MDF room).
- MTI has provided a cost for upgraded UPS system from 3KVA to 16KVA per load analysis of sub-contractor. This was priced as described by all competitive subcontractors.
- MTI has excluded all wireless access points, network switches, phones, as these are provided as part of the Owner's FF&E/Technology budget.

Division 28: Electronic Safety Security

- MTI has excluded the air sampling smoke detection system - not enough information on plans or specs to provide estimate.

Division 31: Earthwork

- MTI has included Division 31 costs in Package 1 GMP.

Division 32: Exterior Improvements

- MTI has included an allowance of \$90,952 for site furnishings.
- MTI has excluded all sodding per specification 32 92 23 as none was shown.
- MTI has excluded a permanent irrigation system as none was shown.

Division 33: Utilities.

Construction Management | General Contracting | Design Build | Project Management

- Storm system upgrades are being priced in Package 1 since this affects this scope of work.
- Lift station design is not specified on plans. Pricing subject to change after final design.


Construction Management | General Contracting | Design Build | Project Management


MORGANTI TEXAS, INC. ■ WWW.MORGANTI.COM

10590 Westoffice Drive, Suite 150 ■ Houston, Texas 77042 ■ Phone: (281) 448-1015 ■ Fax: (281) 448-8416


AFFIRMATIVE ACTION / EQUAL OPPORTUNITY EMPLOYER

Hidalgo County Courthouse Exhibit C
- Tentative 50% GMP Project Schedule

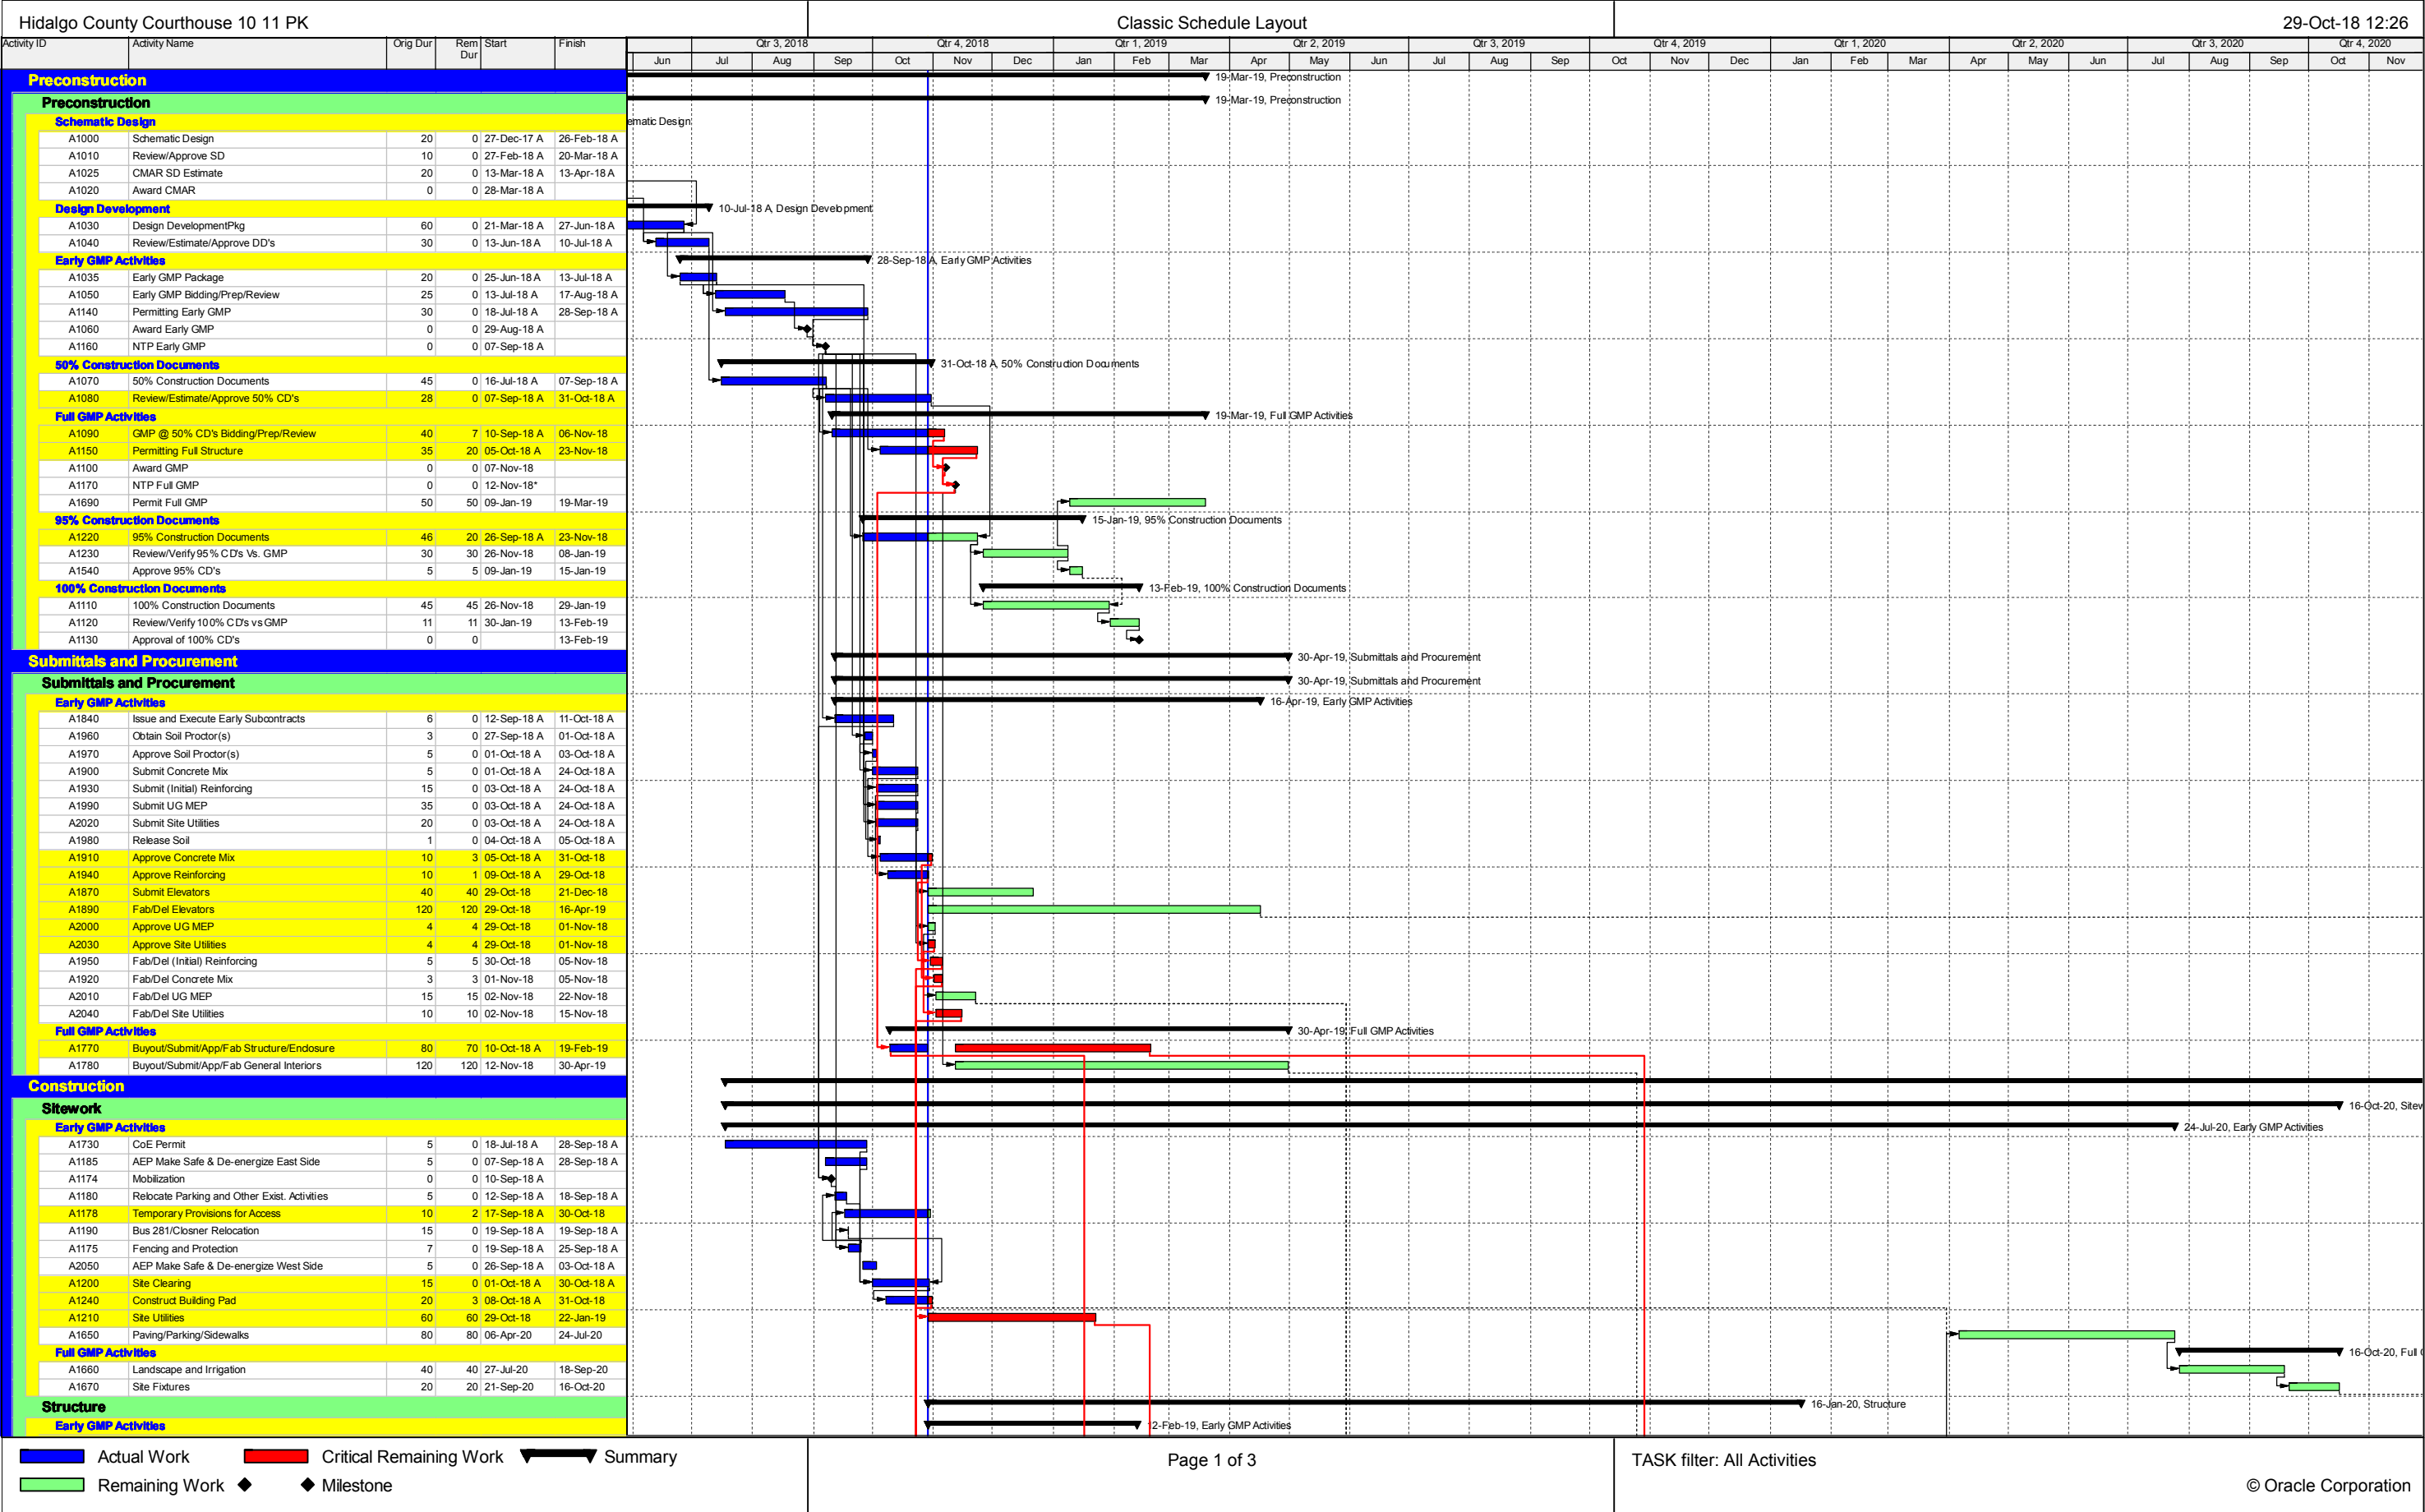

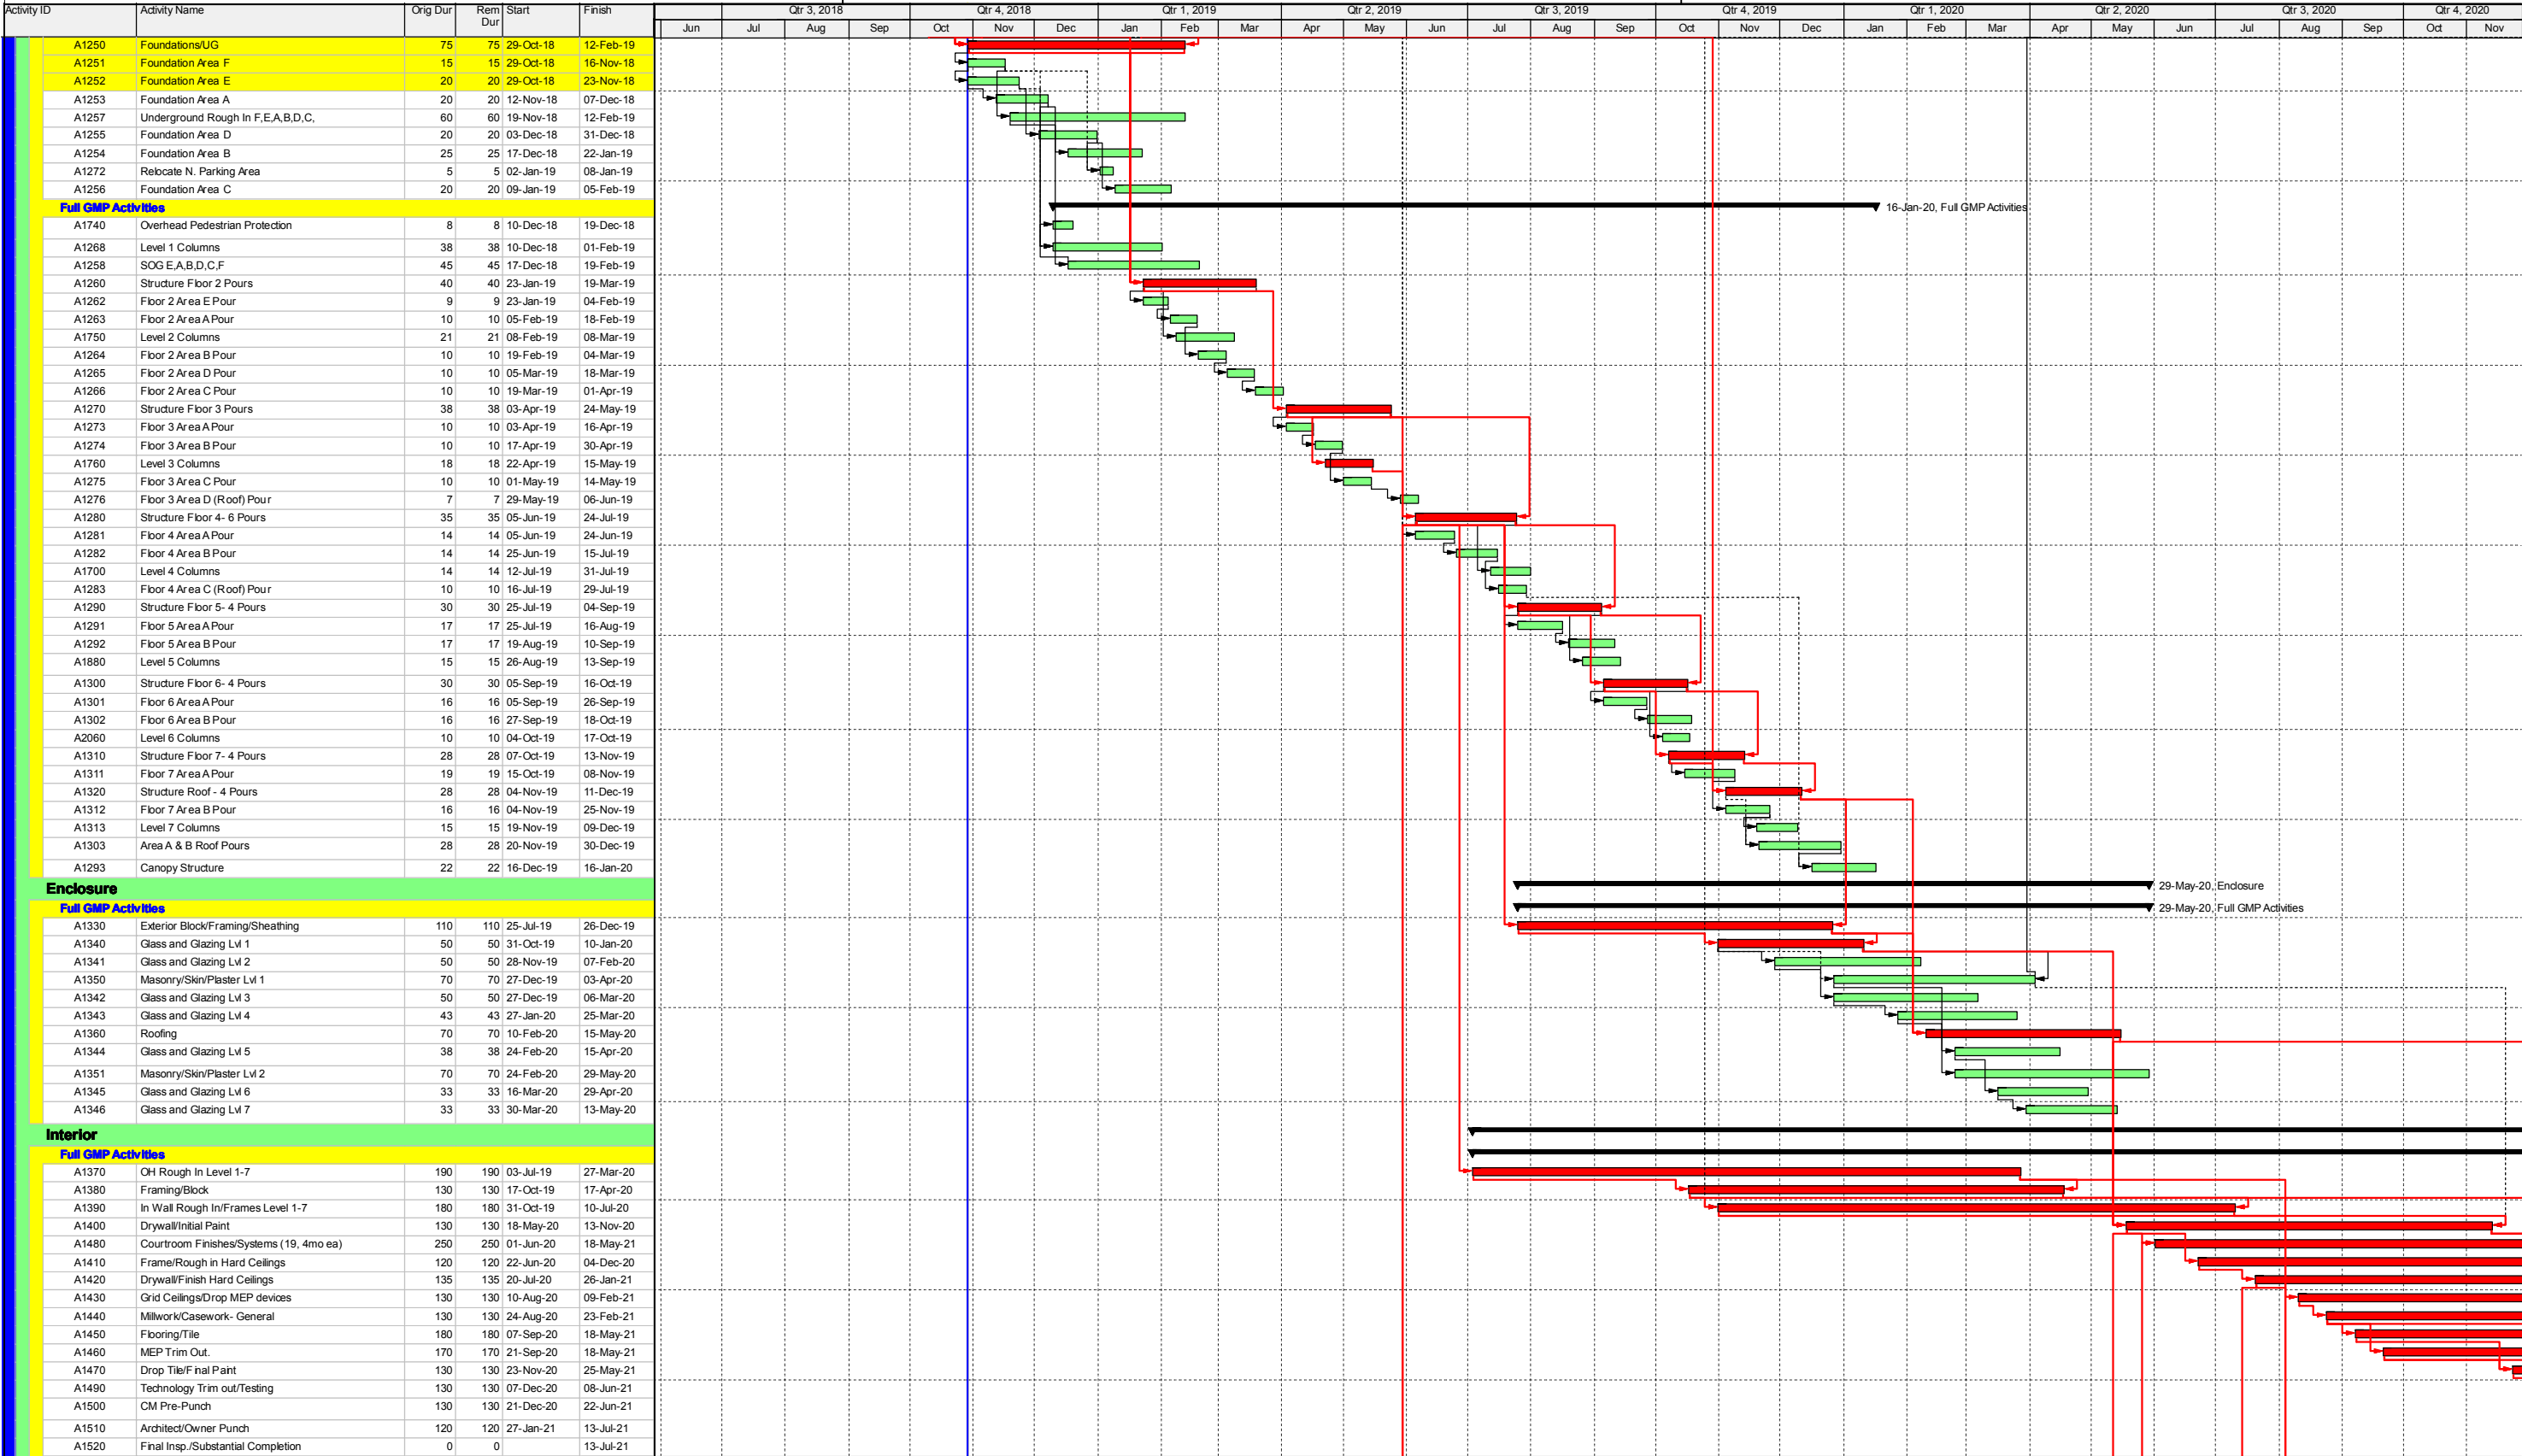

Actual Work Critical Remaining Work Summary
Remaining Work Milestone

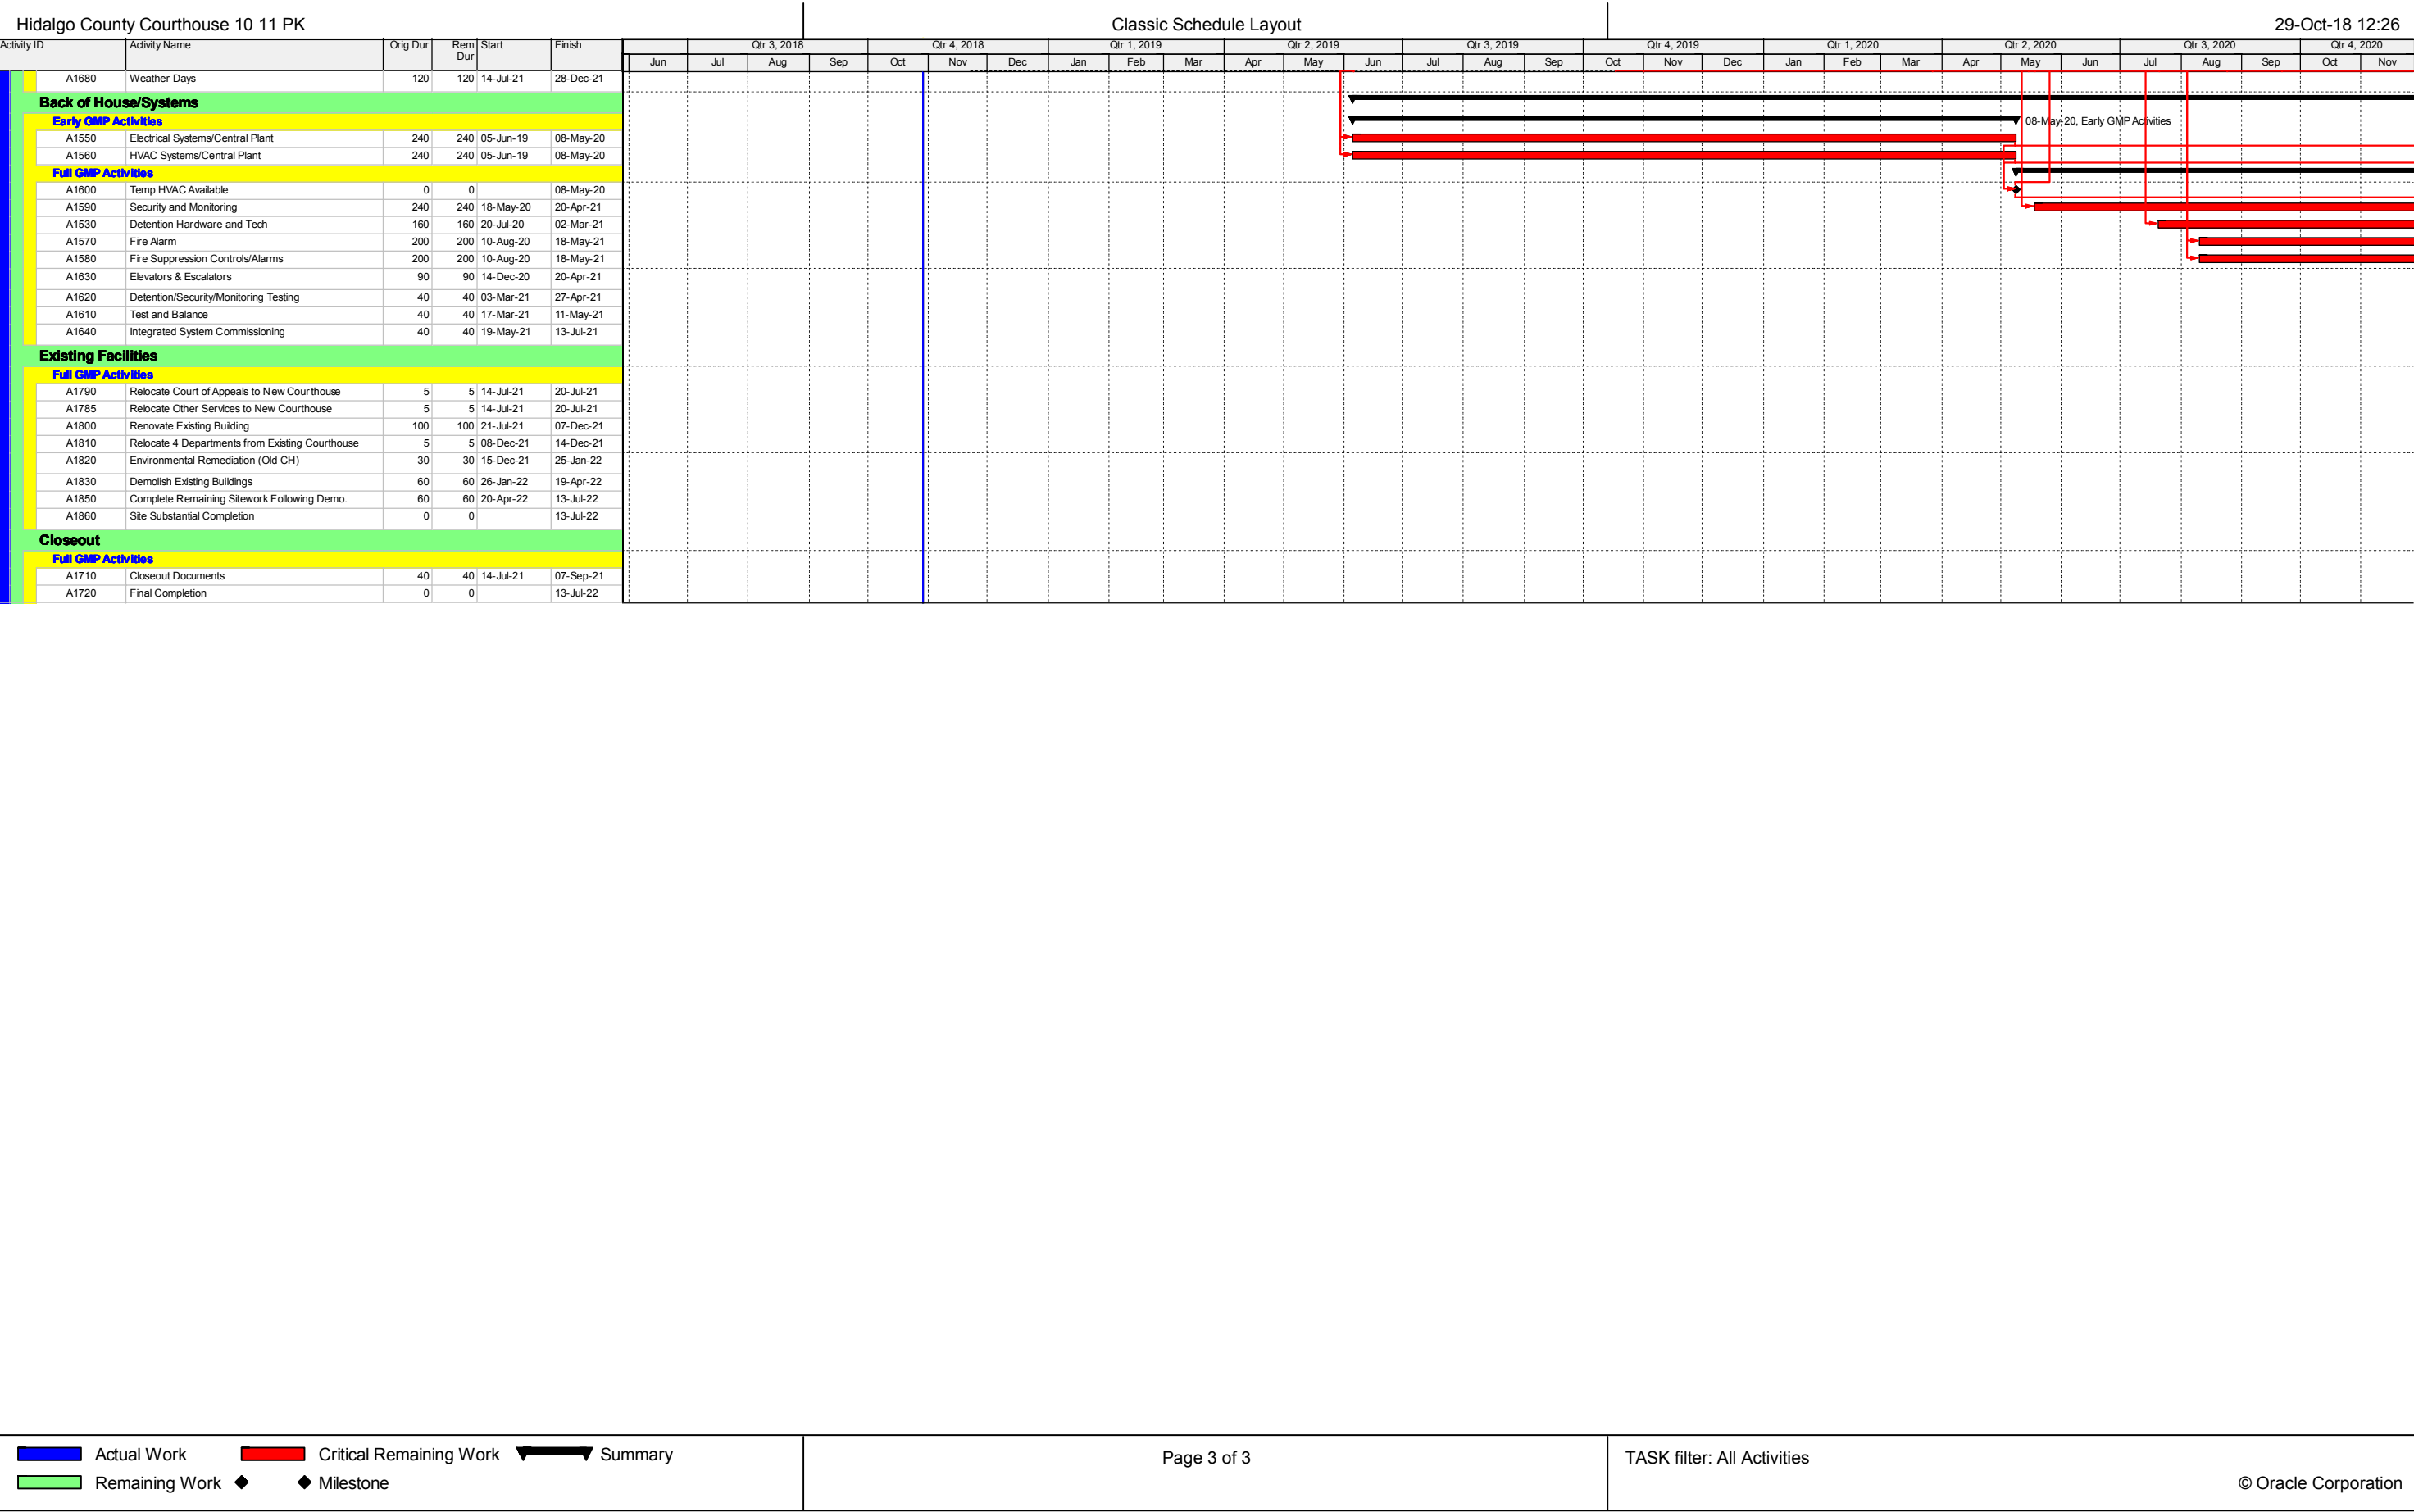

Hidalgo County Courthouse Exhibit D
- 50% GMP Drawing and Spec List

Hidalgo County Court House Drawings Log								
Drawing #	Drawing Name	Original	Current	POST-ESP	ADDENDUM 1	ADDENDUM 2	ADDENDUM 3	ADDEN #1 @100%
G-003	SHEET INDEX	9/4/2018	9/4/2018					
G-005	PROJECT SUMMARY	9/4/2018	9/4/2018					
G-101	LEVEL ONE - LIFE SAFETY	9/4/2018	9/4/2018					
G-101F	CENTRAL UTILITY - LIFE SAFETY	9/4/2018	9/4/2018					
G-102	LEVEL TWO - LIFE SAFETY	9/4/2018	9/4/2018					
G-103	LEVEL THREE - LIFE SAFETY	9/4/2018	9/4/2018					
G-104	LEVEL FOUR - LIFE SAFETY	9/4/2018	9/4/2018					
G-105	LEVEL FIVE - LIFE SAFETY	9/4/2018	9/4/2018					
G-106	LEVEL SIX - LIFE SAFETY	9/4/2018	9/4/2018					
G-107	LEVEL SEVEN - LIFE SAFETY	9/4/2018	9/4/2018					
G-801	SECURITY PLAN - LEVEL 1	9/4/2018	9/4/2018					
G-802	SECURITY PLAN - LEVEL 2	9/4/2018	9/4/2018					
G-803	SECURITY PLAN - LEVEL 3	9/4/2018	9/4/2018					
G-804	SECURITY PLAN - LEVEL 4	9/4/2018	9/4/2018					
G-805	SECURITY PLAN - LEVEL 5	9/4/2018	9/4/2018					
G-806	SECURITY PLAN - LEVEL 6	9/4/2018	9/4/2018					
G-807	SECURITY PLAN - LEVEL 7	9/4/2018	9/4/2018					
CIVIL DRAWINGS								
C-100	SITE ORIENTATION PLAN	9/4/2018	9/4/2018					
C-101.1	EXISTING CONDITIONS PLAN AREA A	9/4/2018	9/4/2018					
C-101.2	EXISTING CONDITIONS PLAN AREA B	9/4/2018	9/4/2018					
C-102	TREE PRESERVATION PLAN	9/4/2018	9/4/2018					
C-103.1	SITE DEMOTION PLAN AREA A	9/4/2018	9/4/2018					
C-103.2	SITE DEMOTION PLAN AREA B	9/4/2018	9/4/2018					
C-104	EROSION CONTROL PLAN	9/4/2018	9/4/2018					
C-105.1	HORIZONTAL CONTROL PLAN AREA A	9/4/2018	9/4/2018					
C-105.2	HORIZONTAL CONTROL PLAN AREA B	9/4/2018	9/4/2018					
C-106.1	SITE GRADING PLAN AREA A	9/4/2018	9/4/2018					
C-106.2	SITE GRADING PLAN AREA B	9/4/2018	9/4/2018					
C-107.1	SITE PAVEMENTS PLAN AREA A	9/4/2018	9/4/2018					
C-107.2	SITE PAVEMENTS PLAN AREA B	9/4/2018	9/4/2018					
C-108.1	EXISTING DRAINAGE AREA MAP	9/4/2018	9/4/2018					
C-108.2	ULTIMATE DRAINAGE AREA MAP	9/4/2018	9/4/2018					
C-108.3	STORM SEWER PLAN	9/4/2018	9/4/2018					
C-109.1	WATER PLAN	9/4/2018	9/4/2018					
C-109.2	SANITARY SEWER PLAN	9/4/2018	9/4/2018					
C-501	SITE DETAILS	9/4/2018	9/4/2018					
C-502	SITE DETAILS	9/4/2018	9/4/2018					
C-503	EROSION CONTROL DETAILS	9/4/2018	9/4/2018					
STRUCTURAL DRAWINGS								
G-004B	SHEET INDEX	9/4/2018	9/4/2018					
S-000	STRUCTURAL COVER SHEET	9/4/2018	9/4/2018					
S-001	GENERAL NOTES	9/4/2018	9/4/2018					
S-002	GENERAL NOTES	9/4/2018	8/2/2018			8/2/2018		
S-003	SPECIAL INSPECTION	9/4/2018	9/4/2018	9/4/2018				
S-004	SYMBOLS & ANNOTATIONS	9/4/2018	9/4/2018					
S-005	TYPICAL CONCRETE DETAILS	9/4/2018	9/4/2018	9/4/2018				
S-006	TYPICAL CONCRETE DETAILS	9/4/2018	9/4/2018	9/4/2018		8/2/2018		
S-007	TYPICAL CONCRETE DETAILS	9/4/2018		9/4/2018				
S-008	TYPICAL CONCRETE DETAILS	9/4/2018		9/4/2018				
S-009	TYPICAL CONCRETE DETAILS	9/4/2018	9/4/2018					
S-010	TYPICAL CONCRETE DETAILS	9/4/2018	9/4/2018					
S-011	TYPICAL CONCRETE DETAILS	9/4/2018	9/4/2018					
S-012	TYPICAL STRUCTURAL STEEL DETAILS	9/4/2018	9/4/2018					

KEY: Red Items have date discrepancies
from Early Site Package to Site Package 2.

S-013	TYPICAL STRUCTURAL STEEL DETAILS	9/4/2018	9/4/2018					
S-014	TYPICAL PRE-ENGINEERED STEEL CONNECTIONS DETAILS	9/4/2018	9/4/2018					
S-015	WIND LOAD PLAN & ELEVATIONS	9/4/2018	10/4/2018					X
S-016	CUP-WIND LOAD PLAN & ELEVATION	9/4/2018	10/4/2018					X
S-017	LIVE LOAD PLAN - LEVEL 1	9/4/2018	9/4/2018					
S-018	LIVE LOAD PLAN - LEVEL 2	9/4/2018	9/4/2018					
S-019	LIVE LOAD PLAN - LEVEL 3	9/4/2018	9/4/2018					
S-020	LIVE LOAD PLAN - LEVEL 4	9/4/2018	9/4/2018					
S-021	LIVE LOAD PLAN - LEVEL 5-8	9/4/2018	9/4/2018					
S-022	LIVE LOAD PLANS - LEVEL 9 & CUP	9/4/2018	9/4/2018					
S-100	COMPOSITE DEEP FOUNDATION PLAN - LEVEL 0	9/4/2018	9/4/2018	9/4/2018				
S-100A	PARTIAL DEEP FOUNDATION PLAN - LEVEL 0 AREA A	9/4/2018	9/4/2018	9/4/2018	7/19/2018	8/2/2018		
S-100B	PARTIAL DEEP FOUNDATION PLAN - LEVEL 0 AREA B	9/4/2018	9/4/2018	9/4/2018		8/2/2018		
S-100C	PARTIAL DEEP FOUNDATION PLAN - LEVEL 0 AREA C	9/4/2018	8/2/2018			8/2/2018		
S-100D	PARTIAL DEEP FOUNDATION PLAN - LEVEL 0 AREA D	9/4/2018	8/2/2018			8/2/2018		
S-100E	PARTIAL DEEP FOUNDATION PLAN - LEVEL 0 AREA E	9/4/2018	9/4/2018	9/4/2018		8/2/2018		
S-101	COMPOSITE FOUNDATION PLAN - LEVEL 1	9/4/2018	9/4/2018	9/4/2018				
S-101A	PARTIAL FOUNDATION PLAN - LEVEL 1 AREA A	9/4/2018	9/4/2018	9/4/2018	7/19/2018	8/2/2018		
S-101B	PARTIAL FOUNDATION PLAN - LEVEL 1 AREA B	9/4/2018	9/4/2018	9/4/2018		8/2/2018		
S-101C	PARTIAL FOUNDATION PLAN - LEVEL 1 AREA C	9/4/2018	9/4/2018	9/4/2018		8/2/2018		
S-101D	PARTIAL FOUNDATION PLAN - LEVEL 1 AREA D	9/4/2018	9/4/2018	9/4/2018		8/2/2018		
S-101E	PARTIAL FOUNDATION PLAN - LEVEL 1 AREA E	9/4/2018	9/4/2018	9/4/2018		8/2/2018		
S-101F	CUP FOUNDATION PLAN - AREA F	9/4/2018	9/4/2018	9/4/2018		8/2/2018		
S-101G	SECURITY FENCE FOUNDATION PLAN	9/4/2018	9/4/2018	9/4/2018		8/2/2018		
S-102	COMPOSITE FRAMING PLAN - LEVEL 2	9/4/2018	9/4/2018					
S-102A	PARTIAL FRAMING PLAN - LEVEL 2 AREA A	9/4/2018	9/4/2018					
S-102B	PARTIAL FRAMING PLAN - LEVEL 2 AREA B	9/4/2018	9/4/2018					
S-102C	PARTIAL FRAMING PLAN - LEVEL 2 AREA C	9/4/2018	9/4/2018					
S-102D	PARTIAL FRAMING PLAN - LEVEL 2 AREA D	9/4/2018	9/4/2018					
S-102E	PARTIAL FRAMING PLAN - LEVEL 2 AREA E	9/4/2018	9/4/2018					
S-102F	CUP FRAMING PLAN - AREA F	9/4/2018	9/4/2018					
S-103	COMPOSITE FRAMING PLAN - LEVEL 3	9/4/2018	9/4/2018					
S-103A	PARTIAL FRAMING PLAN - LEVEL 3 AREA A	9/4/2018	9/4/2018					
S-103B	PARTIAL FRAMING PLAN - LEVEL 3 AREA B	9/4/2018	9/4/2018					
S-103C	PARTIAL FRAMING PLAN - LEVEL 3 AREA C	9/4/2018	9/4/2018					
S-103D	PARTIAL FRAMING PLAN - LEVEL 3 AREA D	9/4/2018	9/4/2018					
S-103E	PARTIAL FRAMING PLAN - LEVEL 3 AREA E	9/4/2018	9/4/2018					
S-104	COMPOSITE FRAMING PLAN - LEVEL 4	9/4/2018	9/4/2018					
S-104A	PARTIAL FRAMING PLAN - LEVEL 4 AREA A	9/4/2018	9/4/2018					
S-104B	PARTIAL FRAMING PLAN - LEVEL 4 AREA B	9/4/2018	9/4/2018					
S-104C	PARTIAL FRAMING PLAN - LEVEL 4 AREA C	9/4/2018	9/4/2018					
S-104D	PARTIAL FRAMING PLAN - LEVEL 4 AREA D	9/4/2018	9/4/2018					
S-105	COMPOSITE FRAMING PLAN - LEVEL 5	9/4/2018	9/4/2018					
S-105A	PARTIAL FRAMING PLAN - LEVEL 5 AREA A	9/4/2018	9/4/2018					
S-105B	PARTIAL FRAMING PLAN - LEVEL 5 AREA B	9/4/2018	9/4/2018					
S-106	COMPOSITE FRAMING PLAN - LEVEL 6	9/4/2018	9/4/2018					
S-106A	PARTIAL FRAMING PLAN - LEVEL 6 AREA A	9/4/2018	9/4/2018					
S-106B	PARTIAL FRAMING PLAN - LEVEL 6 AREA B	9/4/2018	9/4/2018					
S-107	COMPOSITE FRAMING PLAN - LEVEL 7	9/4/2018	9/4/2018					
S-107A	PARTIAL FRAMING PLAN - LEVEL 7 AREA A	9/4/2018	9/4/2018					
S-107B	PARTIAL FRAMING PLAN - LEVEL 7 AREA B	9/4/2018	9/4/2018					
S-108	COMPOSITE ROOF FRAMING PLAN - LEVEL 8	9/4/2018	9/4/2018					
S-108A	PARTIAL ROOFING FRAMING PLAN - LEVEL 8 AREA A	9/4/2018	9/4/2018					
S-108B	PARTIAL ROOFING FRAMING PLAN - LEVEL 8 AREA B	9/4/2018	9/4/2018					
S-109	COMPOSITE HIGH ROOF FRAMING PLAN - LEVEL 9	9/4/2018	9/4/2018					
S-109A	PARTIAL HIGH ROOF FRAMING PLAN - LEVEL 9 AREA A	9/4/2018	9/4/2018					
S-109B	PARTIAL HIGH ROOF FRAMING PLAN - LEVEL 9 AREA B	9/4/2018	9/4/2018					
S-201	EXTERIOR FRAMING ELEVATION	9/4/2018	9/4/2018					
S-301	BUILDING SECTIONS	9/4/2018	9/4/2018					

S-302	BUILDING SECTIONS	9/4/2018	9/4/2018					
S-401	ENLARGED CONCRETE SHEAR WALL PLAN	9/4/2018	9/4/2018					
S-402	CONCRETE SHEAR WALL ELEVATIONS	9/4/2018	9/4/2018					
S-403	CONCRETE SHEAR WALL ELEVATIONS	9/4/2018	9/4/2018					
S-404	CONCRETE SHEAR WALL ELEVATIONS	9/4/2018	9/4/2018					
S-405	CONCRETE SHEAR WALL ELEVATIONS	9/4/2018	9/4/2018					
S-406	CONCRETE SHEAR WALL ELEVATIONS	9/4/2018	9/4/2018					
S-407	CONCRETE SHEAR WALL ELEVATIONS	9/4/2018	9/4/2018					
S-501	FOUNDATION DETAILS	9/4/2018	9/4/2018	9/4/2018		8/2/2018		
S-502	FOUNDATION DETAILS	9/4/2018	9/4/2018	9/4/2018		8/2/2018		
S-503	FOUNDATION DETAILS	9/4/2018	9/4/2018	9/4/2018		8/2/2018		
S-504	FOUNDATION DETAILS	9/4/2018	9/4/2018	9/4/2018		8/2/2018		
S-505	FOUNDATION DETAILS	9/4/2018	9/4/2018	9/4/2018		8/2/2018		
S-506	FOUNDATION DETAILS	9/4/2018	9/4/2018	9/4/2018				
S-507	FOUNDATION DETAILS	9/4/2018	9/4/2018	9/4/2018				
S-508	FRAMING DETAILS	9/4/2018	9/4/2018					
S-509	FRAMING DETAILS	9/4/2018	9/4/2018					
S-600	CONCRETE BAR PLACEMENT DIAGRAM & TYPICAL DETAILS	9/4/2018	9/4/2018					
S-601	DRILLED PIER SCHEDULES	9/4/2018	9/4/2018	9/4/2018		8/2/2018		
S-602	CONCRETE COLUMNS SCHEDULES	9/4/2018	9/4/2018	9/4/2018				
S-603	CONCRETE COLUMNS & WALL SCHEDULES	9/4/2018	9/4/2018	9/4/2018				
S-604	CONCRETE GRADE BEAM SCHEDULES	9/4/2018	9/4/2018	9/4/2018				
S-605	CONCRETE GRADE BEAM SCHEDULES	9/4/2018	9/4/2018					
S-606	CONCRETE BEAM SCHEDULES - LEVEL 2	9/4/2018	9/4/2018					
S-607	CONCRETE BEAM SCHEDULES - LEVEL 2	9/4/2018	9/4/2018					
S-608	CONCRETE BEAM SCHEDULES - LEVEL 3	9/4/2018	9/4/2018					
S-609	CONCRETE BEAM SCHEDULES - LEVEL 3 & 4	9/4/2018	9/4/2018					
S-610	CONCRETE BEAM SCHEDULES - LEVEL 4 & 5	9/4/2018	9/4/2018					
S-611	CONCRETE BEAM SCHEDULES - LEVEL 5 & 6	9/4/2018	9/4/2018					
S-612	CONCRETE BEAM SCHEDULES - LEVEL 6 & 7	9/4/2018	9/4/2018					
S-613	CONCRETE BEAM SCHEDULES - LEVEL 7 & 8	9/4/2018	9/4/2018					
S-614	CONCRETE BEAM SCHEDULES - LEVEL 8	9/4/2018	9/4/2018					
S-615	CONCRETE GIRDER SCHEDULES - LEVEL 2	9/4/2018	9/4/2018					
S-616	CONCRETE GIRDER SCHEDULES - LEVEL 2	9/4/2018	9/4/2018					
S-617	CONCRETE GIRDER SCHEDULES - LEVEL 3	9/4/2018	9/4/2018					
S-618	CONCRETE GIRDER SCHEDULES - LEVEL 3	9/4/2018	9/4/2018					
S-619	CONCRETE GIRDER SCHEDULES - LEVEL 4	9/4/2018	9/4/2018					
S-620	CONCRETE GIRDER SCHEDULES - LEVELS 4 & 5	9/4/2018	9/4/2018					
S-621	CONCRETE GIRDER SCHEDULES - LEVELS 5 & 6	9/4/2018	9/4/2018					
S-622	CONCRETE GIRDER SCHEDULES - LEVELS 6, 7 & 8	9/4/2018	9/4/2018					
S-623	CONCRETE GIRDER SCHEDULES - LEVEL 8	9/4/2018	9/4/2018					
SK-02	STAIR NO 6 - PARTIAL FRAMING PLAN - LEVEL 2		10/4/2018					10/4/2018
SK-03	STAIR NO 7 - PARTIAL FRAMING PLAN - LEVEL 2		10/4/2018					10/4/2018
SK-04	PARTIAL FOUNDATION PLAN - LEVEL 1 AREA D		10/4/2018					10/4/2018
SK-05	PARTIAL FOUNDATION PLAN - LEVEL 1 AREA B		10/4/2018					10/4/2018
LANDSCAPE DRAWINGS								
L-101.1	SITE LANDSCAPE PLAN AREA A	9/4/2018	9/4/2018					
L-101.2	SITE LANDSCAPE PLAN AREA B	9/4/2018	9/4/2018					
ARCHITECTURAL DRAWINGS								
A-101	OVERALL LEVEL 1 PLAN	9/4/2018	9/4/2018					
A-101.1	FAÇADE PLAN - LEVEL 1 - OVERALL	9/4/2018	9/4/2018					
A-101A	LEVEL 1 PLAN AREA A	9/4/2018	9/4/2018					
A-101B	LEVEL 1 PLAN AREA B	9/4/2018	9/4/2018					
A-101C	LEVEL 1 PLAN AREA C	9/4/2018	9/4/2018					
A-101D	LEVEL 1 PLAN AREA D	9/4/2018	9/4/2018					
A-101E	LEVEL 1 PLAN AREA E	9/4/2018	9/4/2018					
A-101F	LEVEL 1 PLAN AREA F	9/4/2018	9/4/2018					
A-101G	LEVEL 1 PLAN AREA G	9/4/2018	9/4/2018					
A-102	OVERALL LEVEL 2 PLAN	9/4/2018	9/4/2018					

A-102.1	FAÇADE PLAN - LEVEL 2 - OVERALL	9/4/2018	9/4/2018					
A-102A	LEVEL 2 PLAN AREA A	9/4/2018	9/4/2018					
A-102B	LEVEL 2 PLAN AREA B	9/4/2018	9/4/2018					
A-102C	LEVEL 2 PLAN AREA C	9/4/2018	9/4/2018					
A-102D	LEVEL 2 PLAN AREA D	9/4/2018	9/4/2018					
A-102E	LEVEL 2 PLAN AREA E	9/4/2018	9/4/2018					
A-102F	ROOF PLAN - CUP	9/4/2018	9/4/2018					
A-103	OVERALL LEVEL 3 PLAN	9/4/2018	9/4/2018					
A-103.1	FAÇADE PLAN - LEVEL 3 - OVERALL	9/4/2018	9/4/2018					
A-103A	LEVEL 3 PLAN AREA A	9/4/2018	9/4/2018					
A-103B	LEVEL 3 PLAN AREA B	9/4/2018	9/4/2018					
A-103C - ALT#2	LEVEL 3 PLAN AREA C - ALT. #2	9/4/2018	9/4/2018					
A-103D	LEVEL 3 PLAN AREA D ROOF	9/4/2018	9/4/2018					
A-103E	THIRD LEVEL PLAN - AREA ROOF	9/4/2018	9/4/2018					
A-103E - ALT #4	THIRD LEVEL PLAN - AREA E ROOF ALT. #4	9/4/2018	9/4/2018					
A-104	OVERALL LEVEL 4 PLAN	9/4/2018	9/4/2018					
A-104.1	FAÇADE PLAN - LEVEL 4-LEVEL 7 OVERALL	9/4/2018	9/4/2018					
A-104A	LEVEL 4 PLAN AREA A	9/4/2018	9/4/2018					
A-104B	LEVEL 4 PLAN AREA B	9/4/2018	9/4/2018					
A-104C	FOURTH LEVEL PLAN - AREA C ROOF	9/4/2018	9/4/2018					
A-104D	FOURTH LEVEL PLAN - AREA D ROOF	9/4/2018	9/4/2018					
A-105	OVERALL LEVEL 5 PLAN	9/4/2018	9/4/2018					
A-105A	LEVEL 5 PLAN AREA A	9/4/2018	9/4/2018					
A-105B	LEVEL 5 PLAN AREA B	9/4/2018	9/4/2018					
A-106	OVERALL LEVEL 6 PLAN	9/4/2018	9/4/2018					
A-106A	LEVEL 6 PLAN AREA A	9/4/2018	9/4/2018					
A-106B	LEVEL 6 PLAN AREA B	9/4/2018	9/4/2018					
A-107	OVERALL LEVEL 7 PLAN	9/4/2018	9/4/2018					
A-107A	LEVEL 7 PLAN AREA A	9/4/2018	9/4/2018					
A-107B	LEVEL 7 PLAN AREA B	9/4/2018	9/4/2018					
A-108	EIGHTH LEVEL PLAN - OVERALL ROOF	9/4/2018	9/4/2018					
A-108A	EIGHTH LEVEL PLAN - AREA A ROOF	9/4/2018	9/4/2018					
A-108B	EIGHTH LEVEL PLAN - AREA B ROOF	9/4/2018	9/4/2018					
A-108 - ALT #14	EIGHTH LEVEL PLAN - ROOF ALTERNATE	9/4/2018	9/4/2018					
AC-101	REFLECTED CEILING PLAN - LEVEL 1 OVERALL	9/4/2018	9/4/2018					
AC-102	REFLECTED CEILING PLAN - LEVEL 2 OVERALL	9/4/2018	9/4/2018					
AC-103	REFLECTED CEILING PLAN - LEVEL 3 OVERALL	9/4/2018	9/4/2018					
AC-104	REFLECTED CEILING PLAN - LEVEL 4 OVERALL	9/4/2018	9/4/2018					
AC-105	REFLECTED CEILING PLAN - LEVEL 5 OVERALL	9/4/2018	9/4/2018					
AC-106	REFLECTED CEILING PLAN - LEVEL 6 OVERALL	9/4/2018	9/4/2018					
AC-107	REFLECTED CEILING PLAN - LEVEL 7 OVERALL	9/4/2018	9/4/2018					
AC-201	RCP - LEVEL 1 SPECIALIZED AREA A&B	9/4/2018	9/4/2018					
AC-202	RCP - LEVEL 2 SPECIALIZED AREA A&B	9/4/2018	9/4/2018					
AC-203	RCP - LEVEL 3 SPECIALIZED AREA A&B	9/4/2018	9/4/2018					
A-201	OVERALL EXTERIOR ELEVATION	9/4/2018	9/4/2018					
A-202	OVERALL EXTERIOR ELEVATION	9/4/2018	9/4/2018					
A-203	OVERALL EXTERIOR ELEVATION	9/4/2018	9/4/2018					
A-251	INTERIOR ELEVATION	9/4/2018	9/19/2018		9/19/2018			
A-252	INTERIOR ELEVATION	9/4/2018	9/4/2018					
A-301	SECTIONS - BUILDING	9/4/2018	9/4/2018					
A-302	SECTIONS - BUILDING	9/4/2018	9/4/2018					
A-303	SECTIONS - BUILDING	9/4/2018	9/4/2018					
A-304	SECTIONS - BUILDING & WALL - CUP	9/4/2018	9/4/2018					
A-310	WALL SECTIONS	9/4/2018	9/4/2018					
A-311	WALL SECTIONS	9/4/2018	9/4/2018					
A-312	WALL SECTIONS	9/4/2018	9/4/2018					
A-313	WALL SECTIONS	9/4/2018	9/4/2018					
A-401	ENLARGED TOILET ROOM PLANS & ELEVATIONS	9/4/2018	9/4/2018					
A-402	ENLARGED TOILET ROOM PLANS & ELEVATIONS	9/4/2018	9/4/2018					

A-403	ENLARGED TOILET ROOM PLANS & ELEVATIONS	9/4/2018	9/4/2018					
A-404	ENLARGED TOILET ROOM PLANS & ELEVATIONS	9/4/2018	9/4/2018					
A-405	ENLARGED TOILET ROOM PLANS & ELEVATIONS	9/4/2018	9/4/2018					
A-406	ENLARGED TOILET ROOM PLANS & ELEVATIONS & LOCKER ELEVATIONS	9/4/2018	9/4/2018					
A-407	ENLARGED DETENTION AREA PLANS & ELEVATIONS - DETENTION	9/4/2018	9/4/2018					
A-411	TYP - COURTROOM FLOOR PLAN AND CEILING PLAN	9/4/2018	9/4/2018					
A-412	ENLARGED HIGH-PROFILE COURTROOM - ALT#12	9/4/2018	9/4/2018					
A-416	ENLARGED PLAN EXTERNAL STAIR & RAMPS	9/4/2018	9/4/2018					
A-417	ENLARGED PLAN EXTERNAL STAIR & RAMPS	9/4/2018	9/4/2018					
A-418	ENLARGED PLAN EXTERNAL STAIR & RAMPS	9/4/2018	9/4/2018					
A-421	STAIR NO.1 ENLARGED STAIR PLANS AND SECTIONS	9/4/2018	9/4/2018					
A-422	STAIR NO.2 ENLARGED STAIR PLANS AND SECTIONS	9/4/2018	9/4/2018					
A-423	STAIR NO.3 ENLARGED STAIR PLANS AND SECTIONS	9/4/2018	9/4/2018					
A-424	STAIR NO.4 & NO.6 ENLARGED STAIR PLANS AND SECTIONS	9/4/2018	9/4/2018					
A-425	STAIR NO.5 & NO.7 ENLARGED STAIR PLANS AND SECTIONS	9/4/2018	9/4/2018					
A-426	STAIR & HANDRAIL DETAILS	9/4/2018	9/4/2018					
A-430	ENLARGED ELEVATED PARKING	9/4/2018	9/4/2018					
A-431	ENLARGED MACHINE ROOM & FIRE SERVICE LOBBY	9/4/2018	9/4/2018					
A-501	EXTERIOR SECTIONS DETAILS	9/4/2018	9/4/2018					
A-502	EXTERIOR SECTIONS DETAILS	9/4/2018	9/4/2018					
A-503	EXTERIOR SECTIONS DETAILS	9/4/2018	9/4/2018					
A-504	DETAILS - EXTERIOR	9/4/2018	9/4/2018					
A-510	EXTERIOR PLAN DETAILS	9/4/2018	9/4/2018					
A-511	EXTERIOR PLAN DETAILS	9/4/2018	9/4/2018					
A-514	EXTERIOR DETAILS	9/4/2018	9/4/2018					
A-551	DETAILS - INTERIOR	9/4/2018	9/4/2018					
A-552	DETAILS - INTERIOR	9/4/2018	9/4/2018					
A-553	DETAILS - INTERIOR	9/4/2018	9/4/2018					
A-554	DETAILS - INTERIOR	9/4/2018	9/4/2018					
A-555	DETAILS - INTERIOR	9/4/2018	9/4/2018					
A-556	DETAILS - INTERIOR	9/4/2018	9/4/2018					
A-561	MILLWORK ELEVATIONS	9/4/2018	9/4/2018					
A-562	MILLWORK ELEVATIONS	9/4/2018	9/4/2018					
A-563	MILLWORK ELEVATIONS	9/4/2018	9/4/2018					
A-564	MILLWORK ELEVATIONS	9/4/2018	9/4/2018					
A-565	MILLWORK ELEVATIONS	9/4/2018	9/4/2018					
A-566	MILLWORK ELEVATIONS	9/4/2018	9/4/2018					
A-567	MILLWORK ELEVATIONS	9/4/2018	9/4/2018					
A-568	MILLWORK SECTIONS	9/4/2018	9/4/2018					
A-569	MILLWORK SECTIONS	9/4/2018	9/4/2018					
A-570	MILLWORK SECTIONS	9/4/2018	9/4/2018					
A-571	MILLWORK SECTIONS	9/4/2018	9/4/2018					
A-572	MILLWORK SECTIONS	9/4/2018	9/4/2018					
A-580	ESCALATOR RAILING	9/4/2018	9/4/2018					
A-601	DOOR SCHEDULE - LEVEL 1	9/4/2018	9/4/2018					
A-602	DOOR SCHEDULE - LEVEL 1	9/4/2018	9/4/2018					
A-603	DOOR SCHEDULE - LEVEL 2	9/4/2018	9/4/2018					
A-604	DOOR SCHEDULE - LEVEL 2	9/4/2018	9/4/2018					
A-605	DOOR SCHEDULE - LEVEL 3	9/4/2018	9/4/2018					
A-606	DOOR SCHEDULE - LEVEL 3	9/4/2018	9/4/2018					
A-607	DOOR SCHEDULE - LEVEL 4	9/4/2018	9/4/2018					
A-608	DOOR SCHEDULE - LEVEL 5	9/4/2018	9/4/2018					
A-609	DOOR SCHEDULE - LEVEL 6	9/4/2018	9/4/2018					
A-610	DOOR SCHEDULE - LEVEL 7	9/4/2018	9/4/2018					
A-611	OPENING SCHEDULE	9/4/2018	9/4/2018					
A-620	INTERIOR PANEL AND FRAME TYPES	9/4/2018	9/4/2018					
A-621	INTERIOR FRAME TYPES	9/4/2018	9/4/2018					
A-709	EXTERIOR WALL TYPES	9/4/2018	9/4/2018					
A-710	UCW ELEVATIONS	9/4/2018	9/4/2018					

A-711	UCW ELEVATIONS	9/4/2018	9/4/2018					
A-712	UCW ELEVATIONS	9/4/2018	9/4/2018					
A-713	UCW ELEVATIONS	9/4/2018	9/4/2018					
A-714	UCW ELEVATIONS	9/4/2018	9/4/2018					
A-715	UCW ELEVATIONS	9/4/2018	9/4/2018					
A-716	UCW ELEVATIONS	9/4/2018	9/4/2018					
A-717	UCW DETAILS	9/4/2018	9/4/2018					
A-718	VISUAL MOCK UP PLAN / ELEVATIONS	9/4/2018	9/24/2018		9/24/2018			
A-719	VISUAL MOCK UP DETAILS	9/4/2018	9/24/2018		9/24/2018			
A-720	STANDARD PARITITION TYPES	9/4/2018	9/4/2018					
A-721	STANDARD PARITITION TYPES	9/4/2018	9/4/2018					
A-722	PARITITIONS HEAD DETAILS	9/4/2018	9/4/2018					
A-723	PARITITION FRAMING DETAILS	9/4/2018	9/4/2018					
A-730	TYPICAL MOUNTING HEIGHTS	9/4/2018	9/4/2018					
A-801	SECURITY DETAILS	9/4/2018	9/4/2018					
A-802	SECURITY DETAILS	9/4/2018	9/4/2018					
AG-301	EXT SIGN PLAN	9/4/2018	9/4/2018					
AG-401	EXT SIGN DETAILS PROJECT COLORS, MATERIALS & METHODS	9/4/2018	9/4/2018					
AG-402	EXT. SIGN DETAILS - SDR, INF, AC	9/4/2018	9/4/2018					
AG-403	EXT SIGN DETAILS - MID, LGO	9/4/2018	9/4/2018					
AG-501	LEVEL 1 PLAN - OVERALL - DIGITAL SIGNAGE	9/4/2018	9/4/2018					
AG-502	LEVEL 2 PLAN - OVERALL - DIGITAL SIGNAGE	9/4/2018	9/4/2018					
AG-503	LEVEL 3 PLAN - OVERALL - DIGITAL SIGNAGE	9/4/2018	9/4/2018					
AG-504	LEVEL 4 PLAN - OVERALL - DIGITAL SIGNAGE	9/4/2018	9/4/2018					
AG-506	LEVEL 6 PLAN - OVERALL - DIGITAL SIGNAGE	9/4/2018	9/4/2018					
AG-507	LEVEL 7 PLAN - OVERALL - DIGITAL SIGNAGE	9/4/2018	9/4/2018					
INTERIOR FINISH DRAWINGS								
I-001	INTERIOR NOTES AND FINISH LEGEND	9/4/2018	9/19/2018		9/19/2018			
I-101A	INTERIOR FINISH PLAN - LEVEL 1 AREA A	9/4/2018	9/4/2018					
I-101B	INTERIOR FINISH PLAN - LEVEL 1 AREA B	9/4/2018	9/4/2018					
I-101C	INTERIOR FINISH PLAN - LEVEL 1 AREA C	9/4/2018	9/4/2018					
I-101D	INTERIOR FINISH PLAN - LEVEL 1 AREA D	9/4/2018	9/4/2018					
I-101E	INTERIOR FINISH PLAN - LEVEL 1 AREA E	9/4/2018	9/4/2018					
I-101F	INTERIOR FINISH PLAN - LEVEL 1 AREA F	9/4/2018	9/4/2018					
I-102A	INTERIOR FINISH PLAN - LEVEL 2 AREA A	9/4/2018	9/4/2018					
I-102B	INTERIOR FINISH PLAN - LEVEL 2 AREA B	9/4/2018	9/4/2018					
I-102C	INTERIOR FINISH PLAN - LEVEL 2 AREA C	9/4/2018	9/4/2018					
I-102D	INTERIOR FINISH PLAN - LEVEL 2 AREA C	9/4/2018	9/4/2018					
I-103A	INTERIOR FINISH PLAN - LEVEL 3 AREA A	9/4/2018	9/4/2018					
I-103B	INTERIOR FINISH PLAN - LEVEL 3 AREA B	9/4/2018	9/4/2018					
I-103C	INTERIOR FINISH PLAN - LEVEL 3 AREA C	9/4/2018	9/4/2018					
I-104A	INTERIOR FINISH PLAN - LEVEL 4 AREA A	9/4/2018	9/4/2018					
I-104B	INTERIOR FINISH PLAN - LEVEL 4 AREA B	9/4/2018	9/4/2018					
IN-101A	INTERIOR DESIGN PLAN - LEVEL 1 AREA A	9/4/2018	9/4/2018					
IN-101B	INTERIOR DESIGN PLAN - LEVEL 1 AREA B	9/4/2018	9/4/2018					
IN-101C	INTERIOR DESIGN PLAN - LEVEL 1 AREA C	9/4/2018	9/4/2018					
IN-101D	INTERIOR DESIGN PLAN - LEVEL 1 AREA D	9/4/2018	9/4/2018					
IN-101E	INTERIOR DESIGN PLAN - LEVEL 1 AREA E	9/4/2018	9/4/2018					
IN-101F	INTERIOR DESIGN PLAN - LEVEL 1 AREA F	9/4/2018	9/4/2018					
IN-102A	INTERIOR DESIGN PLAN - LEVEL 2 AREA A	9/4/2018	9/4/2018					
IN-102B	INTERIOR DESIGN PLAN - LEVEL 2 AREA B	9/4/2018	9/4/2018					
IN-102C	INTERIOR DESIGN PLAN - LEVEL 2 AREA C	9/4/2018	9/4/2018					
IN-102D	INTERIOR DESIGN PLAN - LEVEL 2 AREA D	9/4/2018	9/4/2018					
IN-103A	INTERIOR DESIGN PLAN - LEVEL 3 AREA A	9/4/2018	9/4/2018					
IN-103B	INTERIOR DESIGN PLAN - LEVEL 3 AREA B	9/4/2018	9/4/2018					
IN-103C	INTERIOR DESIGN PLAN - LEVEL 3 AREA C	9/4/2018	9/4/2018					
IN-104A	INTERIOR DESIGN PLAN - LEVEL 4 AREA A	9/4/2018	9/4/2018					
IN-104B	INTERIOR DESIGN PLAN - LEVEL 4 AREA B	9/4/2018	9/4/2018					
I-501	DETAILS - CEILINGS	9/4/2018	9/19/2018		9/19/2018			

FIRE PROTECTION DRAWINGS								
FA-001	FIRE ALARM LEGEND	9/4/2018	9/4/2018					
FA-101A	FIRE ALARM PLAN - LEVEL 1 - AREA A	9/4/2018	9/4/2018					
FA-101B	FIRE ALARM PLAN - LEVEL 1 - AREA B	9/4/2018	9/4/2018					
FA-101C	FIRE ALARM PLAN - LEVEL 1 - AREA C	9/4/2018	9/4/2018					
FA-101D	FIRE ALARM PLAN - LEVEL 1 - AREA D	9/4/2018	9/4/2018					
FA-101E	FIRE ALARM PLAN - LEVEL 1 - AREA E	9/4/2018	9/4/2018					
FA-101F	FIRE ALARM PLAN - LEVEL 1 - AREA F - CUP	9/4/2018	9/4/2018					
FA-102A	FIRE ALARM PLAN - LEVEL 2 - AREA A	9/4/2018	9/4/2018					
FA-102B	FIRE ALARM PLAN - LEVEL 2 - AREA B	9/4/2018	9/4/2018					
FA-102C	FIRE ALARM PLAN - LEVEL 2 - AREA C	9/4/2018	9/4/2018					
FA-102D	FIRE ALARM PLAN - LEVEL 2 - AREA D	9/4/2018	9/4/2018					
FA-102E	FIRE ALARM PLAN - LEVEL 2 - AREA E	9/4/2018	9/4/2018					
FA-103A	FIRE ALARM PLAN - LEVEL 3 - AREA A	9/4/2018	9/4/2018					
FA-103B	FIRE ALARM PLAN - LEVEL 3 - AREA B	9/4/2018	9/4/2018					
FA-103C	FIRE ALARM PLAN - LEVEL 3 - AREA C	9/4/2018	9/4/2018					
FA-104A	FIRE ALARM PLAN - LEVEL 4 - AREA A	9/4/2018	9/4/2018					
FA-104B	FIRE ALARM PLAN - LEVEL 4 - AREA B	9/4/2018	9/4/2018					
FA-105A	FIRE ALARM PLAN - LEVEL 5 - AREA A	9/4/2018	9/4/2018					
FA-105B	FIRE ALARM PLAN - LEVEL 5 - AREA B	9/4/2018	9/4/2018					
FA-106A	FIRE ALARM PLAN - LEVEL 6 - AREA A	9/4/2018	9/4/2018					
FA-106B	FIRE ALARM PLAN - LEVEL 6 - AREA B	9/4/2018	9/4/2018					
FA-107A	FIRE ALARM PLAN - LEVEL 7 - AREA A	9/4/2018	9/4/2018					
FA-107B	FIRE ALARM PLAN - LEVEL 7 - AREA B	9/4/2018	9/4/2018					
FA-501	FIRE ALARM DETAILS	9/4/2018	9/4/2018					
FP-001	AUTOMATIC SPRINKLER SYSTEM PERFORMANCE	9/4/2018	9/4/2018					
FP-101A	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 1 - AREA A	9/4/2018	9/4/2018					
FP-101B	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 1 - AREA B	9/4/2018	9/4/2018					
FP-101C	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 1 - AREA C	9/4/2018	9/4/2018					
FP-101D	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 1 - AREA D	9/4/2018	9/4/2018					
FP-101E	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 1 - AREA E	9/4/2018	9/4/2018					
FP-101F	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 1 - AREA F - CUP	9/4/2018	9/4/2018					
FP-102A	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 2 - AREA A	9/4/2018	9/4/2018					
FP-102B	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 2 - AREA B	9/4/2018	9/4/2018					
FP-102C	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 2 - AREA C	9/4/2018	9/4/2018					
FP-102D	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 2 - AREA D	9/4/2018	9/4/2018					
FP-102E	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 2 - AREA E	9/4/2018	9/4/2018					
FP-103A	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 3 - AREA A	9/4/2018	9/4/2018					
FP-103B	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 3 - AREA B	9/4/2018	9/4/2018					
FP-103C	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 3 - AREA C	9/4/2018	9/4/2018					
FP-104A	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 4 - AREA A	9/4/2018	9/4/2018					
FP-104B	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 4 - AREA B	9/4/2018	9/4/2018					
FP-105A	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 5 - AREA A	9/4/2018	9/4/2018					
FP-105B	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 5 - AREA B	9/4/2018	9/4/2018					
FP-106A	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 6 - AREA A	9/4/2018	9/4/2018					
FP-106B	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 6 - AREA B	9/4/2018	9/4/2018					
FP-107A	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 7 - AREA A	9/4/2018	9/4/2018					
FP-107B	CONCEPTUAL FIRE PROTECTION PLAN - LEVEL 7 - AREA B	9/4/2018	9/4/2018					
FP-601	FIRE PROTECTION RISER DIAGRAM	9/4/2018	9/4/2018					
PLUMBING DRAWINGS								
P-001	PLUMBING SYMBOLS - ABBREVIATIONS AND GENERAL NOTES	9/4/2018	9/4/2018					
P-100	PLUMBING SITE PLAN	9/4/2018	9/4/2018					
P-101A	PLUMBING PLAN - LEVEL 1 - AREA A	9/4/2018	9/24/2018		9/24/2018			
P-101B	PLUMBING PLAN - LEVEL 1 - AREA B	9/4/2018	9/24/2018		9/24/2018			
P-101C	PLUMBING PLAN - LEVEL 1 - AREA C	9/4/2018	9/4/2018					
P-101D	PLUMBING PLAN - LEVEL 1 - AREA D	9/4/2018	9/4/2018					
P-101E	PLUMBING PLAN - LEVEL 1 - AREA E	9/4/2018	9/4/2018					
P-101F	PLUMBING PLAN - LEVEL 1 - AREA F - CUP	9/4/2018	9/24/2018		9/24/2018			
P-102A	PLUMBING PLAN - LEVEL 2 - AREA A	9/4/2018	9/24/2018		9/24/2018			

P-102B	PLUMBING PLAN - LEVEL 2 - AREA B	9/4/2018	9/24/2018		9/24/2018			
P-102C	PLUMBING PLAN - LEVEL 2 - AREA C	9/4/2018	9/4/2018					
P-102D	PLUMBING PLAN - LEVEL 2 - AREA D	9/4/2018	9/4/2018					
P-102E	PLUMBING PLAN - LEVEL 2 - AREA E	9/4/2018	9/4/2018					
P-103A	PLUMBING PLAN - LEVEL 3 - AREA A	9/4/2018	9/24/2018		9/24/2018			
P-103B	PLUMBING PLAN - LEVEL 3 - AREA B	9/4/2018	9/4/2018					
P-103C	PLUMBING PLAN - LEVEL 3 - AREA C	9/4/2018	9/4/2018					
P-104A	PLUMBING PLAN - LEVEL 4 - AREA A	9/4/2018	9/24/2018		9/24/2018			
P-104B	PLUMBING PLAN - LEVEL 4 - AREA B	9/4/2018	9/4/2018					
P-105A	PLUMBING PLAN - LEVEL 5 - AREA A	9/4/2018	9/24/2018		9/24/2018			
P-105B	PLUMBING PLAN - LEVEL 5 - AREA B	9/4/2018	9/24/2018		9/24/2018			
P-106A	PLUMBING PLAN - LEVEL 6 - AREA A	9/4/2018	9/24/2018		9/24/2018			
P-106B	PLUMBING PLAN - LEVEL 6 - AREA B	9/4/2018	9/4/2018					
P-107A	PLUMBING PLAN - LEVEL 7 - AREA A	9/4/2018	9/24/2018		9/24/2018			
P-107B	PLUMBING PLAN - LEVEL 7 - AREA B	9/4/2018	9/4/2018					
P-108A	PLUMBING PLAN - ROOF LEVEL - AREA A	9/4/2018	9/24/2018		9/24/2018			
P-108B	PLUMBING PLAN - ROOF LEVEL - AREA B	9/4/2018	9/24/2018		9/24/2018			
P-108C	PLUMBING PLAN - ROOF LEVEL - AREA C	9/4/2018	9/4/2018					
P-108D	PLUMBING PLAN - ROOF LEVEL - AREA D	9/4/2018	9/4/2018					
P-108E	PLUMBING PLAN - ROOF LEVEL - AREA E	9/4/2018	9/4/2018					
P-108F	PLUMBING PLAN - ROOF LEVEL - AREA F - CUP	9/4/2018	9/4/2018					
P-401	PLUMBING ENLARGED PLANS	9/4/2018	9/24/2018		9/24/2018			
P-402	PLUMBING ENLARGED PLANS	9/4/2018	9/4/2018					
P-403	PLUMBING ENLARGED PLANS	9/4/2018	9/24/2018		9/24/2018			
P-404	PLUMBING ENLARGED PLANS	9/4/2018	9/24/2018		9/24/2018			
P-405	PLUMBING ENLARGED PLANS	9/4/2018	9/4/2018					
P-406	PLUMBING ENLARGED PLANS	9/4/2018	9/24/2018		9/24/2018			
P-407	PLUMBING ENLARGED PLANS	9/4/2018	9/24/2018		9/24/2018			
P-601	PLUMBING ENLARGED PLANS	9/4/2018	9/4/2018					
P-602	PLUMBING ENLARGED PLANS	9/4/2018	9/4/2018					
P-603	PLUMBING ENLARGED PLANS	9/4/2018	9/4/2018					
P-701	PLUMBING SCHEDULE	9/4/2018	9/4/2018					
MECHANICAL DRAWINGS								
MH-001	MECHANICAL GENERAL LEGEND	9/4/2018	9/4/2018					
MH-100	MECHANICAL SITE PLAN	9/4/2018	9/4/2018					
MH-101A	MECHANICAL HVAC PLAN - LEVEL 1 - AREA A	9/4/2018	9/4/2018					
MH-101B	MECHANICAL HVAC PLAN - LEVEL 1 - AREA B	9/4/2018	9/4/2018					
MH-101C	MECHANICAL HVAC PLAN - LEVEL 1 - AREA C	9/4/2018	9/4/2018					
MH-101D	MECHANICAL HVAC PLAN - LEVEL 1 - AREA D	9/4/2018	9/4/2018					
MH-101E	MECHANICAL HVAC PLAN - LEVEL 1 - AREA E	9/4/2018	9/4/2018					
MH-101F	MECHANICAL HVAC PLAN - LEVEL 1 - AREA F - CUP	9/4/2018	9/21/2018		9/21/2018			
MH-102A	MECHANICAL HVAC PLAN - LEVEL 2 - AREA A	9/4/2018	9/4/2018					
MH-102B	MECHANICAL HVAC PLAN - LEVEL 2 - AREA B	9/4/2018	9/4/2018					
MH-102C	MECHANICAL HVAC PLAN - LEVEL 2 - AREA C	9/4/2018	9/4/2018					
MH-102D	MECHANICAL HVAC PLAN - LEVEL 2 - AREA D	9/4/2018	9/4/2018					
MH-102E	MECHANICAL HVAC PLAN - LEVEL 2 - AREA E	9/4/2018	9/4/2018					
MH-103A	MECHANICAL HVAC PLAN - LEVEL 3 - AREA A	9/4/2018	9/4/2018					
MH-103B	MECHANICAL HVAC PLAN - LEVEL 3 - AREA B	9/4/2018	9/4/2018					
MH-103C	MECHANICAL HVAC PLAN - LEVEL 3 - AREA C	9/4/2018	9/4/2018					
MH-104A	MECHANICAL HVAC PLAN - LEVEL 4 - AREA A	9/4/2018	9/4/2018					
MH-104B	MECHANICAL HVAC PLAN - LEVEL 4 - AREA B	9/4/2018	9/4/2018					
MH-105A	MECHANICAL HVAC PLAN - LEVEL 5 - AREA A	9/4/2018	9/21/2018		9/21/2018			
MH-105B	MECHANICAL HVAC PLAN - LEVEL 5 - AREA B	9/4/2018	9/21/2018		9/21/2018			
MH-106A	MECHANICAL HVAC PLAN - LEVEL 6 - AREA A	9/4/2018	9/4/2018					
MH-106B	MECHANICAL HVAC PLAN - LEVEL 6 - AREA B	9/4/2018	9/4/2018					
MH-107A	MECHANICAL HVAC PLAN - LEVEL 7 - AREA A	9/4/2018	9/4/2018					
MH-107B	MECHANICAL HVAC PLAN - LEVEL 7 - AREA B	9/4/2018	9/4/2018					
MH-108	MECHANICAL HVAC PLAN - LEVEL ROOF	9/4/2018	9/21/2018		9/21/2018			
MH-301	MECHANICAL SECTIONS	9/4/2018	9/4/2018					

MH-401	MECHANICAL ENLARGED PLAN	9/4/2018	9/4/2018					
MH-501	MECHANICAL DETAILS I	9/4/2018	9/4/2018					
MH-502	MECHANICAL DETAILS II	9/4/2018	9/4/2018					
MH-503	MECHANICAL DETAILS III	9/4/2018	9/4/2018					
MH-601	MECHANICAL CHILLED WATER FLOW DIAGRAM	9/4/2018	9/4/2018					
MH-602	MECHANICAL CONTROL DIAGRAM I	9/4/2018	9/4/2018					
MH-603	MECHANICAL CONTROL DIAGRAM II	9/4/2018	9/4/2018					
MH-604	MECHANICAL CONTROL DIAGRAMS	9/4/2018	9/4/2018					
MH-605	MECHANICAL CONTROL DIAGRAMS	9/4/2018	9/4/2018					
MH-606	MECHANICAL CONTROL DIAGRAMS	9/4/2018	9/4/2018					
MH-607	MECHANICAL SMOKE MANAGEMENT PLAN	9/4/2018	9/4/2018					
MH-701	MECHANICAL SCHEDULES I	9/4/2018	9/21/2018		9/21/2018			
MH-702	MECHANICAL SCHEDULES II	9/4/2018	9/21/2018		9/21/2018			
MH-703	MECHANICAL SCHEDULES	9/4/2018	9/21/2018		9/21/2018			
MH-704	MECHANICAL SCHEDULES	9/4/2018	9/21/2018		9/21/2018			
MH-705	MECHANICAL SCHEDULES	9/4/2018	9/21/2018		9/21/2018			
MP-101	MECHANICAL HYDRONIC PLAN - LEVEL 1 - AREA A,B,C	9/4/2018	9/4/2018					
MP-102	MECHANICAL HYDRONIC PLAN - LEVEL 2 - AREA A,B,C	9/4/2018	9/4/2018					
MP-103	MECHANICAL HYDRONIC PLAN - LEVEL 3 THRU 7	9/4/2018	9/4/2018					
ELECTRICAL DRAWINGS								
E-001	ELECTRICAL GENERAL LEGEND	9/4/2018	9/4/2018					
E-101	ELECTRICAL LIGHTING SITE PLAN	9/4/2018	9/24/2018		9/24/2018			
E-102	ELECTRICAL POWER SITE PLAN	9/4/2018	9/4/2018					
E-401	ELECTRICAL ENLARGED PLANS	9/4/2018	9/4/2018					
E-402	ELECTRICAL ENLARGED PLANS	9/4/2018	9/4/2018					
E-403	ELECTRICAL ENLARGED PLANS	9/4/2018	9/4/2018					
E-404	ELECTRICAL ENLARGED PLANS	9/4/2018	9/4/2018					
E-405	ELECTRICAL ENLARGED PLANS	9/4/2018	9/4/2018					
E-501	ELECTRICAL DETAILS I	9/4/2018	9/21/2018		9/21/2018			
E-502	ELECTRICAL DETAILS II	9/4/2018	9/4/2018					
E-601	ELECTRICAL ONE - LINE DIAGRAM - MSB-1	9/4/2018	9/24/2018		9/24/2018			
E-602	ELECTRICAL ONE - LINE DIAGRAM - MSB-2 & CENTRAL PLANT	9/4/2018	9/4/2018					
E-701	ELECTRICAL SCHEDULES I	9/4/2018	9/4/2018					
E-702	ELECTRICAL SCHEDULES II	9/4/2018	9/4/2018					
E-703	ELECTRICAL SCHEDULES III	9/4/2018	9/4/2018					
E-704	ELECTRICAL SCHEDULES IV	9/4/2018	9/4/2018					
E-705	ELECTRICAL SCHEDULES V	9/4/2018	9/4/2018					
E-706	ELECTRICAL SCHEDULES VI	9/4/2018	9/4/2018					
E-707	ELECTRICAL SCHEDULES VII	9/4/2018	9/4/2018					
E-708	ELECTRICAL SCHEDULES VIII	9/4/2018	9/4/2018					
E-709	ELECTRICAL SCHEDULES IX	9/4/2018	9/21/2018		9/21/2018			
E-710	ELECTRICAL SCHEDULES X	9/4/2018	9/4/2018					
E-711	ELECTRICAL SCHEDULES XI	9/4/2018	9/4/2018					
E-712	ELECTRICAL SCHEDULES XII	9/4/2018	9/4/2018					
E-713	ELECTRICAL SCHEDULES XIII	9/4/2018	9/21/2018		9/21/2018			
E-714	ELECTRICAL SCHEDULES XIV	9/4/2018	9/21/2018		9/21/2018			
E-715	ELECTRICVAL SCHEDULES XV	9/4/2018	9/21/2018		9/21/2018			
E-716	ELECTRICVAL SCHEDULES XVI	9/4/2018	9/21/2018		9/21/2018			
E-717	ELECTRICVAL SCHEDULES XVII	9/4/2018	9/21/2018		9/21/2018			
E-718	ELECTRICVAL SCHEDULES XVIII	9/4/2018	9/21/2018		9/21/2018			
E-719	ELECTRICAL SCHEDULES XIX	9/4/2018	9/21/2018		9/21/2018			
E-720	ELECTRICAL SCHEDULES XX	9/4/2018	9/4/2018					
E-721	ELECTRICAL SCHEDULES XXI	9/4/2018	9/4/2018					
E-722	ELECTRICAL SCHEDULES XXII	9/4/2018	9/4/2018					
E-723	ELECTRICAL SCHEDULES XXIII	9/4/2018	9/21/2018		9/21/2018			
E-724	ELECTRICAL SCHEDULES XXIV	9/4/2018	9/4/2018					
E-725	ELECTRICAL SCHEDULES XXV	9/4/2018	9/21/2018		9/21/2018			
E-726	ELECTRICAL SCHEDULES XXVI	9/4/2018	9/21/2018		9/21/2018			
EL-101A	ELECTRICAL LIGHTING PLAN - LEVEL 1 - AREA A	9/4/2018	9/4/2018					

EL-101B	ELECTRICAL LIGHTING PLAN - LEVEL 1 - AREA B	9/4/2018	9/4/2018					
EL-101C	ELECTRICAL LIGHTING PLAN - LEVEL 1 - AREA C	9/4/2018	9/4/2018					
EL-101D	ELECTRICAL LIGHTING PLAN - LEVEL 1 - AREA D	9/4/2018	9/4/2018					
EL-101E	ELECTRICAL LIGHTING PLAN - LEVEL 1 - AREA E	9/4/2018	9/4/2018					
EL-101F	ELECTRICAL LIGHTING PLAN - LEVEL 1 - AREA F - CUP	9/4/2018	9/4/2018					
EL-102A	ELECTRICAL LIGHTING PLAN - LEVEL 2 - AREA A	9/4/2018	9/4/2018					
EL-102B	ELECTRICAL LIGHTING PLAN - LEVEL 2 - AREA B	9/4/2018	9/4/2018					
EL-102C	ELECTRICAL LIGHTING PLAN - LEVEL 2 - AREA C	9/4/2018	9/4/2018					
EL-102D	ELECTRICAL LIGHTING PLAN - LEVEL 2 - AREA D	9/4/2018	9/4/2018					
EL-102E	ELECTRICAL LIGHTING PLAN - LEVEL 2 - AREA E	9/4/2018	9/4/2018					
EL-103A	ELECTRICAL LIGHTING PLAN - LEVEL 3 - AREA A	9/4/2018	9/4/2018					
EL-103B	ELECTRICAL LIGHTING PLAN - LEVEL 3 - AREA B	9/4/2018	9/4/2018					
EL-104A	ELECTRICAL LIGHTING PLAN - LEVEL 4 - AREA A	9/4/2018	9/4/2018					
EL-104B	ELECTRICAL LIGHTING PLAN - LEVEL 4 - AREA B	9/4/2018	9/4/2018					
EL-105A	ELECTRICAL LIGHTING PLAN - LEVEL 5 - AREA A	9/4/2018	9/4/2018					
EL-105B	ELECTRICAL LIGHTING PLAN - LEVEL 5 - AREA B	9/4/2018	9/4/2018					
EL-106A	ELECTRICAL LIGHTING PLAN - LEVEL 6 - AREA A	9/4/2018	9/4/2018					
EL-106B	ELECTRICAL LIGHTING PLAN - LEVEL 6 - AREA B	9/4/2018	9/4/2018					
EL-107A	ELECTRICAL LIGHTING PLAN - LEVEL 7 - AREA A	9/4/2018	9/4/2018					
EL-107B	ELECTRICAL LIGHTING PLAN - LEVEL 7 - AREA B	9/4/2018	9/4/2018					
EP-101	MECHANICAL EQUIPMENT PLAN - LEVEL 1	9/4/2018	9/21/2018		9/21/2018			
EP-101A	ELECTRICAL POWER PLAN - LEVEL 1 - AREA A	9/4/2018	9/4/2018					
EP-101B	ELECTRICAL POWER PLAN - LEVEL 1 - AREA B	9/4/2018	9/4/2018					
EP-101C	ELECTRICAL POWER PLAN - LEVEL 1 - AREA C	9/4/2018	9/4/2018					
EP-101D	ELECTRICAL POWER PLAN - LEVEL 1 - AREA D	9/4/2018	9/4/2018					
EP-101E	ELECTRICAL POWER PLAN - LEVEL 1 - AREA E	9/4/2018	9/21/2018		9/21/2018			
EP-101F	ELECTRICAL POWER PLAN - LEVEL 1 - AREA F - CUP	9/4/2018	9/21/2018		9/21/2018			
EP-102	MECHANICAL EQUIPMENT PLAN LEVEL 2	9/4/2018	9/21/2018		9/21/2018			
EP-102A	ELECTRICAL POWER PLAN - LEVEL 2 - AREA A	9/4/2018	9/4/2018					
EP-102B	ELECTRICAL POWER PLAN - LEVEL 2 - AREA B	9/4/2018	9/4/2018					
EP-102C	ELECTRICAL POWER PLAN - LEVEL 2 - AREA C	9/4/2018	9/4/2018					
EP-102D	ELECTRICAL POWER PLAN - LEVEL 2 - AREA D	9/4/2018	9/4/2018					
EP-102E	ELECTRICAL POWER PLAN - LEVEL 2 - AREA E	9/4/2018	9/4/2018					
EP-103	MECHANICAL EQUIPMENT PLAN LEVEL 3	9/4/2018	9/21/2018		9/21/2018			
EP-103A	ELECTRICAL EQUIPMENT PLAN LEVEL 3 - AREA A	9/4/2018	9/4/2018					
EP-103B	ELECTRICAL EQUIPMENT PLAN LEVEL 3 - AREA B	9/4/2018	9/4/2018					
EP-103C	ELECTRICAL EQUIPMENT PLAN LEVEL 3 - AREA C	9/4/2018	9/4/2018					
EP-104	MECHANICAL EQUIPMENT PLAN LEVEL 4	9/4/2018	9/21/2018		9/21/2018			
EP-104A	ELECTRICAL EQUIPMENT PLAN LEVEL 4 - AREA A	9/4/2018	9/4/2018					
EP-104B	ELECTRICAL EQUIPMENT PLAN LEVEL 4 - AREA B	9/4/2018	9/4/2018					
EP-105	MECHANICAL EQUIPMENT PLAN LEVEL 5	9/4/2018	9/21/2018		X			
EP-105A	ELECTRICAL EQUIPMENT PLAN LEVEL 5 - AREA A	9/4/2018	9/4/2018					
EP-105B	ELECTRICAL EQUIPMENT PLAN LEVEL 5 - AREA B	9/4/2018	9/4/2018					
EP-106	MECHANICAL EQUIPMENT PLAN LEVEL 6	9/4/2018	9/21/2018		9/21/2018			
EP-106A	ELECTRICAL EQUIPMENT PLAN LEVEL 6 - AREA A	9/4/2018	9/4/2018					
EP-106B	ELECTRICAL EQUIPMENT PLAN LEVEL 6 - AREA B	9/4/2018	9/4/2018					
EP-107	MECHANICAL EQUIPMENT PLAN LEVEL 7	9/4/2018	9/21/2018		9/21/2018			
EP-107A	ELECTRICAL EQUIPMENT PLAN LEVEL 7 - AREA A	9/4/2018	9/4/2018					
EP-107B	ELECTRICAL EQUIPMENT PLAN LEVEL 7 - AREA B	9/4/2018	9/4/2018					
EP-108	MECHANICAL EQUIPMENT PLAN LEVEL ROOF	9/4/2018	9/21/2018		9/21/2018			
COMMUNICATIONS DRAWINGS								
ET-001	TELECOMMUNICATIONS GENERAL LEGEND	9/4/2018	9/24/2018		9/24/2018			
ET-101	TELECOMMUNICATIONS MAIN TRUNK PATHWAY PLAN - LEVEL 1	9/4/2018	9/4/2018					
ET-101A	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 1 - AREA A	9/4/2018	9/4/2018					
ET-101B	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 1 - AREA B	9/4/2018	9/4/2018					
ET-101C	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 1 - AREA C	9/4/2018	9/4/2018					
ET-101D	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 1 - AREA D	9/4/2018	9/4/2018					
ET-101E	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 1 - AREA E	9/4/2018	9/4/2018					
ET-101F	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 1 - AREA F	9/4/2018	9/4/2018					

ET-102	TELECOMMUNICATIONS MAIN TRUNK PATHWAY PLAN - LEVEL 2	9/4/2018	9/4/2018					
ET-102A	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 2 - AREA A	9/4/2018	9/4/2018					
ET-102B	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 2 - AREA B	9/4/2018	9/4/2018					
ET-102C	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 2 - AREA C	9/4/2018	9/4/2018					
ET-102D	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 2 - AREA D	9/4/2018	9/4/2018					
ET-102E	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 2 - AREA E	9/4/2018	9/4/2018					
ET-103	TELECOMMUNICATIONS MAIN TRUNK PATHWAY PLAN - LEVEL 3	9/4/2018	9/4/2018					
ET-103A	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 3 - AREA A	9/4/2018	9/4/2018					
ET-103B	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 3 - AREA B	9/4/2018	9/4/2018					
ET-103C	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 3 - AREA C	9/4/2018	9/4/2018					
ET-104	TELECOMMUNICATIONS MAIN TRUNK PATHWAY PLAN - LEVEL 4	9/4/2018	9/4/2018					
ET-104A	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 4 - AREA A	9/4/2018	9/4/2018					
ET-104B	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 4 - AREA B	9/4/2018	9/4/2018					
ET-105	TELECOMMUNICATIONS MAIN TRUNK PATHWAY PLAN - LEVEL 5	9/4/2018	9/4/2018					
ET-105A	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 5 - AREA A	9/4/2018	9/4/2018					
ET-105B	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 5 - AREA B	9/4/2018	9/4/2018					
ET-106	TELECOMMUNICATIONS MAIN TRUNK PATHWAY PLAN - LEVEL 6	9/4/2018	9/4/2018					
ET-106A	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 6 - AREA A	9/4/2018	9/4/2018					
ET-106B	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 6 - AREA B	9/4/2018	9/4/2018					
ET-107	TELECOMMUNICATIONS MAIN TRUNK PATHWAY PLAN - LEVEL 7	9/4/2018	9/4/2018					
ET-107A	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 7 - AREA A	9/4/2018	9/4/2018					
ET-107B	TELECOMMUNICATIONS FLOOR PLAN - LEVEL 7 - AREA B	9/4/2018	9/4/2018					
ET-501	TELECOMMUNICATIONS DETAILS I	9/4/2018	9/4/2018					
ET-502	TELECOMMUNICATIONS DETAILS II	9/4/2018	9/4/2018					
ET-601	TELECOMMUNICATIONS DIAGRAMS	9/4/2018	9/4/2018					
ET-701	TELECOMMUNICATIONS SCHEDULES I	9/4/2018	9/4/2018					
ET-702	TELECOMMUNICATIONS SCHEDULES II	9/4/2018	9/4/2018					
EY-001	ELECTRONIC SECURITY GENERAL NOTES AND SYMBOLS	9/4/2018	9/4/2018					
EY-100	ELECTRONIC SECURITY SITE PLAN	9/4/2018	9/4/2018					
EY-101A	ELECTRONIC SECURITY LEVEL 1 PLAN - AREA A	9/4/2018	9/4/2018					
EY-101B	ELECTRONIC SECURITY LEVEL 1 PLAN - AREA B	9/4/2018	9/4/2018					
EY-101C	ELECTRONIC SECURITY LEVEL 1 PLAN - AREA C	9/4/2018	9/4/2018					
EY-101D	ELECTRONIC SECURITY LEVEL 1 PLAN - AREA D	9/4/2018	9/4/2018					
EY-101E	ELECTRONIC SECURITY LEVEL 1 PLAN - AREA E	9/4/2018	9/4/2018					
EY-101F	ELECTRONIC SECURITY LEVEL 1 PLAN - AREA F - CUP	9/4/2018	9/4/2018					
EY-102A	ELECTRONIC SECURITY LEVEL 2 PLAN - AREA A	9/4/2018	9/4/2018					
EY-102B	ELECTRONIC SECURITY LEVEL 2 PLAN - AREA B	9/4/2018	9/4/2018					
EY-102C	ELECTRONIC SECURITY LEVEL 2 PLAN - AREA C	9/4/2018	9/4/2018					
EY-102D	ELECTRONIC SECURITY LEVEL 2 PLAN - AREA D	9/4/2018	9/4/2018					
EY-102E	ELECTRONIC SECURITY LEVEL 2 PLAN - AREA E	9/4/2018	9/4/2018					
EY-103A	ELECTRONIC SECURITY LEVEL 3 PLAN - AREA A	9/4/2018	9/4/2018					
EY-103B	ELECTRONIC SECURITY LEVEL 3 PLAN - AREA B	9/4/2018	9/4/2018					
EY-103C	ELECTRONIC SECURITY LEVEL 3 PLAN - AREA C	9/4/2018	9/4/2018					
EY-104A	ELECTRONIC SECURITY LEVEL 4 PLAN - AREA A	9/4/2018	9/4/2018					
EY-104B	ELECTRONIC SECURITY LEVEL 4 PLAN - AREA B	9/4/2018	9/4/2018					
EY-105A	ELECTRONIC SECURITY LEVEL 5 PLAN - AREA A	9/4/2018	9/4/2018					
EY-105B	ELECTRONIC SECURITY LEVEL 5 PLAN - AREA B	9/4/2018	9/4/2018					
EY-106A	ELECTRONIC SECURITY LEVEL 6 PLAN - AREA A	9/4/2018	9/4/2018					
EY-106B	ELECTRONIC SECURITY LEVEL 6 PLAN - AREA B	9/4/2018	9/4/2018					
EY-107A	ELECTRONIC SECURITY LEVEL 7 PLAN - AREA A	9/4/2018	9/4/2018					
EY-107B	ELECTRONIC SECURITY LEVEL 7 PLAN - AREA B	9/4/2018	9/4/2018					
EY-108A	ELECTRONIC SECURITY LEVEL 8 PLAN - AREA A	9/4/2018	9/4/2018					
EY-108B	ELECTRONIC SECURITY LEVEL 8 PLAN - AREA B	9/4/2018	9/4/2018					
EY-401	ELECTRONIC SECURITY ENLARGED PLANS	9/4/2018	9/4/2018					
EY-402	ELECTRONIC SECURITY ENLARGED PLANS	9/4/2018	9/4/2018					
EY-403	ELECTRONIC SECURITY ENLARGED PLANS	9/4/2018	9/4/2018					
EY-404	ELECTRONIC SECURITY ENLARGED PLANS	9/4/2018	9/4/2018					
EY-501	ELECTRONIC SECURITY DETAILS	9/4/2018	9/4/2018					
EY-502	ELECTRONIC SECURITY DETAILS	9/4/2018	9/4/2018					

[illegible]

Hidalgo County Court House Specs Log

Division/Spec #	Division/Spec Name	Current	Original	ADDENDUM #1	ADDENDUM #2	ADDENDUM #3	ADDENDUM #1 @100%
DIV 00	PROCUREMENT AND CONTRACTING REQUIREMENTS						
00 11 13	ADVERTISEMENT TO BID	9/24/2018	9/4/2018	X			
00 21 13	INSTRUCTIONS TO BIDDERS	9/24/2018	9/4/2018	X			
00 26 00	SUBSTITUTIONS PRIOR TO BIDDING	9/24/2018	9/4/2018	X			
00 41 13	BID FORM	10/4/2018	9/4/2018	X	X	X	
DIV 01	GENERAL REQUIREMENTS						
01 11 16	WORK BY OWNER	9/24/2018	9/4/2018	X			
01 22 00	UNIT PRICES	10/3/2018	9/4/2018	X	X		
01 23 00	ALTERNATES	10/3/2018	9/4/2018	X	X		
01 23 04	CHANGES IN WORK	9/24/2018	9/4/2018	X			
01 25 13	SUBSTITUTION PROCEDURES AFTER EXECUTION OF CONTRACT	9/24/2018	9/4/2018	X			
01 26 13	REQUESTS FOR INFORMATION (RFI)	9/24/2018	9/4/2018	X			
01 29 01	APPLICATIONS FOR PAYMENT AND SCHEDULE OF VALUES (CM)	9/24/2018	9/4/2018	X			
01 33 00	SUBMITTAL PROCEDURES	9/24/2018	9/4/2018	X			
01 42 16	DEFINITIONS	9/24/2018	9/4/2018	X			
01 42 19	REFERENCE STANDARDS	9/24/2018	9/4/2018	X			
01 43 39	MOCKUP REQUIREMENTS	9/24/2018	9/4/2018	X			
01 45 00	QUALITY ASSURANCE AND CONTROL	9/24/2018	9/4/2018	X			
01 45 23	TESTS AND INSPECTIONS	9/24/2018	9/4/2018	X			
01 61 00	ACCEPTABLE MANUFACTURERS AND PRODUCTS	9/24/2018	9/4/2018	X			
01 71 23	FIELD ENGINEERING	9/24/2018	9/4/2018	X			
01 73 29	CUTTING AND PATCHING	9/24/2018	9/4/2018	X			
01 74 23	CLEANING	9/24/2018	9/4/2018	X			
01 77 01	CONTRACT CLOSEOUT (CM)	9/24/2018	9/4/2018	X			
01 78 23	OPERATION AND MAINTENANCE DATA	9/24/2018	9/4/2018	X			
01 78 36	WARRANTIES AND GUARANTEES	9/24/2018	9/4/2018	X			
01 78 39	PROJECT RECORD DOCUMENTS	9/24/2018	9/4/2018	X			
01 79 00	SYSTEM DEMONSTRATIONS	9/24/2018	9/4/2018	X			
01 91 00	GENERAL COMMISSIONING REQUIREMENTS		9/4/2018				
DIV 03	CONCRETE						
03 35 00	CONCRETE FINISHING AND REPAIR OF SURFACE DEFECTS		9/4/2018				
03 38 16	POST-TENSIONED CONCRETE - UNBONDED TENDONS		9/4/2018				
DIV 04	MASONRY						
04 05 05	COLD AND HOT WEATHER MASONRY PROCEDURES		9/4/2018				
04 05 10	MASONRY CLEANING		9/4/2018				
04 05 13	PORTLAND CEMENT - LIME MORTAR AND GROUT		9/4/2018				
04 05 23	MASONRY ACCESSORIES		9/4/2018				

DIV 05	METALS						
05 21 10	STEEL JOISTS		9/4/2018				
05 31 23	METAL ROOF DECKING		9/4/2018				
05 31 26	PERFORATED STEEL ROOF DECKING		9/4/2018				
05 40 00	COLD FORMED METAL FRAMING		9/4/2018				
05 50 10	MISCELLANEOUS METAL FABRICATIONS		9/4/2018				
05 50 13	STEEL STAIRS AND RAILINGS		9/4/2018				
05 51 36	ALUMINUM LADDERS		9/4/2018				
05 70 00	DECORATIVE METAL		9/4/2018				
05 73 00	CUSTOM METAL RAILING	9/24/2018	9/4/2018	X			
05 73 13	GLASS SUPPORTED RAILINGS		9/4/2018				
DIV 06	WOOD, PLASTICS, AND COMPOSITES						
06 10 53	ROUGH CARPENTRY		9/4/2018				
06 16 43	GYPSUM SHEATHING		9/4/2018				
06 20 00	FINISH CARPENTRY	9/24/2018	9/4/2018	X			
DIV 07	THERMAL AND MOISTURE PROTECTION						
07 13 26	SELF-ADHERING SHEET MEMBRANE WATERPROOFING		9/4/2018				
07 16 04	CONCRETE FLOOR MOISTURE TESTING		9/4/2018				
07 18 00	TRAFFIC COATINGS		9/4/2018				
07 21 00	BUILDING INSULATION	9/24/2018	9/4/2018	X			
07 21 35	SPRAY APPLIED FIBER INSULATION		9/4/2018				
07 27 29	FLUID APPLIED AIR BARRIER - VAPOR PERMEABLE		9/4/2018				
07 42 19	METAL PLATE RAINSCREEN WALL PANELS		9/4/2018				
07 42 93	SOFFIT PANELS		9/4/2018				
07 44 19	EXTERIOR PORCELAIN WALL CLADDING	9/24/2018	9/4/2018	X			
07 54 21	ADHERED FLEECE BACK PVC ROOFING		9/4/2018				
07 62 00	FLASHING AND SHEET METAL		9/4/2018				
07 72 13	PREFABRICATED ROOF CURBING		9/4/2018				
07 72 33	ROOF HATCHES		9/4/2018				
07 84 00	FIRESTOPPING		9/4/2018				
07 84 53	PERIMETER FIRE CONTAINMENT SYSTEMS		9/4/2018				
07 92 13	EXTERIOR JOINT SEALANTS		9/4/2018				
07 92 16	INTERIOR JOINT SEALANTS		9/4/2018				
DIV 08	OPENINGS						
08 11 13	HOLLOW METAL (HM) DOORS AND FRAMES		9/4/2018				
08 12 16	INTERIOR ALUMINUM DOOR AND WINDOW FRAMES		9/4/2018				
08 14 16	FLUSH WOOD DOORS		9/4/2018				
08 14 23	PLASTIC LAMINATE FACED DOORS		9/4/2018				
08 14 33	STILE AND RAIL WOOD DOORS		9/4/2018				
08 31 16	ACCESS PANELS AND DOORS		9/4/2018				
08 33 00	SIDE COILING SECURITY GRILLES (CG)		9/4/2018				
08 33 23	OVERHEAD COILING DOORS (CD)		9/4/2018				
08 34 56	SECURITY GATES		9/4/2018				
08 34 83	ELEVATOR DOOR SMOKE CONTAINMENT SYSTEM		9/4/2018				

08 41 13	LOW-RISE ALUMINUM STOREFRONT		9/4/2018				
08 41 15	ALUMINUM-FRAMED ENTRANCES		9/4/2018				
08 41 18	INTERIOR ALUMINUM STOREFRONT		9/4/2018				
08 44 14	UNITIZED CURTAIN WALL ASSEMBLY	9/24/2018	9/4/2018	X			
08 71 00	DOOR HARDWARE		9/4/2018				
08 71 13	AUTOMATIC SWINGING DOOR OPERATORS		9/4/2018				
08 81 23	EXTERIOR GLASS AND GLAZING		9/4/2018				
08 81 26	INTERIOR GLASS AND GLAZING		9/4/2018				
08 88 53	SECURITY GLAZING		9/4/2018				
08 91 00	ARCHITECTURAL LOUVERS		9/4/2018				
DIV 09	FINISHES						
09 22 16	NON-STRUCTURAL METAL FRAMING		9/4/2018				
09 22 36	METAL LATH		9/4/2018				
09 23 00	GYPSUM PLASTER		9/4/2018				
09 23 55	IMPACT RESISTANT GYPSUM PLASTER		9/4/2018				
09 24 23	PORTLAND CEMENT PLASTER (PC)		9/4/2018				
09 24 24	PORTLAND CEMENT STUCCO		9/4/2018				
09 29 00	GYPSUM WALLBOARD		9/4/2018				
09 30 00	TILE		9/4/2018				
09 51 00	ACOUSTICAL CEILINGS (ACT)		9/4/2018				
09 54 47	EXTERIOR MODULAR METAL CEILING SYSTEMS		9/4/2018				
09 57 53	METAL SECURITY CEILINGS		9/4/2018				
09 65 13	RESILIENT BASE (RB)		9/4/2018				
09 65 17	LINOLEUM (LN)		9/4/2018				
09 65 36	STATIC DISSIPATIVE RESILIENT TILE FLOORING (SDRT)		9/4/2018				
09 68 13	CARPET TILE (CPT)		9/4/2018				
09 84 00	ACOUSTICAL PANEL SYSTEM - CEMENTITIOUS WOOD FIBER		9/4/2018				
09 84 47	MODULAR METAL WALL SYSTEM		9/4/2018				
09 91 13	EXTERIOR PAINTING		9/4/2018				
09 91 23	INTERIOR PAINTING		9/4/2018				
09 96 23	GRAFFITI - MOISTURE PROTECTION SURFACE SEALER		9/4/2018				
DIV 10	SPECIALTIES						
10 11 00	MARKERBOARDS AND TACKBOARDS		9/4/2018				
10 13 00	DIRECTORIES AND BULLETIN BOARDS		9/4/2018				
10 14 03	IDENTIFICATION DEVICES - EXTERIOR		9/4/2018				
10 14 06	IDENTIFICATION DEVICES - INTERIOR		9/4/2018				
10 14 16	PLAQUES		9/4/2018				
10 14 43	PHOTOLUMINESCENT EGRESS MARKINGS		9/4/2018				
10 14 63	DIGITAL SIGNAGE SYSTEMS		9/4/2018				
10 21 14	SOLID POLYMER HDPE TOILET PARTITIONS		9/4/2018				
10 26 00	WALL PROTECTION SPECIALTIES		9/4/2018				
10 28 13	TOILET AND BATH ACCESSORIES		9/4/2018				
10 44 00	FIRE PROTECTION SPECIALTIES		9/4/2018				
10 51 13	METAL LOCKERS		9/4/2018				
10 55 23	MAIL BOXES		9/4/2018				

10 55 36	DROP BOX		9/4/2018				
10 56 26	MOTORIZED MOBILE STORAGE SHELVING		9/4/2018				
10 75 00	FLAGPOLES		9/4/2018				
10 81 13	BIRD CONTROL DEVICE		9/4/2018				
DIV 11	EQUIPMENT						
11 12 00	PARKING EQUIPMENT		9/4/2018				
11 13 19	DOCK LEVELERS AND EQUIPMENT		9/4/2018				
11 19 00	DETENTION EQUIPMENT		9/4/2018				
11 19 19	TAMPER RESISTANT FASTENERS		9/4/2018				
11 24 23	WINDOW WASHING SYSTEM		9/4/2018				
11 24 26	SAFETY TIE-BACKS		9/4/2018				
11 52 13	PROJECTION SCREENS		9/4/2018				
DIV 12	FURNISHINGS						
12 05 01	FURNITURE AND FURNISHINGS - GENERAL REQUIREMENTS		9/4/2018				
12 24 14	ROLLER SHADES		9/4/2018				
12 32 00	ARCHITECTURAL CASEWORK	9/24/2018	9/4/2018	X			
12 36 63	SOLID SURFACE FABRICATIONS (SSF)		9/4/2018				
12 67 00	BENCHES		9/4/2018				
DIV 13	SPECIAL CONSTRUCTION						
13 42 63	STEEL DETENTION CELLS – PANELIZED CONSTRUCTION		9/4/2018				
DIV 14	CONVEYING EQUIPMENT						
14 21 00	ELECTRIC TRACTION ELEVATORS		9/4/2018				
14 31 00	ESCALATORS		9/4/2018				
14 42 16	WHEELCHAIR LIFT		9/4/2018				
DIV 20	MECHANICAL GENERAL REQUIREMENTS						
20 05 10	ACCESS PANELS		9/4/2018				
20 05 19	PIPING SPECIALTIES		9/4/2018				
20 05 50	MECHANICAL SOUND AND VIBRATION CONTROL		9/4/2018				
20 07 00	PIPE, DUCT AND EQUIPMENT INSULATION		9/4/2018				
20 08 00	TESTING AND BALANCING		9/4/2018				
DIV 21	FIRE SUPPRESSION						
21 10 00	FIRE PROTECTION SYSTEMS		9/4/2018				
21 22 00	CLEAN AGENT FIRE PROTECTION SYSTEM		9/4/2018				
DIV 22	PLUMBING						
22 10 16	PLUMBING PIPING		9/4/2018				
22 11 23	PLUMBING PUMPS		9/4/2018				
22 11 26	PACKAGED DOMESTIC WATER PRESSURE BOOSTER SYSTEM		9/4/2018				
22 31 16	WATER SOFTENER		9/4/2018				
22 33 00	DOMESTIC WATER HEATERS		9/4/2018				
22 42 00	PLUMBING FIXTURES		9/4/2018				

DIV 23	HEATING, VENTILATING, AND AIR CONDITIONING						
23 21 23	HVAC PUMPS		9/4/2018				
23 23 00	REFRIGERANT PIPING SYSTEM		9/4/2018				
23 25 16	COOLING TOWER TREATMENT SYSTEM		9/4/2018				
23 31 13	AIR DISTRIBUTION SYSTEM		9/4/2018				
23 35 00	EXHAUST AND VENTILATING FANS		9/4/2018				
23 35 13	LOCAL EXHAUST SYSTEMS		9/4/2018				
23 36 00	AIR TERMINAL UNITS		9/4/2018				
23 37 23	LOUVERED PENTHOUSE		9/4/2018				
23 64 16	CENTRIFUGAL CHILLER		9/4/2018				
23 65 13	COOLING TOWER - PACKAGED		9/4/2018				
23 72 13	TOTAL ENERGY HEAT RECOVERY WHEEL		9/4/2018				
23 73 23	FACTORY BUILT CUSTOM AIR HANDLING UNITS		9/4/2018				
23 81 23	COMPUTER ROOM AIR CONDITIONING UNIT		9/4/2018				
23 82 43	ELECTRIC HEATERS		9/4/2018				
DIV 25	INTEGRATED AUTOMATION						
25 50 00	BUILDING MANAGEMENT AND CONTROL SYSTEM		9/4/2018				
DIV 26	ELECTRICAL						
26 00 10	ELECTRICAL GENERAL REQUIREMENTS		9/4/2018				
26 00 11	WIRING EQUIPMENT FURNISHED BY OTHERS		9/4/2018				
26 00 13	ESSENTIAL ELECTRICAL SYSTEMS		9/4/2018				
26 05 26	GROUNDING AND BONDING FOR ELECTRICAL SYSTEMS		9/4/2018				
26 05 34	BOXES		9/4/2018				
26 05 43	UNDERGROUND DUCTS AND RACEWAYS FOR ELECTRICAL SYSTEMS		9/4/2018				
26 05 53	IDENTIFICATION FOR ELECTRICAL SYSTEMS		9/4/2018				
26 09 23	LIGHTING CONTROL DEVICES		9/4/2018				
26 09 43	NETWORKED LIGHTING CONTROL SYSTEM		9/4/2018				
26 22 13	LOW VOLTAGE DISTRIBUTION TRANSFORMERS		9/4/2018				
26 23 00	SWITCHGEAR		9/4/2018				
26 24 13	SWITCHBOARDS		9/4/2018				
26 24 16	PANELBOARDS		9/4/2018				
26 28 00	OVERCURRENT PROTECTIVE DEVICES		9/4/2018				
26 32 13	DIESEL ENGINE DRIVEN GENERATOR SETS		9/4/2018				
26 33 54	UNINTERRUPTIBLE POWER SUPPLY SYSTEMS		9/4/2018				
26 36 23	AUTOMATIC TRANSFER SWITCHES		9/4/2018				
26 41 13	LIGHTNING PROTECTION SYSTEM		9/4/2018				
26 43 13	SURGE PROTECTIVE DEVICES (SPD)		9/4/2018				
26 51 13	BUILDING LIGHTING		9/4/2018				
26 56 00	SITE LIGHTING		9/4/2018				
DIV 27	COMMUNICATIONS						
27 02 00	STRUCTRED CABLING SYSTEMS AND PATHWAYS AND SPACE SYSTEMS FOR ALL VOICE & DATA, AND ELECTRONIC SAFETY AND SECURITY (ADDED AD #4)		9/4/2018				

27 05 26	GROUNDING AND BONDING FOR COMMUNICATION SYSTEMS (ADDED AD #4)		9/4/2018				
27 05 28	PATHWAYS FOR COMMUNICATION SYSTEMS (REVISED AD #4)		9/4/2018				
27 05 29	HANGERS AND SUPPORTS FOR COMMUNICATIONS (ADDED AD #4)		9/4/2018				
27 05 28.28	FIRESTOPPING		9/4/2018				
27 05 30	EMPTY CONDUIT AND OUTLET BOXES		9/4/2018				
27 05 36	CABLE TRAYS FOR COMMUNICATIONS SYSTEMS	9/24/2018	9/4/2018	X			
27 05 43	UNDERGROUND PATHWAYS AND STRUCTURES FOR COMMUNICATION SYSTEMS (ADDED AD #4)		9/4/2018				
27 05 44	SLEEVES AND SLEEVE SEALS FOR COMMUNICATIONS PATHWAYS AND CABLING (ADDED AD #4)		9/4/2018				
27 05 53	IDENTIFICATION FOR COMMUNICATIONS SYSTEMS (ADDED AD #4)		9/4/2018				
27 10 00	STRUCTURED CABLING (ADDED AD #4)		9/4/2018				
27 11 00	COMMUNICATIONS EQUIPMENT ROOM FITTINGS (ADDED AD #4)		9/4/2018				
27 11 16	COMMUNICATIONS RACKS, FRAMES, AND ENCLOSURES (ADDED AD #4)		9/4/2018				
27 11 70	HOT AISLE COLD THERMAL CONTAINMENT SYSTEM (ADDED AD #4)		9/4/2018				
27 13 13	COMMUNICATIONS COPPER BACKBONE CABLING (ADDED AD #4)		9/4/2018				
27 13 23	COMMUNICATIONS OPTICAL FIBER BACKBONE CABLING (ADDED AD #4)		9/4/2018				
27 13 33	COMMUNICATIONS COAXIAL BACKBONE CABLING (ADDED AD #4)		9/4/2018				
27 15 13	COMMUNICATIONS COPPER HORIZONTAL CABLING (ADDED AD #4)		9/4/2018				
27 15 23	COMMUNICATION OPTICAL FIBER HORIZONTAL CABLING (ADDED AD #4)		9/4/2018				
27 15 33	COMMUNICATIONS COAXIAL HORIZONTAL CABLING		9/4/2018				
27 41 16	INTEGRATED AUDIO/VIDEO SYSTEMS AND EQUIPMENT		9/4/2018				
27 41 26	TELEVISION SYSTEM		9/4/2018				
27 51 00	COMMUNICATIONS SYSTEMS - GENERAL REQUIREMENTS		9/4/2018				
27 51 23	INTERCOMMUNICATION SYSTEMS - MICROPROCESSOR BASED (RE-ISSUED AD #4)		9/4/2018				
DIV 28	ELECTRONIC SAFETY AND SECURITY						
28 05 00	BASIC MATERIALS & METHODS FOR ELECTRONIC SYSTEMS		9/4/2018				
28 05 10	EQUIPMENT ENCLOSURES		9/4/2018				
28 05 20	LOW VOLTAGE WIRE AND CABLE		9/4/2018				
28 13 00	ACCESS CONTROL SYSTEM		9/4/2018				
28 20 00	DETENTION COMMUNICATION SYSTEM		9/4/2018				
28 23 00	VIDEO SURVEILLANCE SYSTEM		9/4/2018				
28 31 00	FIRE ALARM SYSTEM		9/4/2018				
28 31 13	FIRE ALARM AND DETECTION SYSTEMS		9/4/2018				
28 31 13E	FIRE ALARM AND DETECTION SYSTEMS		9/4/2018				
28 31 30	AIR SAMPLING SMOKE DETECTION SYSTEM		9/4/2018				
28 31 43	FIRE DEPARTMENT RADIO SYSTEM		9/4/2018				
28 46 10	PROGRAMMABLE LOGIC CONTROLLER		9/4/2018				
28 46 20	GRAPHICAL USER INTERFACE		9/4/2018				
28 46 30	NETWORK EQUIPMENT		9/4/2018				
28 50 00	UNINTERRUPTIBLE POWER SUPPLY		9/4/2018				
DIV 31	EARTHWORK						
31 22 00	SITE EXCAVATION AND ROUGH GRADING		9/4/2018				

31 22 19	TOPSOILING AND FINISHED GRADING		9/4/2018				
DIV 32	EXTERIOR IMPROVEMENTS						
32 13 13	CONCRETE PAVING AND CURBS		9/4/2018				
32 13 15	DECORATIVE CEMENT CONCRETE PAVEMENT		9/4/2018				
32 17 13	PARKING BUMPERS		9/4/2018				
32 17 23	PAVING STRIPING AND MARKING		9/4/2018				
32 31 15	GATE OPERATOR - SLIDING		9/4/2018				
32 31 18	PRE-FABRICATED ORNAMENTAL ALUMINUM FENCE		9/4/2018				
32 84 23	IRRIGATION SYSTEM		9/4/2018				
32 92 19	SEEDING		9/4/2018				
32 92 23	SODDING		9/4/2018				
32 93 13	PLANTS AND PLANTING		9/4/2018				

Hidalgo County Courthouse Exhibit E - 30 Day Look Ahead Schedule

Exhibit E

8 WEEK LOOK AHEAD SCHEDULE

Project Name: Hidalgo County Courthouse
Project Manager: Brian Pippin
Superintendent: Brian McNeal

HCCH Hidalgo County Courthouse

[illegible]
