


ConvergeOne Statement of Work

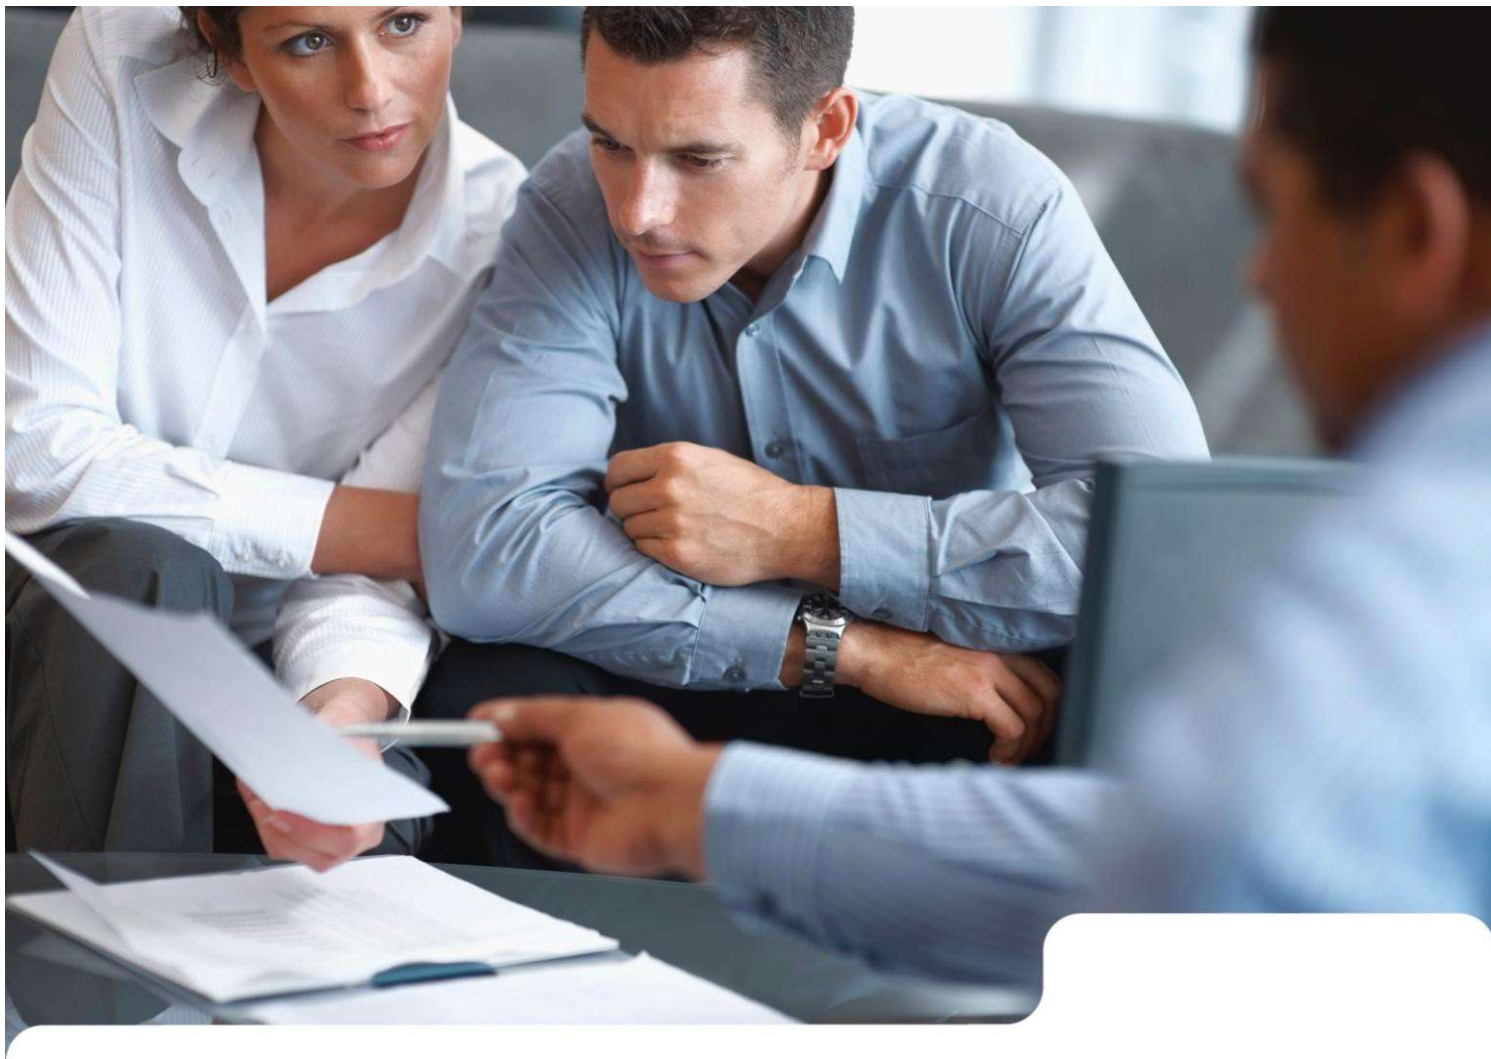

Routing Change Services

PREPARED FOR: WILLIAMSON COUNTY

PREPARED BY: Chad Brinkley

National Account Manager
CBrinkley@convergeone.com

Luis Grados

Senior Solutions Architect
LGrados@convergeone.com

REFERENCE: Opportunity: OP-000673031
Solution: SO-000750162
[REDACTED]

DIR-TSO-4167 is the contract vehicle
For the services described in the SOW

DATE: April 8, 2022

TABLE OF CONTENTS

1. Confidentiality Notice.....3

2. Scope of Work - Terms and Conditions.....3

3. Project Timeline Expectations4

4. Project Overview4

5. Project Scope of Services5

6. Project Management.....6

7. Change Order Process7

8. Milestone and/or Project Acceptance7

9. Customer Responsibilities7

10. Professional Services Assumptions8

11. Professional Services Pricing and Billing Schedule10

12. Customer Authorization to Proceed12

1. CONFIDENTIALITY NOTICE

THE INFORMATION CONTAINED HEREIN IS CONSIDERED CONFIDENTIAL AND PROPRIETARY, PRODUCED SOLELY FOR THE CUSTOMER IDENTIFIED ABOVE.

This Statement of Work ("SOW") is proprietary to ConvergeOne, Inc. and contains ConvergeOne, Inc. Confidential Information. It may not be disclosed in whole or in part without the express written authorization of ConvergeOne. No portion of this SOW may be duplicated or used for any purpose other than to receive Services or deliverables from ConvergeOne described herein.

2. SCOPE OF WORK - TERMS AND CONDITIONS

This Statement of Work or Scope of Work ("SOW") and the applicable Solution Summary (and any documents attached thereto and incorporated therein by reference) (collectively, this "Order") is subject to the following terms and conditions **DIR-TSO-4167 is the contract vehicle** (i) the Master Sales Agreement or other applicable master agreement in effect as of the date hereof between ConvergeOne, Inc. and/or its subsidiaries and affiliates (collectively, "ConvergeOne" or "Seller") and Williamson County ("Customer"); or (ii) if no such master agreement is currently in place between ConvergeOne and Customer, the Online General Terms and Conditions currently found on the internet at: <https://www.convergeone.com/online-general-terms-and-conditions/>. If Customer's Agreement is a master agreement entered into with one of ConvergeOne, Inc.'s predecessors, affiliates and/or subsidiaries, ("Legacy Master Agreement"), the terms and conditions of such Legacy Master Agreement shall apply to this Order, subject to any modifications located at <https://www.convergeone.com/online-general-terms-and-conditions/>. In the event of a conflict between the terms and conditions in the Agreement and this Order, the order of precedence shall be as follows: (i) this Order (with the most recent and specific document controlling if there are conflicts between the Solution Summary, this SOW and any other applicable supporting document(s) incorporated into this Order), (ii) Attachment A to the Agreement (if applicable), and (iii) the main body of the Agreement.

Customer's signature on this Order (or Customer's issuance of a purchase order in connection with this Order) shall represent Customer's agreement with each document in this Order.

This Order may include the sales of any of the following to Customer: (a) any hardware, third party software, and/or Seller software (collectively, "Products"); any installation services, professional services, and/or third party provided support services that are generally associated with the Products and sold to customers by Seller ("Professional Services"); any Seller-provided vendor management services, software release management services, remote monitoring services and/or, troubleshooting services (collectively, "Managed Services"); and/or any Seller-provided maintenance services ordered by Customer to maintain and service Supported Products or Supported Systems at Supported Sites to ensure that they operate in conformance with their respective documentation and specifications

("Maintenance Services"). For ease of reference only, Professional Services, Managed Services and Maintenance Services may be referred to collectively as "Services." Unless otherwise defined herein, capitalized terms used herein will have the same meanings as set forth in the Agreement.

Any dates and/or time intervals listed in this Order are approximate and for planning purposes only. ConvergeOne will use commercially reasonable efforts to accommodate any requested dates; provided however, projects milestones will be fully discussed and mutually agreed upon between ConvergeOne and Customer after project kickoff.

Products and/or Services not specifically itemized are not provided herein. Any additional applications, technologies, integrations, or other Products and/or Services not specified herein, are not included in this SOW, and may result in additional charges at any time during the project.

Unless signed, this Order will be valid for a period of thirty (30) days following the date hereof. Thereafter, this Order will no longer be of any force and effect.

The outline of deliverables for this Order follows below.

3. PROJECT TIMELINE EXPECTATIONS

Approximately 5 business days after signed acceptance of this SOW, ConvergeOne will assign a project manager that will make contact and start planning a project kick-off meeting. The project kick-off may not take place immediately. Project start times depend on the availability of ConvergeOne and Customer resources.

The expected duration of this project has been budgeted at two (2) weeks from the time of kick-off to completion. If the project exceeds this timeframe, a project change order may be required to extend the engagement, resulting in additional fees.

4. PROJECT OVERVIEW

Thank you for the opportunity to work with you on the Routing Change Services project. This document describes the work to be performed during this engagement and covers the assumptions as the basis for this agreement, the responsibilities of ConvergeOne personnel, and the responsibilities of the Customer.

4.1. Project Location(s)

Below is a list of the location(s) that should be included in this project.

Table 4-1

Site Name	Site Address
-----------	--------------

5. PROJECT SCOPE OF SERVICES

This section identifies the work that will be performed as part of this project. Below is an initial, high-level list of tasks and assumptions for the project. This schedule may change depending on the Customer's business requirements and other factors. Also, depending on the schedule finally agreed upon at the kickoff meeting, the days worked may not be contiguous. ConvergeOne will conduct a meeting with the Customer to review and finalize the technical approach, constraints and project schedule. This meeting is intended to ensure that all parties are working with consistent expectations for the project.

5.1. Enterprise Networking

Migrate Existing Layer 3 Devices from EIGRP to OSPF

The purpose of this project is to migrate the existing customer's network from EIGRP to OSPF as their routing protocol. The current mix of layer 3 devices at multiple locations includes:

- Cisco 4500 switches
- Cisco 4300 and 4400 routers
- Palo Alto 3220 and 820 firewalls
- Meraki MX60 appliances

The customer would like to migrate to OSPF in order to enable better interoperability with non-Cisco network devices that do not support EIGRP. A current running configuration and network topology diagram have been provided by the customer.

Converge One will assign a network consultant to perform the required tasks on this project. Ideally, the new OSPF settings can be implemented in parallel with the existing EIGRP configuration using a higher administrative distance in order to facilitate the migration to OSPF on a short outage window.

Below are the required tasks that the consultant will complete across this project.

Enterprise Networking Custom Tasks

- Perform initial configuration discovery of the following:
 - Cisco 4500x-16 core switches.
 - Cisco 4300 and 4400 ISR routers.
 - Palo Alto 3220 and 820 firewalls.
 - Meraki MX60 appliances.

- Review current EIGRP routing configuration in preparation for the OSPF migration.
- Create a new OSPF routing design for the network, considering current EIGRP implementation and the possibility to run both protocols at the same time until cutover using different administrative distances.
- The consultant will carefully make the necessary network/routing configuration changes on the devices within scope of this project.
- Perform after-hours cutover from EIGRP routing to OSPF routing.
- The consultant will create and/or update any existing network topology documentation to reflect the new routing changes.
- The consultant will host a two (2) hour knowledge transfer session with the assigned customer's network engineer(s).

6. PROJECT MANAGEMENT

ConvergeOne will provide Project Management Services to help you effectively manage the project and control risks in the deployment. ConvergeOne will designate a Project Manager who will act as the single point of accountability for all ConvergeOne contract deliverables for the duration of the Project. ConvergeOne follows the Project Management Body of Knowledge (PMBOK) for project delivery. The PMBOK is an adaptable approach that enables technology project success by aligning business and technology goals. Key elements include an iterative delivery process, clear project metrics, proactive risk management, and effective response to change.

6.1. Project Manager

ConvergeOne will designate a Project Manager (PM) responsible for overseeing the project. Once the contract is signed and accepted by ConvergeOne, this individual will act as the Customer's single point of contact for all planning and issues related to solution delivery. The ConvergeOne PM will work closely with the Customer to guide the implementation and work on a mutually agreed-upon schedule. The ConvergeOne Project Manager is responsible for the following:

- Conduct internal (ConvergeOne) and joint ConvergeOne/Customer meetings.
- Develop a project plan, including activities, milestones, roles, and responsibilities.
- Schedule and manage required ConvergeOne resources and partners.
- Conduct Issue and Risk Management.
- Provide agenda and meeting notes.
- Track Customer and ConvergeOne project deliverables.
- Manage change orders and any associated billing with the Customer.

- Manage project closeout process, punch list, and Customer acceptance.

7. CHANGE ORDER PROCESS

Despite good project planning, design, and review, project plans often require some degree of change at some point. These changes are handled using change order requests, which must be agreed upon by all parties to the contract before such work can be performed.

Either ConvergeOne or the Customer may initiate a change order for any deliverable, work requirement, assumption, or dependency that is part of the project. All requests must be in writing and handled by the ConvergeOne Project Manager. ConvergeOne will review the change and provide pricing as applicable before proceeding. The ConvergeOne Project Manager may also engage project team members to assess the impact of the change. Agreed changes must be approved in writing by an authorized representative of the Customer, via email, or modified purchase order.

8. MILESTONE AND/OR PROJECT ACCEPTANCE

Upon completion of the services described in this SOW, ConvergeOne shall provide Customer with an Acceptance Form. Upon delivery of the Acceptance Form, Customer has five (5) working days to review and accept. Failure to respond within the designated five (5) day period, signifies the completion of the milestone or project. To refuse acceptance, Customer must both indicate non-acceptance with written notification to ConvergeOne within the five (5) day period noted above and describe why it was not accepted. ConvergeOne shall have up to ten (10) days after the receipt of such notice to correct the error given it is within ConvergeOne scope and control to do so. The period to correct the error may be extended by mutual consent.

9. CUSTOMER RESPONSIBILITIES

9.1. Provide a single point of contact that will be responsible for:

- Understanding the business process impact and technical requirements and who has the authority to make binding decisions on Customer's behalf.
- Working with ConvergeOne Project Manager to develop mutually agreed project schedule, including outside of Normal Business Hours test and cutover windows (if applicable).
- Ensuring all Customer responsibilities are completed in accordance with the project schedule.
- Reasonable notification of schedule and changes for the installation work.

- Attending all project status meetings.

9.2. Site Preparation:

- Ensure equipment room is ready, including all electrical, wiring, grounding, lighting, racks, and HVAC required to maintain equipment within operating conditions specified by the equipment manufacturer.
- Ensure that existing Customer network is configured, connected, and operating within the manufacturer's specifications.
- Customer will provide QOS on all their network equipment to the WAN-based upon Supplier's guidelines and requirements if carrying voice.
- Customer will provide remote access to all network devices within the scope of this project.
- Customer will provide an appropriate cutover window for the routing protocol migration.

9.3. Ensure availability of appropriate Customer resources that will:

- Assist in the development and execution of applicable test plans.
- Provide accurate documentation for all existing systems and networks.
- Provide all necessary IP addresses, subnet masks, and default gateways.
- Provide a qualified Network Administrator with working knowledge of Customer requirements.
- Provide information on planned changes in the network.

10. PROFESSIONAL SERVICES ASSUMPTIONS

The following assumptions were made to create this Statement of Work. Should any of these assumptions prove to be incorrect or incomplete then ConvergeOne may modify the price, scope of work, or milestones. Any such modifications shall be managed by the Change Order Procedure.

10.1. General Assumptions

- All non-service impacting work described in this scope will be performed during U.S. normal business hours defined as 8:00 AM to 5:00 PM local time; Monday through Friday, excluding ConvergeOne designated holidays. "Cutover" for the sites will be completed during business hours unless otherwise stated in this scope of work.
- The Customer must identify any specific requirements for maintenance windows and change control. The Customer retains overall responsibility for any business process impact and any Customer-internal change management procedures and communications.

- ConvergeOne will install specific software versions agreed upon at the time of project kickoff. Upgrades to the software are not included in the SOW. ConvergeOne may choose to install an upgrade if required by the manufacturer or to resolve a problem.
- The Customer is responsible for the underlying data infrastructure including network and virtualization. Systems must be capable of supporting the proposed solution. ConvergeOne can supply consulting and remediation services to ensure successful implementation, if not included in this scope, through a change order and billed at an additional fee.
- The Customer is responsible for all communications and scheduling of any contractors or vendors not managed by the ConvergeOne Project Manager.
- Any product or service delivery dates communicated outside of this SOW or the Project Plan, are not to be considered valid or binding.
- If the project extends beyond the timeline specified in the Project Plan due to delays caused by parties other than ConvergeOne and its subcontractors, ConvergeOne may invoice for service performed to date.
- The Customer is responsible to verify and arrange the installation of all applicable network connections and provide a functional network for application deployment.
- Projects requiring multiple site visits and/or intervals of inactivity between events must be noted as such prior to acceptance of this SOW.
- The Customer is responsible to notify ConvergeOne if the site requires any specialized access for personnel and/or Union trades for any tasks associated with this SOW. Notification of requirements must take place prior to the quote. Any and all additional costs for post-quote changes or additional site restrictions requiring specialized training or Union Labor shall be chargeable to the Customer.
- The Customer is responsible for managing all 3rd Parties not outlined in this SOW.
- Services not specifically called out in this SOW will be deemed out of scope.
- VPN access will be provided to ConvergeOne resources to allow for work to be accomplished remotely when applicable. If unfettered remote access to the Customer network cannot be provided, additional charges will be required.

10.2. Technical Assumptions

- Unless specifically called out, above, no IP address changes are included in the SOW. If requested, additional charges may apply.
- The Customer is responsible to have current licensing, maintenance, and support on the components of the servers, database, storage, and network infrastructure including hardware, software (including operating systems), and any associated costs.

- The Customer is responsible for any operating system patches and anti-virus software installation and support.
- The Customer is responsible to ensure the existing network is free of layer 3 protocol and broadcast errors.
- The Customer is responsible for the cost and acquisition of any 3rd party security certificates necessary for successful deployment. ConvergeOne can provide services for Security Audits and Certificate deployment which can be billed at an additional fee.
- The Customer is responsible for resolving interoperability issues with other vendors not acting as a sub-contractor to ConvergeOne.
- The Customer is responsible for any firmware updates to re-used circuit packs, media modules, or cards not specifically identified within this SOW. ConvergeOne can provide services for the firmware updates through a change order and billed at an additional fee.

11. PROFESSIONAL SERVICES PRICING AND BILLING SCHEDULE

Billing terms for this project supersede any MSA in place and are only applicable to the services stated in this scope of work. **Invoices are due within thirty (30) days from the date of the Williamson County Auditor receipt of an invoice.** Any change to the Project Pricing and Payment schedule will be managed through the Change Order procedures specified herein. All stated prices are exclusive of any taxes, fees and duties or other amounts, however designated, and including without limitation value added and withholding taxes which are levied or based upon such charges, or upon this SOW (other than taxes based on the net income of ConvergeOne). The Customer shall pay any taxes related to services purchased or licensed pursuant to this SOW or the Customer shall present an exemption certificate acceptable to the taxing authorities. Applicable taxes shall be billed as a separate item on the invoice.

11.1. Project Price and Milestone Billing Schedule

The fixed fee price for this services engagement is below and will be billed with the following milestone schedule:

Total Price: \$9,249.00

- Milestone 1 (100%) - Final Customer Acceptance of the Project

11.2. Project Expenses:

There are no anticipated project related expenses expected for this project above the price included in this SOW. In the event that the need for additional expense arise, a Change Order will be presented by the Project Manager for approval by the Customer in advance. ConvergeOne

will make reasonable effort to minimize expenses and will ensure sufficient time is built into the project schedule to maximize efficiency when scheduling site visits.


Texas Prompt Payment Act Compliance: Payment for goods and services shall be governed by Chapter 2251 of the Texas Government Code. An invoice shall be deemed overdue the 31st day after the later of (1) the date Customer receives the goods under the contract; (2) the date the performance of the service under the contract is completed; or (3) the date the Williamson County Auditor receives an invoice for the goods or services. Interest charges for any overdue payments shall be paid by Customer in accordance with Texas Government Code Section 2251.025. More specifically, the rate of interest that shall accrue on a late payment is the rate in effect on September 1 of Customer's fiscal year in which the payment becomes due. The said rate in effect on September 1 shall be equal to the sum of one percent (1%); and (2) the prime rate published in the Wall Street Journal on the first day of July of the preceding fiscal year that does not fall on a Saturday or Sunday.

Right to Audit: ConvergeOne agrees that the Customer or its duly authorized representatives shall, until the expiration of three (3) years after final payment under this Contract, have access to and the right to examine and photocopy any and all books, documents, papers and records of ConvergeOne which are directly pertinent to the services to be performed under this Contract for the purposes of making audits, examinations, excerpts, and transcriptions. ConvergeOne agrees that the Customer shall have access during normal working hours to all necessary ConvergeOne facilities and shall be provided adequate and appropriate workspace in order to conduct audits in compliance with the provisions of this section. The Customer shall give ConvergeOne reasonable advance notice of intended audits.

12. CUSTOMER AUTHORIZATION TO PROCEED

The use of signatures on this SOW is to ensure agreement and understanding on project objectives and assumptions, and the work and deliverables to be performed by ConvergeOne. By signing below, the duly authorized Customer representative signifies their commitment to proceed with the project as described in this SOW.

Customer's Authorized Representative:


Bill Gravell (May 12, 2022 10:18 CDT)

Signature

Bill Gravell

Printed Name

County Judge

Title

May 12, 2022

Date

PO Number
