Ramsey WTP

75% Schedule (5/9/22)

ID	Task Name	Start	Finish	Duration	Predecessors
0	**Ramsey WTP**	**Thu 7/22/21**	**Thu 2/15/24**	**675 days**	
1	**Project Initiation**	**Thu 7/22/21**	**Wed 9/29/21**	**50 days**	
2	Contracts Signed	Wed 9/29/21	Wed 9/29/21	0 days	
3	**Preliminary Design Phase**	**Wed 8/18/21**	**Fri 10/15/21**	**43 days**	
4	**WTP Tours & Campus Layout WGMs**	Wed 8/18/21	Tue 8/31/21	10 days	
5	**Process & Controls WGMs**	Wed 8/18/21	Fri 9/10/21	18 days	
6	**Building Concept Approval WGM**	Fri 10/15/21	Fri 10/15/21	0 days	5
7	**Final Design Phase**	**Tue 10/26/21**	**Tue 7/12/22**	**189 days**	**5**
8	Spatial Design Meeting (All Disc.)	Tue 10/26/21	Tue 10/26/21	0 days	6
9	Development Review Meeting	Thu 12/9/21	Thu 12/9/21	0 days	8
10	Planning Commission Meeting	Thu 1/27/22	Thu 1/27/22	0 days	9
11	Public Works Committee Meeting	Tue 5/17/22	Tue 5/17/22	0 days	10
12	**95% Set Review**	**Tue 6/21/22**	**Thu 6/23/22**	**3 days**	**11**
13	**MDH Submittal**	Thu 6/30/22	Thu 6/30/22	1 day	
14	**Final Edits to Plans & Specs**	Fri 6/24/22	Thu 6/30/22	5 days	12
15	**Council Meeting**	Tue 7/12/22	Tue 7/12/22	0 days	14
16	**Bidding Phase**	**Wed 7/13/22**	**Tue 8/23/22**	**29 days**	**15**
17	**Send Request for Advertisement**	Wed 7/13/22	Wed 7/13/22	1 day	
18	**Advertise**	Fri 7/15/22	Fri 7/15/22	0 days	
19	**Advertise**	Fri 7/22/22	Fri 7/22/22	0 days	
20	**Bid Opening**	Mon 8/8/22	Mon 8/8/22	0 days	
21	**City Council Awards Bid**	Tue 8/23/22	Tue 8/23/22	0 days	
22	**Construction**	**Tue 8/30/22**	**Thu 2/15/24**	**383 days**	**21**
23	**Execute Construction Contract**	Tue 9/6/22	Wed 9/7/22	2 days	21
24	**Pre-Construction Meeting**	Tue 8/30/22	Tue 8/30/22	1 day	21
25	**Progress Meetings**	Tue 8/30/22	Thu 1/18/24	363 days	
26	**Substantial Completion**	Thu 2/15/24	Thu 2/15/24	0 days	25

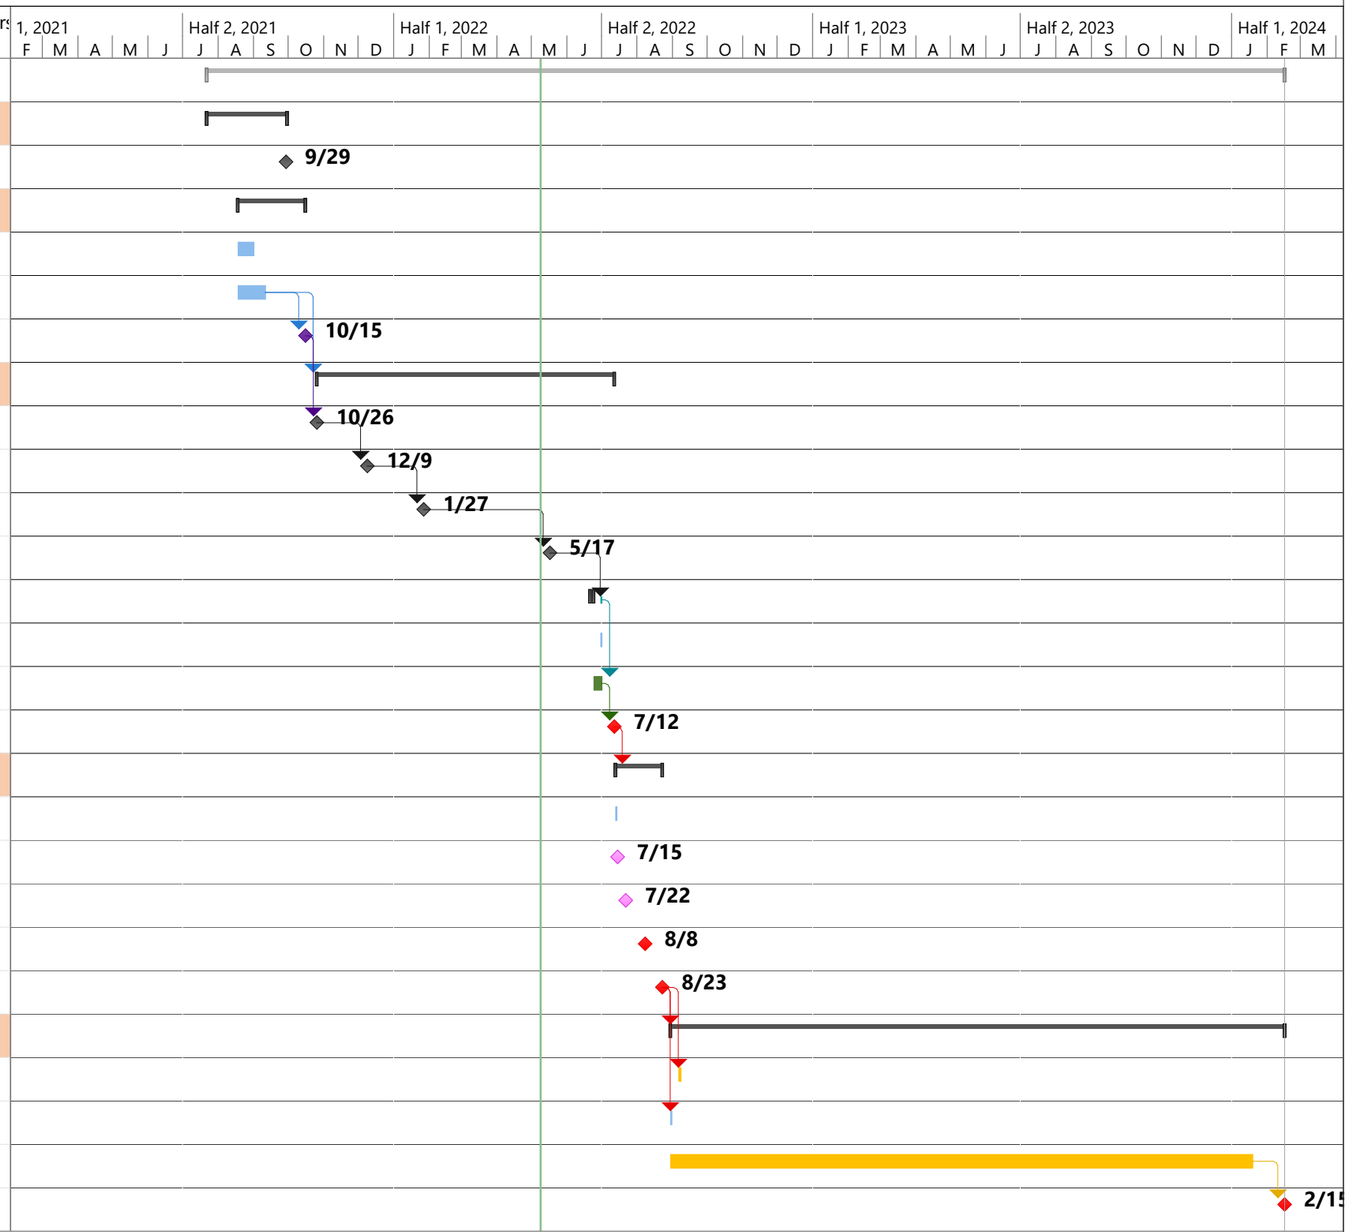

Project: Ramsey WTP
Date: Mon 5/9/22

Task	Project Summary	Manual Task	Start-only	Deadline
Split	Inactive Task	Duration-only	Finish-only	Progress
Milestone	Inactive Milestone	Manual Summary Rollup	External Tasks	Manual Progress
Summary	Inactive Summary	Manual Summary	External Milestone	
