





Beulah/University Realignment Project

3 December 2024



Beulah/University Realignment Project

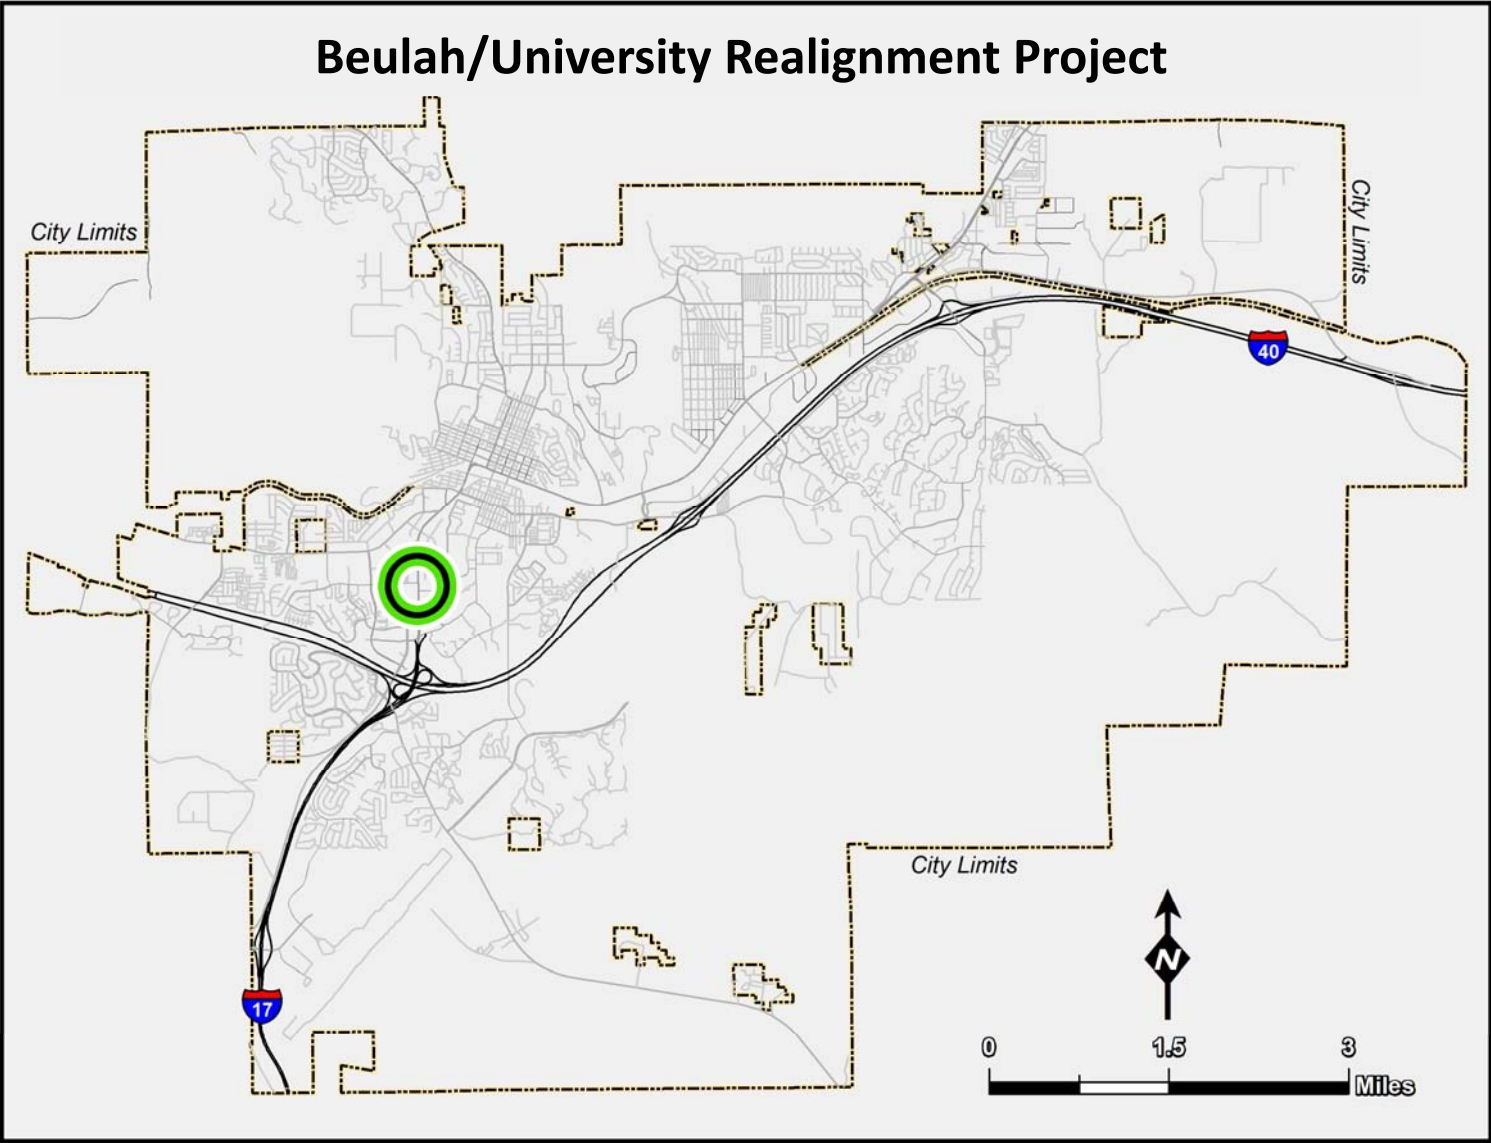

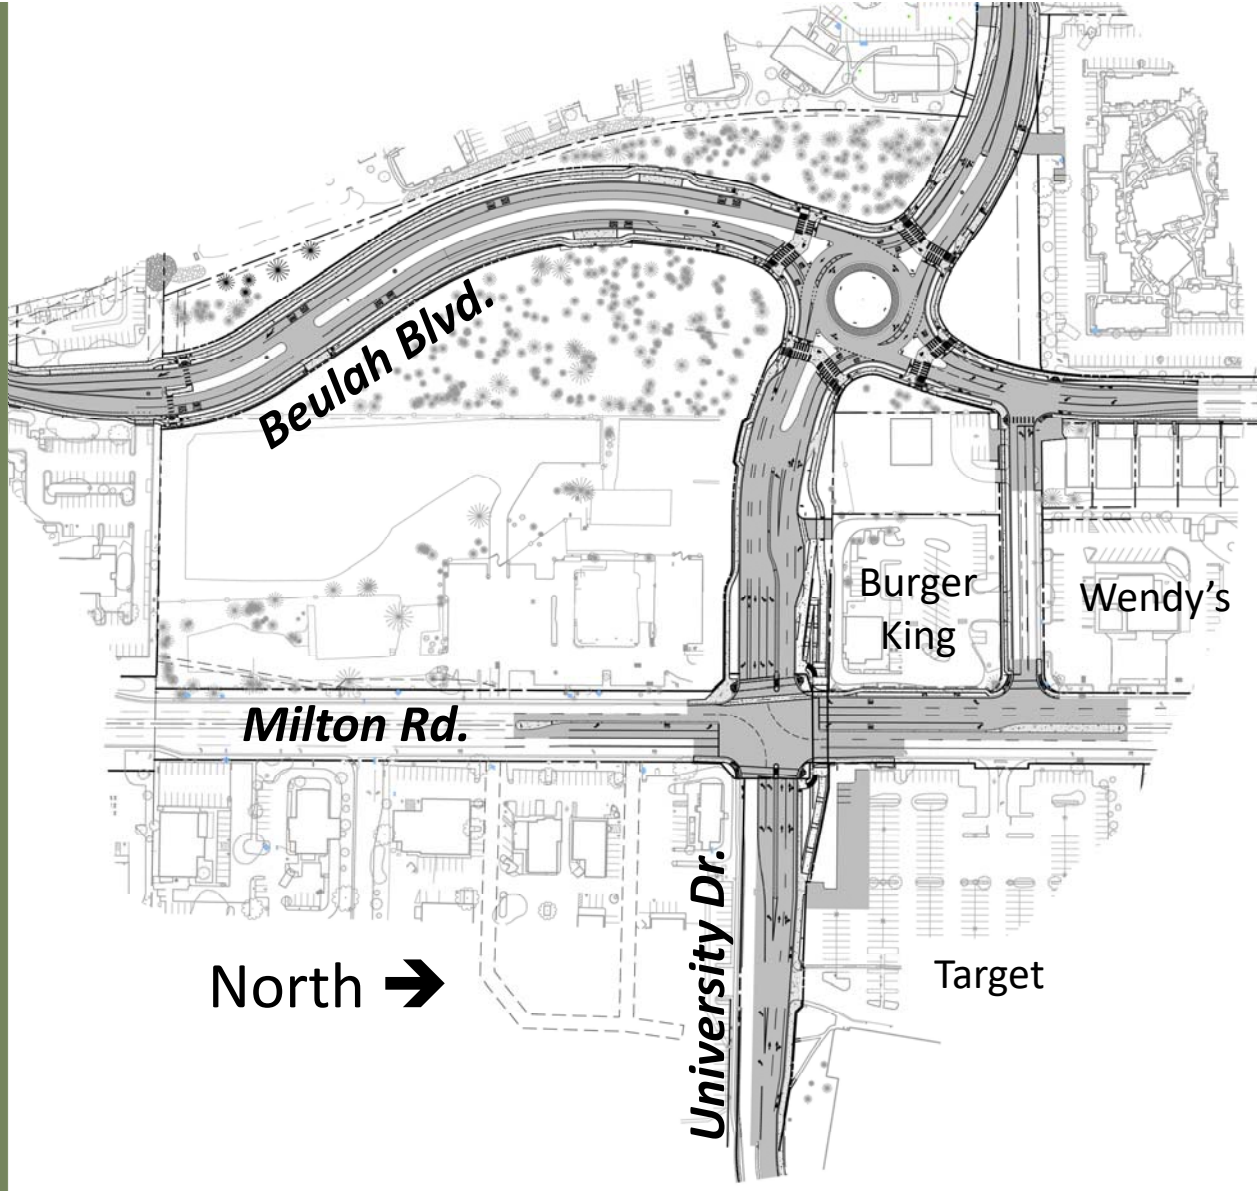

Beulah Blvd.

Milton Rd.

University Dr.

Burger King

Wendy's

Target

North →




Change Order 1



Scope of Work:

- Extend the Fiber Optic Conduit Network
 - Two – 4-Inch Conduits (~310 LF)
 - Communication Cabinet, Foundation and Gear
 - Fiber Optic Cable
 - Fiber Optic Splice Closure
- **Cost = \$94,107.73**
- **Time = 5 Calendar Days**

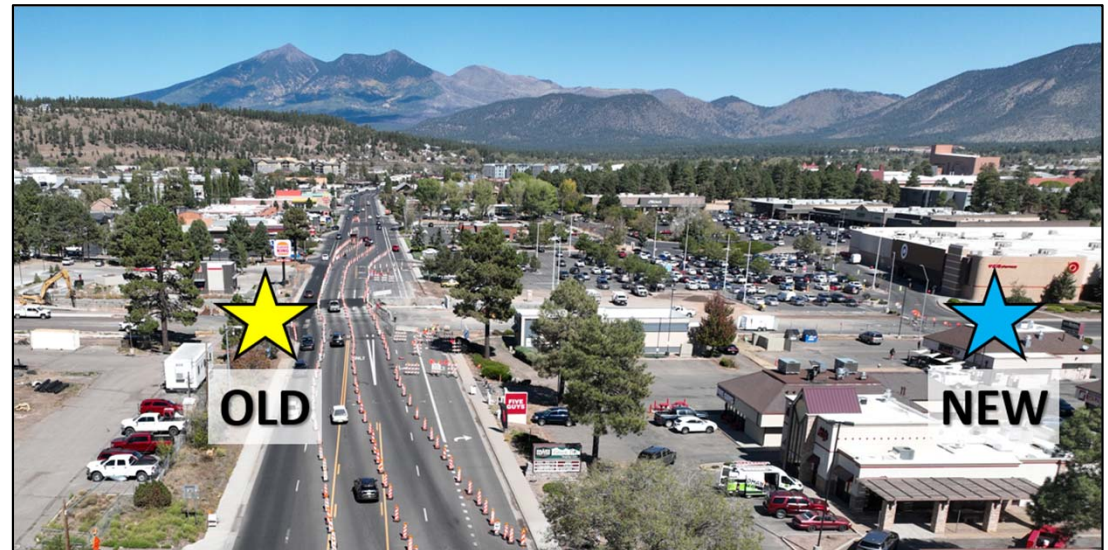



Change Order 2



Scope of Work:

Eight Components:

1. Wendy's southern driveway & paving of the remnant section of Fresquez Avenue
2. Correcting drainage along the western portion of University Avenue with added stormwater catch basins and sidewalk improvements
3. Modifying and raising Haven Health driveway ramp
4. Modification of sidewalk and Burger King driveway along Milton and ADA ramp modifications to match existing sidewalks to the new Milton sidewalk



Change Order 2



Scope of Work:

Eight Components:

5. Removal of two dead ponderosa trees
6. Temporary striping on the extended portion of Beulah Boulevard, the roundabout, Yale Street, and west University Avenue
7. Bollards and additional striping at Yale Street/Fresquez Avenue
8. Modifications to the stairs at multi-family complexes (Yale Street)

Cost = \$390,173.15

Time = 20 Calendar Days



Project Schedule



• **Winter 2024/2025**

- *All Four Lanes of Milton Re-Opened (until Spring 2025)*
- *New RAB and Beulah Extension Re-Opened (Not to Milton)*
- *Surface Ped Crossing on South Side of Milton/University Intersection*
- *Ramps, Stairs, Landscaping Walls on Entries to Tunnel*
- *Eastbound University Drive for NAU Graduation*

• **Spring 2025**

- *Permanent Pavement, New Medians, and Striping (Milton; Up to RAB)*

• **Summer/Fall 2025**

- *Finalize Project: Landscaping, Surface Improvements*



Progress



- **Based on Payments Paid**
 - *\$15,784,371 of \$19,403,441 or ~81%*
- **Based on Days of Contract**
 - *597 of 902 or ~66%*





Questions



Thank You

David Pedersen

Project Manager Senior Lead

Capital Improvements

dpedersen@flagstaffaz.gov

Office :: 928.213.2677



**Project
Website**



**Sign Up for
Weekly Updates!**



SCAN ME
