

2. Non-Exclusive Services of Engineer. Hidalgo County reserves the right to request these services from other sources other than the Engineer and shall not be in violation of any terms or conditions of this Agreement.

3. Term. This Agreement is for a period of **one (1) year**, effective October 13, 2016, and will expire October 13, 2017 or unless sooner terminated as provided herein. The Engineer will not begin to work or incur costs until authorized in writing by the County with each "Work Authorization" particularly described in Exhibit "D".

4. Compensation. As consideration for rendering the Services provided for in this Agreement, the County agrees to pay the Engineer the amounts specified in Exhibit "C" attached hereto payable against written invoice submitted by Engineer. The maximum amount payable under this Agreement shall not exceed the amount for each work authorization unless an amendment is executed as provided hereinafter. The Engineer shall submit periodic requests for payment within (30) thirty days after completion of each Work Authorization. The request for payment shall be made using forms acceptable to the County and shall show the total amount earned to the date of submission and the amount due and payable as of the date of the current billing. Upon receipt of said request for payment, County shall submit a requisition for payment for said Services in the customary manner provided for payments utilized by Hidalgo County, Texas. Engineer agrees to separately account for the receipt and/or expenditure of funds received pursuant to this Agreement and to keep accurate books and records of all such receipts and/or expenditures. All payments to Engineer shall be mailed to the address shown in numbered paragraph 24 herein.

5. Inspection of Work. The County has the right at all reasonable times to inspect or otherwise evaluate the work performed hereunder and the premises in which it is being performed. If any inspection or evaluation is made on the premises of the Engineer, or of a subcontractor, the Engineer shall provide and require its subcontractor to provide all reasonable facilities and assistance for the safety and convenience of the inspectors in the performance of their duties. All inspections and evaluations shall be performed in such a manner as will not unduly delay their work.

6. Amendments. If it becomes necessary at any time during this Agreement to change the scope of Services, the Agreement period, the maximum amount payable, the complexity, or the character of this Agreement, an amendment shall be executed by use of a (Supplemental Agreement Form) more particularly described in Exhibit "E" within the agreement. The County retains the right to reject any such amendment proposed by the Engineer. Any such amendments shall be made in writing, agreed to by all parties hereto, and duly executed before the end of the Agreement as specified. If the County finds it necessary to require changes in completed work because of errors made by the Engineer, the County shall require the Engineer to correct the work at no cost to the County and without amendment to the Agreement. If the changes are made at the request of the County and are not due to errors of the Engineer, the County will reimburse the Engineer for the additional work at the same rate of pay established in Exhibit "C," "Engineer's Rates." If payment for the additional work will cause the maximum amount payable under this Agreement to be exhausted, an amendment shall be proposed in accordance with all State procurement laws.

7. Reporting. The Engineer shall promptly advise the County in writing of events which have a significant impact upon the Agreement, including:

- a. Problems, delays, or adverse conditions which will materially affect the ability to meet time schedules and goals, or preclude the attainment of project work units by established time periods. This disclosure shall be accompanied by a statement of the action taken, or contemplated and any County or, if Federal Funds are involved, Federal assistance needed to resolve the situation.
- b. Favorable developments or events which enable meeting time schedules and goals to be met sooner than anticipated or which are producing more work units than originally projected.

8. Ownership of Documents. Upon completion or termination of this Agreement, all documents prepared by the Engineer or furnished to the Engineer by the County shall be delivered to and become the property of the County. All sketches, photographs, calculations, and other data prepared

under this Agreement shall be made available, upon request, to the County without restriction or limitation on their further use. The Engineer may, at its own expense, have copies made of the documents or any other data furnished to the County under this Agreement.

9. Suspension of Work. Should County desire to suspend the work under this Agreement, but not terminate this Agreement, the County shall provide thirty (30) calendar days verbal notification to Engineer, followed by written confirmation from the County to Engineer to that effect. The thirty-day notice may be waived as agreed in writing by both the County and Engineer to that effect. The work under this Agreement may be reinstated and resumed in full force and effect within sixty (60) days of receipt of written notice from the County to the Engineer. The sixty-day notice may be waived as agreed in writing by both the County and Engineer. If the County suspends the work, the Termination Date as identified above is not affected and this Agreement will terminate on the date specified.

10. Progress and Coordination. The Engineer shall, from time to time during the progress of the work, confer with the County. The Engineer shall prepare and present such information as may be pertinent and necessary, or as may be requested by the County, in order to evaluate features of the Engineer's services and work.

At the request of the County or the Engineer, conferences shall be provided at the Engineer's office, the offices of the County, or at other locations designated by the County. These conferences shall also include evaluation of the Engineer's services and work when requested by the County.

All applicable study reports shall be submitted in preliminary form for approval by the County before the final report is issued. The County's comments regarding the Engineer's preliminary report will be addressed by the Engineer in the final report.

If funds by other agencies or entities are to be used for the development of the project under this Agreement, the Engineer's Services and work will be subject to periodic review and approval by other agencies or entities, including those of the city, county, state and/or federal agencies.

Should it be determined that the progress in the production of the Engineer's Services and work does not satisfy the requirements of the approved Work Authorization as provided by Exhibit "D",

attached hereto, the County shall review the approved Work Authorization with the Engineer to determine the corrective action needed by either the County or the Engineer.

The Engineer shall promptly advise the County in writing of events which have a significant impact upon the progress of the Engineer's Services and work and the approved Work Schedule, including:

- a. problems, delays, adverse conditions which will materially affect the ability to attain Agreement objectives, prevent the meeting of time schedules and goals, or preclude the timely completion and submittal of Project deliverables by the Engineer within established time periods; this disclosure will be accompanied by a statement by the Engineer of recommended or immediate action taken, or contemplated, and any Owner or other agency or entity assistance needed to resolve the situation; and
- b. favorable developments or events which enable meeting the Work Schedule goals sooner than anticipated.

11. Independent Contractor. Engineer must comply with all applicable Hidalgo County policies and with any applicable federal, state or local laws, regulations, orders or ordinances applicable to the Services provided by Engineer under this Agreement. Notwithstanding the foregoing sentence, Engineer represents and maintains that it is an Independent Contractor and is not an employee of Hidalgo County, Texas or any agency thereof, and represents and warrants that it does not desire or request any fringe benefits provided to employees of Hidalgo County, Texas, and/or any agency thereof, including, but not limited to benefits associated with Hidalgo County's civil service program. Engineer agrees to be responsible for any federal income tax, withholding or social security tax liability that might arise from payments received hereunder.

12. Subcontracting and Assignment. The Engineer shall not assign subconsultant or transfer the Engineer's interest in this Agreement without the prior written consent of the County. The Engineer shall bind every subconsultant by written agreement to observe all the terms of this Agreement

to the extent that they may be applicable to each subconsultant. No subcontractor relieves the Engineer of any responsibilities under this Agreement.

13. Voluntary Termination. County may terminate this Agreement at any time for any reason or no reason at all upon giving thirty (30) days prior written notice to the Engineer.

14. Insurance. Engineer agrees to provide liability insurance covering its activities in providing the Services for County in an amount not less than the minimum amounts prescribed by the Texas Tort Claims Act, §100.001, et seq., Texas Civil Practices and Remedies Code, and shall furnish County a certificate issued by the insurer that such insurance is in full force and effect.

15. Payment of Franchise Tax. The Engineer hereby certifies that the Engineer is not delinquent in Texas franchise tax payments, or that the Engineer is exempt from, or not subject to, such tax. A false statement concerning corporation's franchise tax status shall constitute grounds for termination of the Agreement at the sole option of the County.

16. No Assignment. Except as otherwise herein provided, Engineer may not assign the obligations or rights under this Agreement to any person without the prior written consent of County.

17. Conflict. Nothing in this Agreement shall be construed so as to require the commission of any act contrary to law, and whenever there is any conflict between any provision of this Agreement and any present or future law, ordinance or administrative, executive or judicial regulation, order or decree, or amendment thereof, contrary to which the parties have no legal right to Agreement, the latter shall prevail, but in such event the affected provision or provisions of this Agreement shall be modified only to the extent necessary to bring them the legal requirements and only during the time such conflict exists.

18. Termination by County. If Engineer fails to deliver quality Services, fails to achieve the defined goals, outcomes, strategies and outputs required by County, or if Engineer fails to comply with any conditions in this Agreement, then County shall have the right to terminate this Agreement upon the giving of ten (10) days prior written notice to Engineer.

19. **No Waiver.** No waiver by County of any breach of any provision of this Agreement shall be deemed to be a waiver of any preceding or succeeding breach of the same or any other provision hereof.

20. **Entire Agreement.** This Agreement contains the entire agreement between the parties hereto, and each party acknowledges that neither has made (either directly or through any agent or representative) any representations or agreements in connection with this Agreement not specifically set forth herein. This Agreement may be modified or amended only by agreement in writing executed by County and Engineer, and not otherwise.

21. **Venue.** This Agreement shall be construed under and in accordance with the laws of the State of Texas, and all obligations of the parties created hereunder are performable in Hidalgo County, Texas. The parties hereby consent to personal jurisdiction in Hidalgo County, Texas.

22. **Hold Harmless.** In the event Engineer should cause, either directly or indirectly, damage, loss, destruction, liability, or claims against the other party as a result of intentional conduct, negligence or otherwise, Engineer shall hold harmless and indemnify County from any and all obligations, liabilities, cause of action, lawsuits, damages, and assessments, including legal fees, etc., that from the Engineer's intentional actions or negligence. This indemnification clause shall survive this Agreement and be enforceable as a separate agreement in the event its survival and enforcement becomes necessary.

23. **Attorney's Fees.** In the unlikely event that a dispute occurs which is litigated, or a cause of action in law or equity is filed concerning the operation, construction, interpretation, or enforcement of this Agreement, the losing party shall bear the cost of the attorney's fees incurred by the prevailing party and any and all costs applicable thereto, including, but not limited to, court costs, deposition fees, expert witness fees, out-of-pocket expenses and travel expenses which are incurred by the prevailing party.

24. **Notices.** Except as may be otherwise specifically provided in this Agreement, all notices, demands, requests or communications required or permitted hereunder shall be in writing and shall either be (i) personally delivered against a written receipt, or (ii) sent by a registered or certified mail, return

receipt requested, postage prepaid and addressed to the parties at the addresses set forth below, or at such other addresses as may have been theretofore specified by written notice delivered in accordance herewith:

If to County: **Hidalgo County Urban County**
Attn: Diana R. Serna, UCP Director
427 East Duranta Avenue, Suite 107
Alamo, Texas 78516

If to Engineer: **Lefevre Engineering & Management Consulting, LLC.**
Attn: Richard LeFevre, P.E. President
612 Nolana, Suite 520
Mc Allen, Texas 78504

Each notice, demand, request or communication which shall be delivered or mailed in the manner described above shall be deemed sufficiently given for all purposes at such time as it is personally delivered to the addresses or, if mailed at such time as it is deposited in the United States mail.

25. Executions of Documents. The parties hereto covenant and agree that they will execute such other and further instruments and documents as are or may become necessary or convenient to effectuate and carry out the terms of this Agreement.

26. Binding Agreement. This Agreement shall be binding upon and inure to the benefit of the parties hereto and their respective heirs, executors, administrators, legal representatives, successors, and assigns where permitted by this Agreement.

27. Gender. All pronouns used in this Agreement shall include the other gender, whether used in the masculine, feminine or neutral gender, and the singular shall include the plural whenever and as often as may be appropriate.

28. Authority. The execution and performance of this Agreement by County and Engineer have been duly authorized by all necessary laws, resolutions or corporate action, and this Agreement constitutes the valid and enforceable obligations of County and Engineer in accordance with its terms.

29. Professional Seal. All documents and data furnished by the Engineer to the County shall bear Professional seal of a licensed Engineer employed by the Engineer.

30. Commitment of Current Revenues Only. In the event that, during any term hereof, the Commissioners Court does not appropriate sufficient funds to meet the obligations of County under this Agreement, County may terminate this Agreement upon ninety (90) days written notice to the Engineer. County agrees, however, to use reasonable efforts to secure funds necessary for the continued performance of this Agreement. The parties intend this provision to be a continuing right to terminate this Agreement at the expiration of each budget period of County pursuant to the provisions of Tex. Loc. Govt. Code Ann. ' 271.903 (Vernon Supp. 1996).

31. Immunities. Nothing in this Agreement is intended to and County does not hereby waive, release or relinquish any right to assert any of the defenses County enjoys by virtue of the state or federal constitution, laws, rules or regulations, and any sovereign, official or qualified immunity available to County as to any claim or action of any person, entity, or individual against County.

EXECUTED as of the day and year first written above.

HIDALGO COUNTY

By: _____
Ramon Garcia, County Judge

ATTEST:

Arturo Guajardo Jr., County Clerk

Approved by Commissioners' Court on: October 13, 2016.

ENGINEER:
LeFevre Engineering & Management Consulting, LLC.

By: _____

Printed Name Richard Lefevre P.E.

Title: Owner

APPROVED AS TO FORM:

Atlas, Hall & Rodriguez, L.L.P.

By: Stephen L. Crain, Attorney

On this: July 12, 2016.

ATTACHMENTS:

- EXHIBIT A** -Scope of Services to be provided by the County
- EXHIBIT B** -Scope of Services to be provided by the Engineer
- EXHIBIT C** -Engineer's Rates
- EXHIBIT D** -Work Authorization Form
- EXHIBIT E** -Supplemental Agreement Form
- EXHIBIT F** -Certificates of Insurance

EXHIBIT A

-Scope of Services to be provided by the County

The following provides an outline of the services to be provided by the Owner in the development of Projects (as defined and more particularly identified in Exhibit "A" attached to this Agreement).

General:

The Owner will provide to the Engineer the following:

- 1) Provide the authorization to proceed with services through coordination with the project consulting and design Engineer.
- 2) Payment for work performed by the Engineer and accepted by the Owner in accordance with Article 3 of this Agreement.
- 3) Assistance to the Engineer, as necessary, to obtain the required data and information from other local, regional, State and Federal agencies the Engineer cannot easily obtain.
- 4) Provide any available relevant data the Owner may have on file concerning the projects.
- 5) Provide timely review and decisions in response to the Engineer's request for information and/or required submittals and deliverables, in order for the Engineer to maintain the agreed upon work schedule prepared in accordance with Exhibit "A" attached to this Agreement.
- 6) Attend and participate in progress meetings as required and as coordinated and conducted by Engineer.
- 7) Provide the authorization to proceed with services on project by project basis through consulting design and construction Engineer.

EXHIBIT B

-Scope of Services to be provided by the Engineer

Urban County Program – City of Penitas – Sidewalks Project

LeFEVRE ENGINEERING & MANAGEMENT CONSULTING, LLC. (LEMC)

The County of Hidalgo, Texas, Urban County Program on behalf of the City of Penitas proposes to the reconstruction of sidewalks along S. Main Street to include but not limited to, adjacent abutting streets within the same general vicinity.

Contract Amount: \$7,500.00

Task 1 – Survey & Geotechnical

Necessary field information will be developed by field surveys. Record plans will be issued as a guide for the survey work and for the analysis of design alternatives. Conduct Geotechnical Services including bores for Geotechnical Report with recommendations with regards to asphalt construction.

Task 2 – Project Orientation and Startup

LEMC proposes an initial project orientation meeting be scheduled so that both the County and the engineer may have a clear understanding of the design and construction process, parameters to be used and the final product desired.

Task 3 – Design

LEMC will assure that improvements are designed and incorporated in the plans are adequate for the area, Hidalgo County requirements.

Task 4 – Preliminary Plans and Estimates

LEMC will provide County staff a set of plans and estimates for accordance, evaluation and coordination.

Task 5 – Final Plans and Specifications

Final plans, specifications and estimates will be prepared during this task. The output of this task will be the documents necessary for bidding and constructing the project.

Task 6 – Bidding and Award

A pre-bid meeting will be scheduled if necessary in order to brief potential bidders and suppliers on the project. Necessary clarifications or addendum will be issued. LEMC will attend the bid opening and assist as the County desires.

Task 7 – Construction, Inspection, and Material Testing

LEMC will periodically observe ongoing work, identify survey control for the contractor (Construction Staking not included) and assist the County with certifying periodic payment requests. Upon completion by the contractor, a final inspection will be scheduled with the contractor and County staff. The outcome of these final inspections will be a Certificate of completion or a punch list of items for the contractor to complete, prior to issuance of a Certificate of Completion. Upon completion of the project LEMC will provide Record Drawings ("As-Builts"). Material Testing will be including and testing will be performed with regards to specifications and plans for proctors and cores required for evaluation of asphalt parking lot and subsurface compaction.

EXHIBIT C

-Engineer Contract Rates

Urban County Program – City of Penitas – Sidewalks Project

Engineering Cost Proposal and Fee Breakdown

Basic Engineering	\$2,800.00
Inspection	\$1,200.00
Construction Administration	\$1,500.00
Survey Topography	\$1,000.00
Geotech & Material Testing	\$1,000.00
Total	\$7,500.00

	Hourly Fees
PRINCIPAL	\$200.00/HOUR
PROJECT ENGINEER	\$175.00/HOUR
PROJECT MANAGER	\$130.00/HOUR
DESIGNER/TECHNICIAN	\$ 85.00/HOUR
ADMINISTRATIVE	\$ 65.00/HOUR
INSPECTOR/PROJECT REPRESENTATIVE	\$ 75.00/HOUR

*Reimbursables, Materials, and Travel are incorporated into hourly fees for individuals and will not be requested for this project.

September 30, 2016

Submitted to:

Diana R. Serna
Director
c/o Urban County Program

Re: Best and Final Offer – Urban County Program – City of Penitas – Sidewalk Project

Ms. Serna:


As requested, please find the enclosed Best and Final Offer (BAFO) submitted by LeFevre Engineering & Management Consulting, LLC on the proposed rates submitted as set forth below in connection to the above referenced project.

Engineering Cost Proposal and Fee Breakdown by:	
LeFevre Engineering & Management Consulting, LLC	
Survey/Topography	\$ 1,000
Basic Engineering	\$ 2,800
Construction Administration	\$ 1,500
Inspection	\$ 1,200
Geotech & Material Testing	\$ 1,000
Total	\$ 7,500

The above price does not include survey for acquisition of any and all easements required for construction of this project. The survey included in pricing is only to be used for engineering requirements and NOT for acquisition of properties, property disputes, etc. Any survey to be used for acquisition of properties, boundary searches, etc., that will need a registered land surveyor will need to be added as additional services or provided by others.

Please call me if you should have any questions at (956) 687-5362.

Respectfully yours,



Richard LeFevre, P.E.
President

CC: \\server\lemc\5 Projects\Hidalgo\Penitas\Contract\Sidewalk\BAFO - Penitas-Sidewalk- FINAL.docx

EXHIBIT D
-Work Authorization Form

HIDALGO COUNTY
Professional Engineering Services

WORK AUTHORIZATION NO. 1

THIS WORK AUTHORIZATION is made pursuant to the terms and conditions of Section I.A. of the Agreement made by and between **HIDALGO COUNTY**, action herein by and through the **Commissioner's Court**, hereinafter called the "**Owner**," and, **Lefevre Engineering & Management Consulting, LLC** professional engineers of **Mc Allen,** Texas, hereinafter called "**Engineer**".

PART 1. SCOPE OF WORK

The purpose of this Work Authorization is for the "engineering services" to provide **Professional Engineering Services**.

The scope of services to be provided by the **Owner** is identified in **EXHIBIT "A" – Scope of Services to be provided by the Owner** attached hereto.

The scope of services to be provided by the **Engineer** is identified in **EXHIBIT "B" – Scope of Services to be provided by the Engineer** attached hereto.

PART 2. ESTIMATED COST

The estimated cost for services under this Work Authorization is **\$7,500.00**. This amount is based upon the costs outlined in the **Estimated Cost Proposal** attached hereto as **EXHIBIT "D"**.

PART 3. PAYMENT

Compensation and payment to the **Engineer** for the services established under this Work Authorization shall be made in accordance with Article/Part/Section **4** of the Agreement.

PART 4. FUNDING

This Work Authorization No. **1** shall be funded through funding source:

Account No. 5016-60-0312-5000-6000-UCP-GVG

Purchase Order Number _____ **(MUST BE INCLUDED AFTER CC APPROVAL)**

PART 5. PERIOD OF SERVICE

This Work Authorization shall become effective on the date of final acceptance of the parties hereto, and terminate **upon completion of scopes of the work authorization**.

PART 6. RESPONSIBILITIES AND OBLIGATIONS

This Authorization does not waive the parties' responsibilities and obligations provided under the **Agreement**.

PART 7. ACKNOWLEDGEMENT AND CONFIRMATION

Acknowledgement and Confirmation by Hidalgo County Urban County Program, Diana Serna (Director) as to content and detail of this **Work Authorization No. 1** .

**HIDALGO COUNTY
URBAN COUNTY PROGRAM**

BY: _____
Diana R. Serna, Director

PART 8. ACCEPTANCE AND APPROVAL

This Work Authorization is hereby accepted, approved by Hidalgo County Commissioners' Court on October 13, 2016 as indicated below and effective as of 13th day of October, 2016 .

**THE ENGINEER:
LEFEVRE ENGINEERING & MANAGEMENT
CONSULTING, LLC.**

**THE OWNER:
HIDALGO COUNTY**

By: Richard Lefevre P.E Owner

By: Ramon Garcia, County Judge

ATTEST:

Arturo Guajardo Jr., County Clerk

EXHIBIT A

-Scope of Services to be provided by the County

The following provides an outline of the services to be provided by the Owner in the development of Projects (as defined and more particularly identified in Exhibit "A" attached to this Agreement).

General:

The Owner will provide to the Engineer the following:

- 1) Provide the authorization to proceed with services through coordination with the project consulting and design Engineer.
- 2) Payment for work performed by the Engineer and accepted by the Owner in accordance with Article 3 of this Agreement.
- 3) Assistance to the Engineer, as necessary, to obtain the required data and information from other local, regional, State and Federal agencies the Engineer cannot easily obtain.
- 4) Provide any available relevant data the Owner may have on file concerning the projects.
- 5) Provide timely review and decisions in response to the Engineer's request for information and/or required submittals and deliverables, in order for the Engineer to maintain the agreed upon work schedule prepared in accordance with Exhibit "A" attached to this Agreement.
- 6) Attend and participate in progress meetings as required and as coordinated and conducted by Engineer.
- 7) Provide the authorization to proceed with services on project by project basis through consulting design and construction Engineer.

EXHIBIT B

-Scope of Services to be provided by the Engineer

Urban County Program – City of Penitas – Sidewalks Project

LeFEVRE ENGINEERING & MANAGEMENT CONSULTING, LLC. (LEMC)

The County of Hidalgo, Texas, Urban County Program on behalf of the City of Penitas proposes to the reconstruction of sidewalks along S. Main Street to include but not limited to, adjacent abutting streets within the same general vicinity.

Contract Amount: \$7,500.00

Task 1 – Survey & Geotechnical

Necessary field information will be developed by field surveys. Record plans will be issued as a guide for the survey work and for the analysis of design alternatives. Conduct Geotechnical Services including bores for Geotechnical Report with recommendations with regards to asphalt construction.

Task 2 – Project Orientation and Startup

LEMC proposes an initial project orientation meeting be scheduled so that both the County and the engineer may have a clear understanding of the design and construction process, parameters to be used and the final product desired.

Task 3 – Design

LEMC will assure that improvements are designed and incorporated in the plans are adequate for the area, Hidalgo County requirements.

Task 4 – Preliminary Plans and Estimates

LEMC will provide County staff a set of plans and estimates for accordance, evaluation and coordination.

Task 5 – Final Plans and Specifications

Final plans, specifications and estimates will be prepared during this task. The output of this task will be the documents necessary for bidding and constructing the project.

Task 6 – Bidding and Award


A pre-bid meeting will be scheduled if necessary in order to brief potential bidders and suppliers on the project. Necessary clarifications or addendum will be issued. LEMC will attend the bid opening and assist as the County desires.

Task 7 – Construction, Inspection, and Material Testing

LEMC will periodically observe ongoing work, identify survey control for the contractor (Construction Staking not included) and assist the County with certifying periodic payment requests. Upon completion by the contractor, a final inspection will be scheduled with the contractor and County staff. The outcome of these final inspections will be a Certificate of completion or a punch list of items for the contractor to complete, prior to issuance of a Certificate of Completion. Upon completion of the project LEMC will provide Record Drawings (“As-Builts”). Material Testing will be including and testing will be performed with regards to specifications and plans for proctors and cores required for evaluation of asphalt parking lot and subsurface compaction.


CITY OF PENITAS - SIDEWALK IMPROVEMENT PROJECT
EXHIBIT C - Work Schedule

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	September	October	November	December	January
1	Project Start Up	7 days	Mon 10/10/16	Tue 10/18/16			8/28 9/4 9/11 9/18 9/25	10/2 10/9 10/16 10/23 10/31	11/6 11/13 11/20 11/27 12/4 12/11 12/18 12/25	1/1 1/8 1/15 1/22 1/29	
2	Define Scope of Work and Tasks	7 days	Mon 10/10/16	Tue 10/18/16				10/2 10/9 10/16 10/23 10/31			
3											
4	Survey	14 days	Wed 10/19/16	Mon 11/7/16				10/2 10/9 10/16 10/23 10/31			
5	Design Topography	14 days	Wed 10/19/16	Mon 11/7/16				10/2 10/9 10/16 10/23 10/31			
6											
7	Preliminary Plans (30% Submittal)	15 days	Tue 11/8/16	Mon 11/28/16				10/2 10/9 10/16 10/23 10/31			
8	Preliminary Plans and Specifications	15 days	Tue 11/8/16	Mon 11/28/16				10/2 10/9 10/16 10/23 10/31			
9											
10	60-90% Submittal of Plans and Specifications	20 days	Tue 11/29/16	Mon 12/26/16				10/2 10/9 10/16 10/23 10/31			
11	Plans and Specifications	20 days	Tue 11/29/16	Mon 12/26/16				10/2 10/9 10/16 10/23 10/31			
12											
13	100% Submittal	7 days	Tue 12/27/16	Wed 1/4/17				10/2 10/9 10/16 10/23 10/31			
14	Final Plans & Specifications	7 days	Tue 12/27/16	Wed 1/4/17				10/2 10/9 10/16 10/23 10/31			

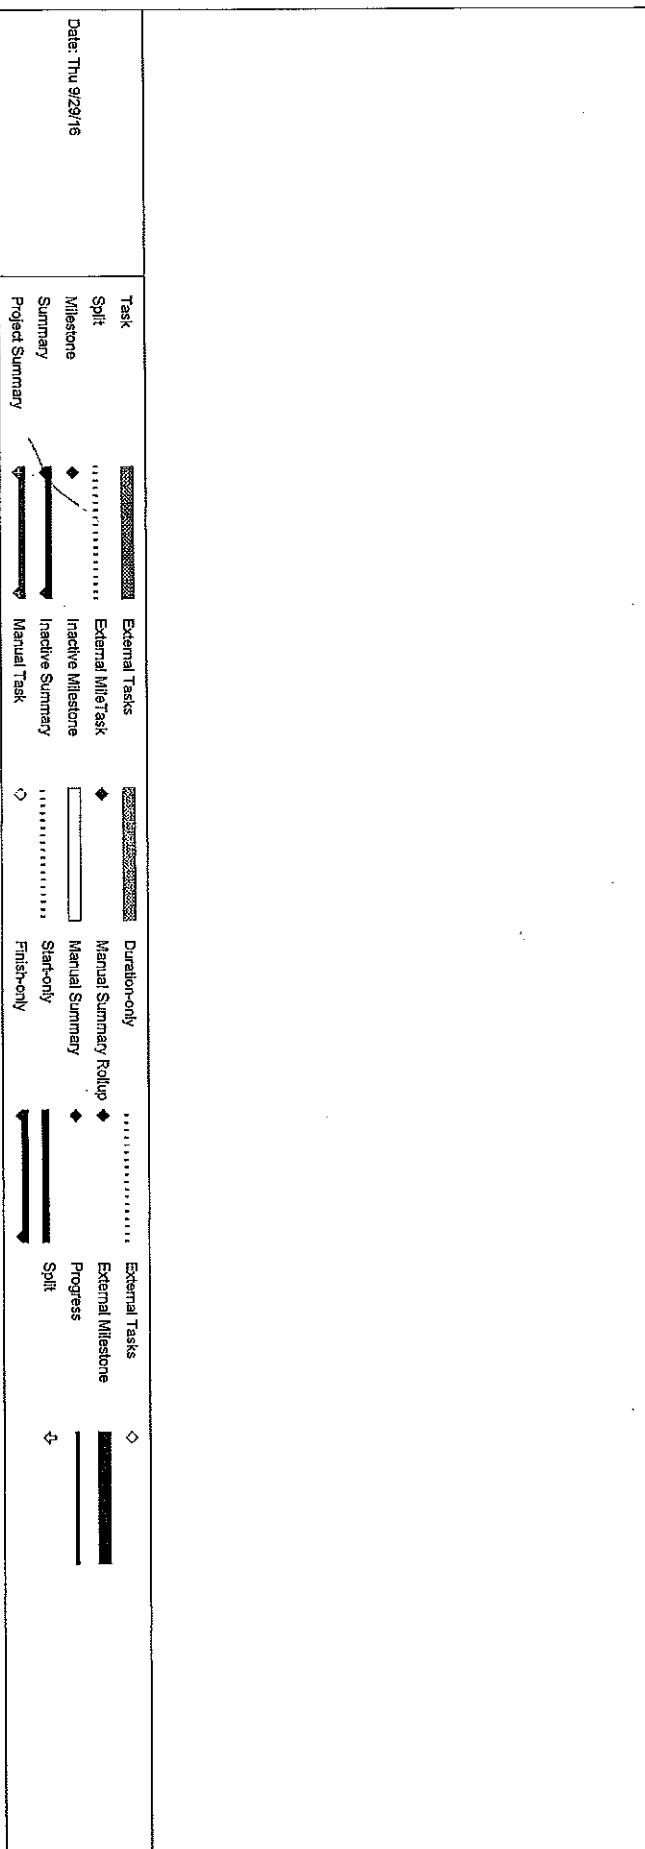


Date: Thu 9/29/16


Task
Split
Milestone
Summary
Project Summary



External Task
External Milestone
Inactive Milestone
Inactive Summary
Manual Task



Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only



External Task
External Milestone
Progress
Split



City of Peñitas - Sidewalk Improvement Project EOPCC



ITEM NO.	DESCRIPTION	EST. QNTY.	UNIT	UNIT PRICE	TOTAL PRICE
P.205 - City of Peñitas - Sidewalk Improvement Project					
General Project					
1-1	Mobilization, Bonds and insurance (not to exceed 3% of Total Bid) and project signage	LS	1	\$ 2,500.00	\$ 2,500.00
Total General Project				\$	2,500.00
City of Peñitas - Sidewalk Improvement Project					
2-1	Remove and Replace Concrete Sidewalk as per plans and specifications (Approx. 220 LF of Concrete Sidewalk meeting ADA requirements); complete in place	LS	1	\$ 22,000.00	\$ 22,000.00
City of Peñitas - Sidewalk Improvement Project				\$	22,000.00
Total General Project				\$	2,500.00
City of Peñitas - Sidewalk Improvement Project				\$	22,000.00
TOTAL BASE BID PRICE				\$	24,500.00

All other provisions are unchanged and remain in full force and effect.

IN WITNESS WHEREOF, the Engineer and the Owner have caused this Supplemental Agreement to the Agreement for Professional Services to be executed as of the _____ day of _____, 20__.

**THE ENGINEER:
LEFEVRE ENGINEERING & MANAGEMENT
CONSULTING, LLC.**

**THE OWNER:
HIDALGO COUNTY**

By: Richard Lefevre, P.E., President

By: Ramon Garcia, County Judge

ATTEST:

Arturo Guajardo Jr., County Clerk

LIST OF ATTACHMENTS

(as required)

EXHIBIT F
-Certificates of Insurance

CERTIFICATE OF INTERESTED PARTIES

FORM 1295

1 of 1

Complete Nos. 1 - 4 and 6 if there are interested parties.
 Complete Nos. 1, 2, 3, 5, and 6 if there are no interested parties.

OFFICE USE ONLY CERTIFICATION OF FILING

1 Name of business entity filing form, and the city, state and country of the business entity's place of business.
 LeFevre Engineering & Management Consulting, LLC
 McAllen, TX United States

Certificate Number:
 2016-117865

Date Filed:
 09/29/2016

2 Name of governmental entity or state agency that is a party to the contract for which the form is being filed.
 Hidalgo County Urban County Program


Date Acknowledged:

3 Provide the identification number used by the governmental entity or state agency to track or identify the contract, and provide a description of the services, goods, or other property to be provided under the contract.
 5016-60-0312-5000-6000
 Engineering Services

4	Name of Interested Party	City, State, Country (place of business)	Nature of interest (check applicable)	
			Controlling	Intermediary

5 Check only if there is NO Interested Party.

6 AFFIDAVIT I swear, or affirm, under penalty of perjury, that the above disclosure is true and correct.



[Handwritten Signature]
 Signature of authorized agent of contracting business entity

AFFIX NOTARY STAMP / SEAL ABOVE

Sworn to and subscribed before me, by the said Richard Lefevre, this the 29th day of September, 20 16, to certify which, witness my hand and seal of office.

[Handwritten Signature]
 Signature of officer administering oath

Eric Cantu
 Printed name of officer administering oath

Notary
 Title of officer/administering oath

CERTIFICATE OF INTERESTED PARTIES

FORM 1295

1 of 1

Complete Nos. 1 - 4 and 6 if there are interested parties.
Complete Nos. 1, 2, 3, 5, and 6 if there are no interested parties.

OFFICE USE ONLY CERTIFICATION OF FILING

1 Name of business entity filing form, and the city, state and country of the business entity's place of business.
LeFevre Engineering & Management Consulting, LLC
McAllen, TX United States

Certificate Number:
2016-117865

Date Filed:
09/29/2016

2 Name of governmental entity or state agency that is a party to the contract for which the form is being filed.
Hidalgo County Urban County Program

Date Acknowledged:
09/29/2016

3 Provide the identification number used by the governmental entity or state agency to track or identify the contract, and provide a description of the services, goods, or other property to be provided under the contract.
5016-60-0312-5000-6000
Engineering Services

4	Name of Interested Party	City, State, Country (place of business)	Nature of interest (check applicable)	
			Controlling	Intermediary

5 Check only if there is NO Interested Party.

6 AFFIDAVIT I swear, or affirm, under penalty of perjury, that the above disclosure is true and correct.

Signature of authorized agent of contracting business entity

AFFIX NOTARY STAMP / SEAL ABOVE

Sworn to and subscribed before me, by the said _____, this the _____ day of _____, 20_____, to certify which, witness my hand and seal of office.

Signature of officer administering oath Printed name of officer administering oath Title of officer administering oath
